
Date:	09/17/2022	Weather:		Coding:	PACP 7.0
Pipe Length (ft)	: 51.2	Owner:	City of Hobart	Pre Clean:	No Pre-Cleaning
P.O.#:	YES502259	Surveyor:	S. Bucklin	PSR:	M-705-045-M-705-045
Customer:	City of Hobart	Clean Date:		Shape:	С
Street:	East 4th Street		Flow Control:	Not Controlled	ł
City:	Hobart, IN		Year Renewed:		
Location:	Local rural streets v	with light traffic,	t Tape/Media #:		
Purpose:	Routine Assessmer	nt	Dia/Height:	8"	
Use:	Sanitary Sewage Pi	ре	Material:	СР	
Drain Area:			Lining:	None	
Category:	NA				
Comment:	No U/S access four	ıd.			
Location Detail	s:		Direction of Surve	y: Upstream	
US MH:	M-705-045	DS MH:	M-705-045	Total Length Surveyed (ft): 1.3
0&M Index:	3.00	O&M Quick:	5111	O&M Rating:	6.00
Structural Index:	0.00	Structural Qu	uick: 0000	Structural Rating	0.00
Overall Index:	3.00	Overall Quick	E 444		6.00





Code: Description:	AMH Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-705-045

Tuesday, April 25, 2023

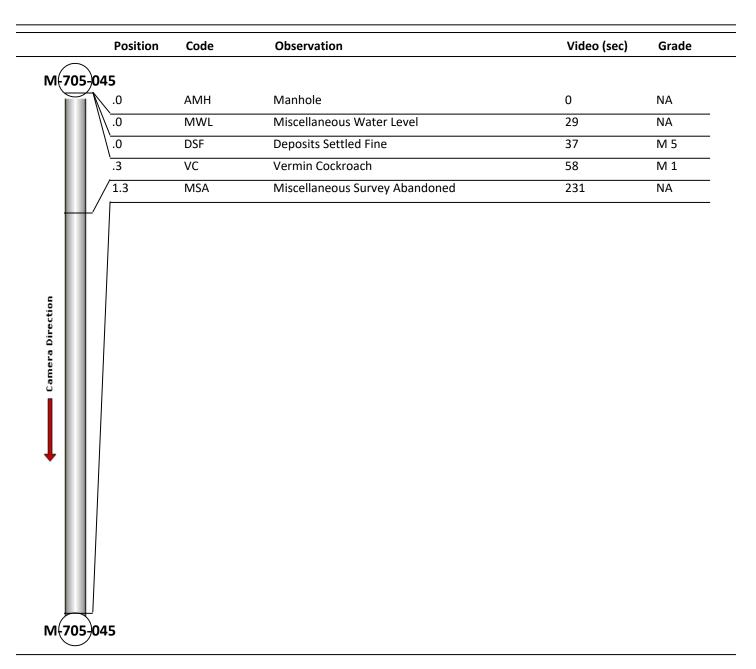

MWL
Miscellaneous Water Level
.0
0
0
65.000
NO



Code: Description:	DSF Deposits Settled Fine
Distance (ft): Structural Grade: O&M Grade: Clock Start/From: Clock To: 1st Value: 2nd Value: Value Percent:	.0 0 5 2 10 65.000
Continuous Index: Within 8" of Joint: Remarks:	YES



Code: Description:	VC Vermin Cockroach
Distance (ft):	.3
Structural Grade:	0
O&M Grade:	1
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	YES
Remarks:	



Distance (ft):1.3Structural Grade:0O&M Grade:0Clock Start/From:Clock To:1st Value:	PAST
