
| Date:             | 03/22/2018  | Weather:      |                 |                   | Coding:            | PACP 6.0      |
|-------------------|-------------|---------------|-----------------|-------------------|--------------------|---------------|
| Pipe Length (ft): |             | Owner:        | NA              |                   | Pre Clean:         | Not Known     |
| P.O.#:            |             | Surveyor:     | Selasie Honu    |                   | PSR:               | P-803-065-050 |
| Customer:         |             | Clean Date:   | 01/01/1900      |                   | Shape:             | С             |
| Street:           | N HOBART RD | Flow Control: |                 |                   | Not Controlled     |               |
| City:             | Hobart, IN  |               | Year Renewed:   |                   |                    |               |
| Location:         | Other       |               | Tape/Media #:   |                   |                    |               |
| Purpose:          | Not Known   |               | Dia/Height:     |                   | 10"                |               |
| Use:              | Sanitary    |               | Material:       |                   | VCP                |               |
| Drain Area:       | NA          |               | Lining:         |                   |                    |               |
| Category:         | NA          |               |                 |                   |                    |               |
| Comment:          |             |               |                 |                   |                    |               |
| Location Details: | :           |               | Direction of Su | rvey:             | Upstream           |               |
| US MH:            | M-803-065   | DS MH:        | M-903-050       | Total Leng        | gth Surveyed (ft): | 53.5          |
| D&M Index:        | 2.09        | O&M Quick:    | 31              | <mark>2A</mark> O | &M Rating:         | 23.00         |
| Structural Index: | 0.00        | Structural Qu | uick: 00        |                   | ructural Rating:   | 0.00          |
| Overall Index:    | 2.09        | Overall Quick |                 | ~ ~               | verall Rating:     | 23.00         |





| Code:<br>Description: | DAGS<br>Deposits Attached Grease |
|-----------------------|----------------------------------|
| Distance (ft):        | .0                               |
| Structural Grade:     | 0                                |
| O&M Grade:            | 2                                |
| Clock Start/From:     | 7                                |
| Clock To:             | 5                                |
| 1st Value:            |                                  |
| 2nd Value:            |                                  |
| Value Percent:        | 10.000                           |
| Continuous Index:     | S01                              |
| Within 8" of Joint:   | NO                               |
| Remarks:              |                                  |

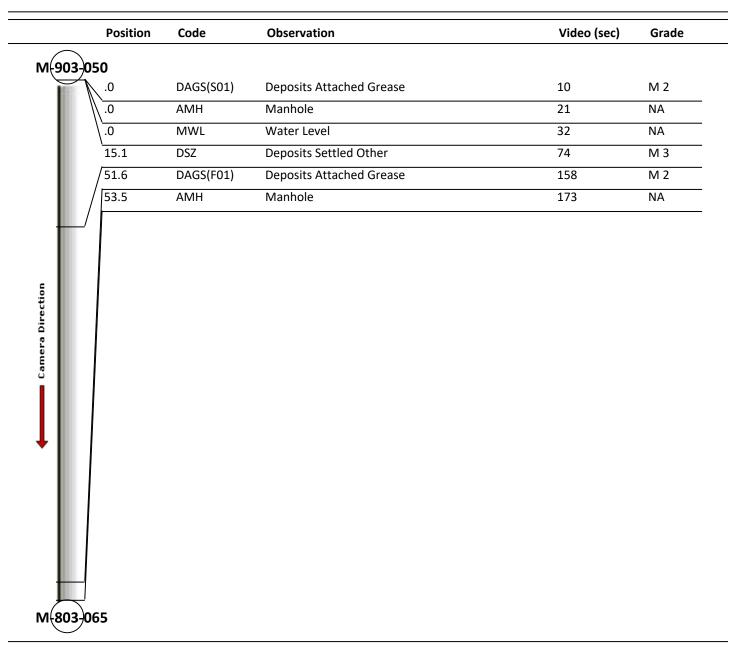

Code: AMH Description: Manhole

| Distance (ft):      | .0        |
|---------------------|-----------|
| Structural Grade:   | 0         |
| O&M Grade:          | 0         |
| Clock Start/From:   |           |
| Clock To:           |           |
| 1st Value:          |           |
| 2nd Value:          |           |
| Value Percent:      |           |
| Continuous Index:   |           |
| Within 8" of Joint: | NO        |
| Remarks:            | M-903-050 |





| DSZ                           |
|-------------------------------|
| <b>Deposits Settled Other</b> |
|                               |
|                               |
| 15.1                          |
| 0                             |
| 3                             |
| 4                             |
| 8                             |
|                               |
|                               |
| 20.000                        |
|                               |
| NO                            |
|                               |

Remarks:

Code:

Description:

MISC

DAGS

**Deposits Attached Grease** 



| Distance (ft):      | 51.6   |
|---------------------|--------|
| Structural Grade:   | 0      |
| O&M Grade:          | 2      |
| Clock Start/From:   | 7      |
| Clock To:           | 5      |
| 1st Value:          |        |
| 2nd Value:          |        |
| Value Percent:      | 10.000 |
| Continuous Index:   | F01    |
| Within 8" of Joint: | NO     |
| Remarks:            |        |



Code:AMHDescription:Manhole

| Distance (ft):      | 53.5      |
|---------------------|-----------|
| Structural Grade:   | 0         |
| O&M Grade:          | 0         |
| Clock Start/From:   |           |
| Clock To:           |           |
| 1st Value:          |           |
| 2nd Value:          |           |
| Value Percent:      |           |
| Continuous Index:   |           |
| Within 8" of Joint: | NO        |
| Remarks:            | M-803-065 |
|                     |           |
