


Manhole Inspection Report



Date:	09/28/2022	Weather:		Coding:	RZMACP
MH#:	M-606-058	Owner:	NA	Len. Surveyed:	17.6
P.O.#:		Surveyor:	Jen Costello	Rim to Invert:	19.4
Customer:		Cert. #:	U-907-5518	Wall Material:	Concrete (cast in place)

Street:	8th St. 168' East of Wisconsin St.	Project:	Hobart, IN
City:	Hobart, IN	GPS Northing:	2286498.222
Location:	Yard	GPS Easting:	2902034.898
Drain Area:	Southwest	GPS Accuracy:	Sub-Meter
Cover Shape:	Circular	Evidence of Surcharge:	No
Cover Size:	24.0	Potential for Runoff:	None
Comments:			


O&M Index:	2.00	O&M Quick:	2100	O&M Rating:	2.00
Structural Index:	1.16	Structural Quick:	411B	Structural Rating:	22.00
Overall Index:	1.20	Overall Quick:	4121	Overall Rating:	24.00

	Position	Code	Observation	Video (sec)	Grade
	M-606-058				
	.0	MGO	General Observation	10	NA
	.0	SRI	Surface Roughness Increased	21	S 1
	2.5	FM	Fracture Multiple	40	S 4
	2.5	MGO	General Observation	51	NA
	8.9	RPP	Repair Patch	78	NA
	17.6	DSGV	Deposits Settled Gravel	107	M 2
	17.6	SRI	Surface Roughness Increased	118	S 1
	17.6	MGO	General Observation	129	NA




Code: **MGO**
Description: **General Observation**


Distance (ft): **.0**
Structural Grade: **0**
O&M Grade: **0**
Clock Start/From:
Clock To:
1st Value:
2nd Value:
Value Percent:
Step: **NO**
Remarks: **access mh**

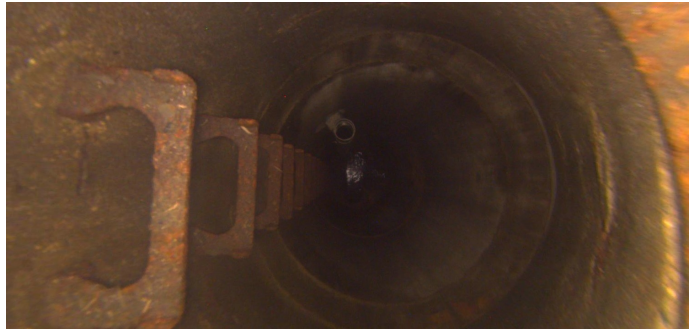


Code:	SRI
Description:	Surface Roughness Increased
Distance (ft):	.0
Structural Grade:	1
O&M Grade:	0
Clock Start/From:	12
Clock To:	12
1st Value:	
2nd Value:	
Value Percent:	
Step:	NO
Remarks:	

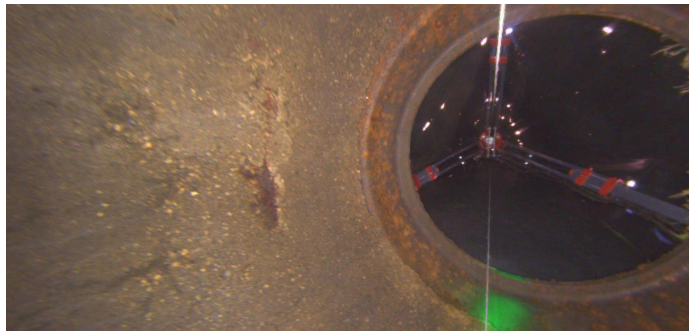

Code:	FM
Description:	Fracture Multiple
Distance (ft):	2.5
Structural Grade:	4
O&M Grade:	0
Clock Start/From:	2
Clock To:	3
1st Value:	
2nd Value:	
Value Percent:	
Step:	NO
Remarks:	

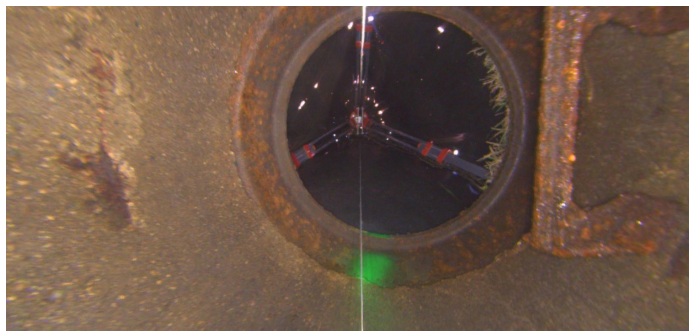

Code:	MGO
Description:	General Observation
Distance (ft):	2.5
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Step:	NO
Remarks:	underside of frame

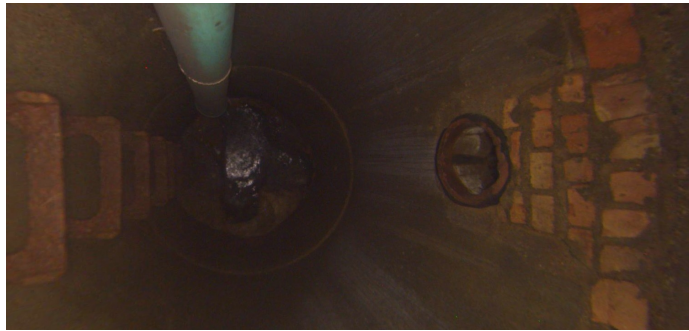


Code: **RPP**
Description: **Repair Patch**

Distance (ft): **8.9**
Structural Grade: **0**
O&M Grade: **0**
Clock Start/From: **2**
Clock To: **3**
1st Value:
2nd Value:
Value Percent:
Step: **NO**
Remarks: **brick**




Code: **DSGV**
Description: **Deposits Settled Gravel**

Distance (ft): **17.6**
Structural Grade: **0**
O&M Grade: **2**
Clock Start/From: **12**
Clock To: **12**
1st Value:
2nd Value:
Value Percent: **5.000**
Step: **NO**
Remarks:

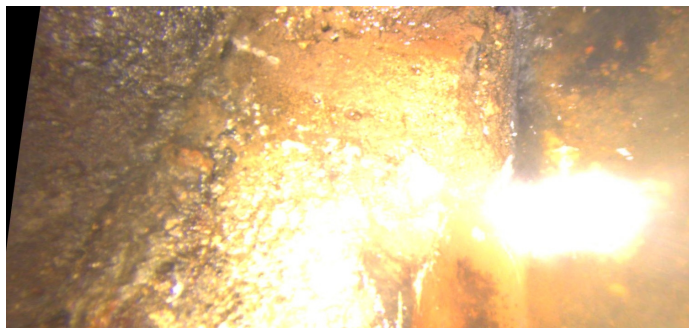

Code: **SRI**
Description: **Surface Roughness Increased**

Distance (ft): **17.6**
Structural Grade: **1**
O&M Grade: **0**
Clock Start/From: **12**
Clock To: **12**
1st Value:
2nd Value:
Value Percent:
Step: **NO**
Remarks:

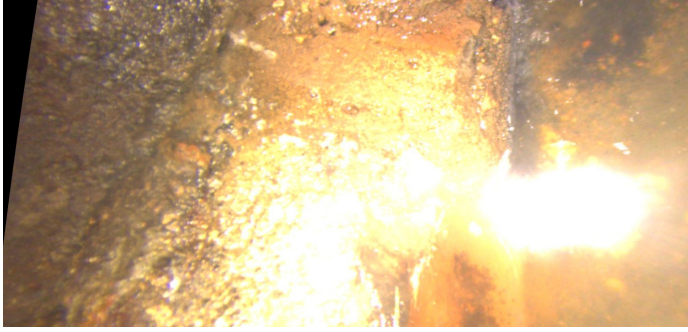

Code:	MGO
Description:	General Observation
Distance (ft):	17.6
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Step:	NO
Remarks:	end of survey
