

Manhole Inspection Report



Date:	04/27/2018	Weather:		Coding:	RZMACP
MH#:	M-706-010.1	Owner:	NA	Len. Surveyed:	8.2
P.O.#:		Surveyor:	Jen Costello	Rim to Invert:	8.2
Customer:		Cert. #:	U-907-5518	Wall Material:	Concrete (reinforced)

Street:	State St. 223' South of 8th St.	Project:	Hobart, IN
City:	Hobart, IN	GPS Northing:	41.52482224
Location:		GPS Easting:	-87.25336456
Drain Area:	Southeast	GPS Accuracy:	Nearest Meter
Cover Shape:	Circular	Evidence of Surcharge:	No
Cover Size:	22.5	Potential for Runoff:	None
Comments:			


O&M Index:	<u>0.00</u>	O&M Quick:	0000	O&M Rating:	<u>0.00</u>
Structural Index:	<u>4.00</u>	Structural Quick:	4100	Structural Rating:	<u>4.00</u>
Overall Index:	<u>4.00</u>	Overall Quick:	4100	Overall Rating:	<u>4.00</u>

Position	Code	Observation	Video (sec)	Grade
M-706-010.1				
.0	MGO	General Observation	10	NA
1.8	MGP	General Photo	27	NA
3.8	FM	Fracture Multiple	44	S 4
8.2	MGO	General Observation	65	NA



Code: **MGO**
Description: **General Observation**

Distance (ft): **.0**
Structural Grade: **0**
O&M Grade: **0**
Clock Start/From:
Clock To:
1st Value:
2nd Value:
Value Percent:
Step: **NO**
Remarks: **ACCESS MH**

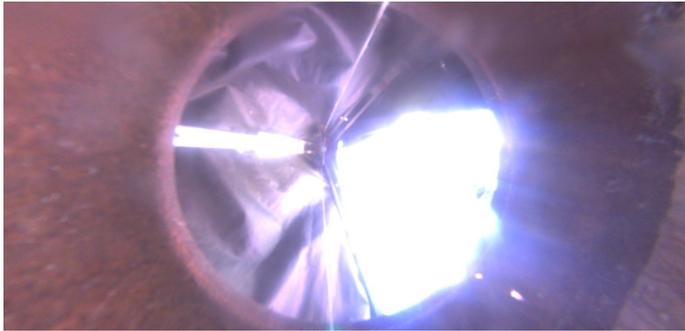

Code: **MGP**
Description: **General Photo**

Distance (ft): **1.8**
Structural Grade: **0**
O&M Grade: **0**
Clock Start/From:
Clock To:
1st Value:
2nd Value:
Value Percent:
Step: **NO**
Remarks: **UNDERSIDE OF FRAME**



Code: **FM**
Description: **Fracture Multiple**

Distance (ft): **3.8**
Structural Grade: **4**
O&M Grade: **0**
Clock Start/From: **9**
Clock To: **3**
1st Value:
2nd Value:
Value Percent:
Step: **NO**
Remarks:



Code: **MGO**
Description: **General Observation**

Distance (ft): **8.2**
Structural Grade: **0**
O&M Grade: **0**
Clock Start/From:
Clock To:
1st Value:
2nd Value:
Value Percent:
Step: **NO**
Remarks: **END SURVEY**
