Profile/Pho	oto Observation I	Report			RedZo
Date:	04/19/2018	Weather:		Coding:	PACP 4.2
Pipe Length (ft):	381.2	Owner:	City of Hobart	Pre Clean:	No Pre-Cleaning
P.O.#:	2004	Surveyor:	SAN	PSR:	P-1004-040-039
Customer:	Red Zone	Clean Date:		Shape:	С
Street:	Coral Dr		Flow Control:	Not Controlled	
City:	Hobart In		Year Renewed:		
Location:	Light Highway		Tape/Media #:	Deliverable 1	
Purpose:	Routine Assessment		Dia/Height:	15"	
Use:	Sanitary		Material:	PVC	
Drain Area:	Northeast		Lining:		
Category:	NA				
Comment:	418-3				
Location Details	: Center of street		Direction of Surve	ey: Downstream	
US MH:	M-1004-040	DS MH:	M-1004-039	Total Length Surveyed (ft)	: 381.2
D&M Index:	2.67	O&M Quick:	4122	O&M Rating:	8.00
Structural Index:	0.00	 Structural Qu	uick: 0000		0.00
Overall Index:	2.67	Overall Quicl	44.22		8.00

	Position	Code	Observation	Video (sec)	Grade
M-1004	- 040				
\square	0.	AMH	Manhole	32	NA
- 11	.0	MWL	Water Level	61	NA
- 11	0.	MGO	General Observation	99	NA
	\\5.4	TF	Tap Factory	171	NA
	\\50.8	TF	Tap Factory	279	NA
	61.0	TF	Tap Factory	351	NA
	94.3	TF	Tap Factory	437	NA
	137.9	TFD	Tap Factory Defective	614	M 2
	137.9	IR	Infil Runner	659	M 4
s 🗖	-\\137.9	DAE	Deposits Attached Encrustation	764	M 2
Camera Direction	150.4	TF	Tap Factory	821	NA
Dir	278.4	TF	Tap Factory	1081	NA
nera	288.4	TF	Tap Factory	1133	NA
Car	300.2	TF	Tap Factory	1215	NA
	320.5	TF	Tap Factory	1319	NA
	374.6	TF	Tap Factory	1450	NA
- I	381.2	AMH	Manhole	1522	NA
	J				
]				
]				



Code: Description:	AMH Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-1004-040

Thursday, May 4, 2023

м-(1004)-039



Code:	MWL
Description:	Water Level
Distance (ft):	0
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	5.000
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	




Code:	MGO
Description:	General Observation
Distance (ft):	.0
Structural Grade:	0
O&M Grade: Clock Start/From: Clock To:	0
1st Value: 2nd Value:	
Value Percent: Continuous Index:	
Within 8" of Joint:	NO
Remarks:	roots in manhole



Code: Description:	TF Tap Factory
·	. ,
Distance (ft):	5.4
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	11
Clock To:	
1st Value:	4.000
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	



Code: Description:	TF Tap Factory
Distance (ft): Structural Grade: O&M Grade: Clock Start/From: Clock To: 1st Value: 2nd Value:	50.8 0 0 1 4.000
Value Percent: Continuous Index: Within 8" of Joint: Remarks:	NO

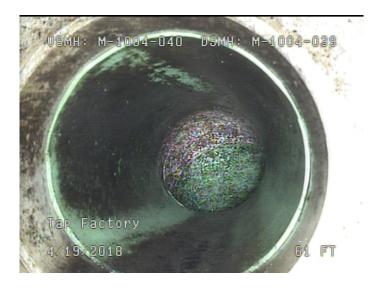

Code:	TF
Description:	Tap Factory
Distance (ft):	61.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	1
Clock To:	
1st Value:	4.000
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	



Code: Description:	TF Tap Factory
Distance (ft):	94.3
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	11
Clock To:	
1st Value:	4.000
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	



TFD
Tap Factory Defective
137.9
0
2
1
4.000
NO
infil in tap




Code: Description:	IR Infil Runner
Distance (ft): Structural Grade: O&M Grade: Clock Start/From: Clock To: 1st Value: 2nd Value: Value Percent: Continuous Index: Within 8" of Joint:	137.9 0 4 1
Remarks:	



Code: Description:	DAE Deposits Attached Encrustation
Distance (ft):	137.9
Structural Grade:	0
O&M Grade:	2
Clock Start/From:	2
Clock To:	5
1st Value:	
2nd Value:	
Value Percent:	10.000
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	in tap



Code: Description:	TF Tap Factory
Distance (ft):	150.4
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	11
Clock To:	
1st Value:	4.000
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	

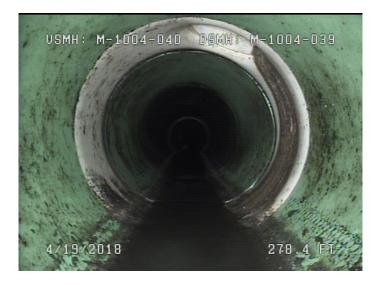

Code: Description:	TF Tap Factory
Distance (ft):	278.4
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	1
Clock To:	
1st Value:	4.000
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	



Code: Description:	TF Tap Factory
Distance (ft): Structural Grade: O&M Grade: Clock Start/From: Clock To: 1st Value: 2nd Value: Value Percent: Continuous Index:	288.4 0 0 11 4.000
Within 8" of Joint: Remarks:	NO



Code: Description:	TF Tap Factory
Distance (ft):	300.2
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	2
Clock To:	
1st Value:	4.000
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	



Code: Description:	TF Tap Factory
Distance (ft):	320.5
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	11
Clock To:	
1st Value:	4.000
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	



p Factory
4.6
000
)



Code: Description:	AMH Manhole
Distance (ft):	381.2
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-1004-039
