
Date:	04/11/2018	Weather:		Coding:	PACP 6.0
Pipe Length (ft):	137.6	Owner:	NA	Pre Clean:	Not Known
P.O.#:		Surveyor:	Jen Costello	PSR:	P-1004-063-037
Customer:		Clean Date:	01/01/1900	Shape:	С
Street:	Hillcrest Ave.		Flow Control:	Not Controlled	
City:	Hobart, IN		Year Renewed:		
Location:	Other		Tape/Media #:		
Purpose:	Not Known		Dia/Height:	10"	
Use:	Sanitary		Material:	PVC	
Drain Area:	NA		Lining:		
Category:	NA				
Comment:					
Location Details	:		Direction of Survey	Downstream	
US MH:	M-1004-063	DS MH:	M-1004-037	Total Length Surveyed (ft)	: 132.9
0&M Index:	0.00	O&M Quick:	0000	O&M Rating:	0.00
Structural Index:	0.00	Structural Qu	uick: 0000	Structural Rating:	0.00
Overall Index:	0.00	Overall Quicl		Overall Rating:	0.00





Code:	АМН	
Description:	Manhole	
Distance (ft):	.0	
Structural Grade:	0	
O&M Grade:	0	
Clock Start/From:		
Clock To:		
1st Value:		
2nd Value:		
Value Percent:		
Continuous Index:		
Within 8" of Joint:	NO	
Remarks:	M-1004-063	

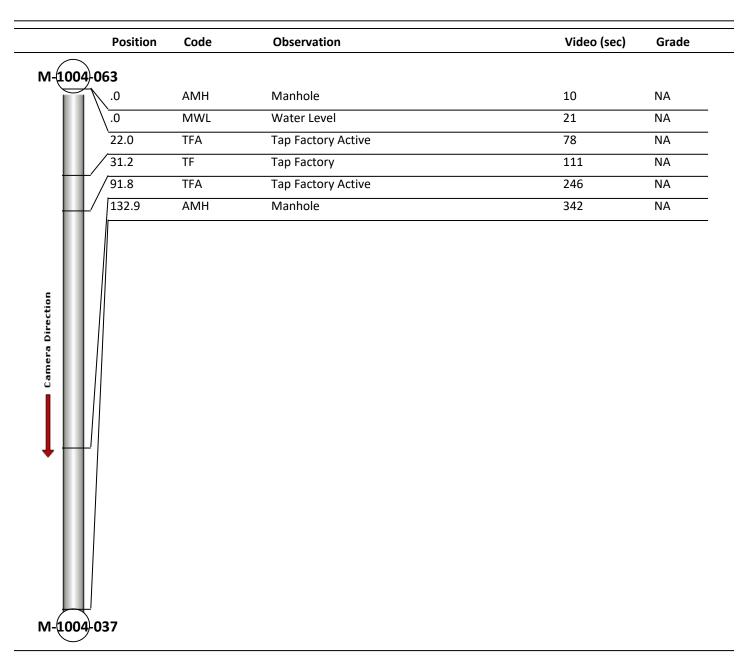

Code: MWL Description: Water Level

.0
0
0
5.000
NO



Code: Description:	TFA Tap Factory Active
Distance (ft):	22.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	9
Clock To:	
1st Value:	4.000
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	
Remarks:	



Code:	TF
Description:	Tap Factory
Distance (ft):	31.2
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	3
Clock To:	
1st Value:	4.000
2nd Value:	

2nd Value: Value Percent: Continuous Index: Within 8" of Joint: Remarks:

Within 8" of Joint:

Remarks:



Code:	TFA	
Description:	Tap Factory Active	
Distance (ft):	91.8	
Structural Grade:	0	
O&M Grade:	0	
Clock Start/From:	9	
Clock To:		
1st Value:	4.000	
2nd Value:		
Value Percent:		
Continuous Index:		



Code: AMH Description: Manhole

Distance (ft):	132.9
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-1004-037
