


Date:	04/11/2018	Weather:		Coding:	PACP 6.0
Pipe Length (ft):	123.3	Owner:	NA	Pre Clean:	Not Known
P.O.#:		Surveyor:	Jen Costello	PSR:	P-1004-074-073
Customer:		Clean Date:	01/01/1900	Shape:	С
Street:	TULIP LN		Flow Control:	Not Controlled	
City:	Hobart, IN		Year Renewed:		
Location:	Other		Tape/Media #:		
Purpose:	Not Known		Dia/Height:	8"	
Use:	Sanitary		Material:	PVC	
Drain Area:	NA		Lining:		
Category:	NA				
Comment:					
Location Details	:		Direction of Survey	/: Downstream	
US MH:	M-1004-073	DS MH:	M-1004-074	Total Length Surveyed (ft)	: 120.1
0&M Index:	0.00	O&M Quick:	0000	O&M Rating:	0.00
itructural Index:	0.00	Structural Qu	uick: 0000	Structural Rating:	0.00
Overall Index:	0.00	Overall Quick		Overall Rating:	0.00

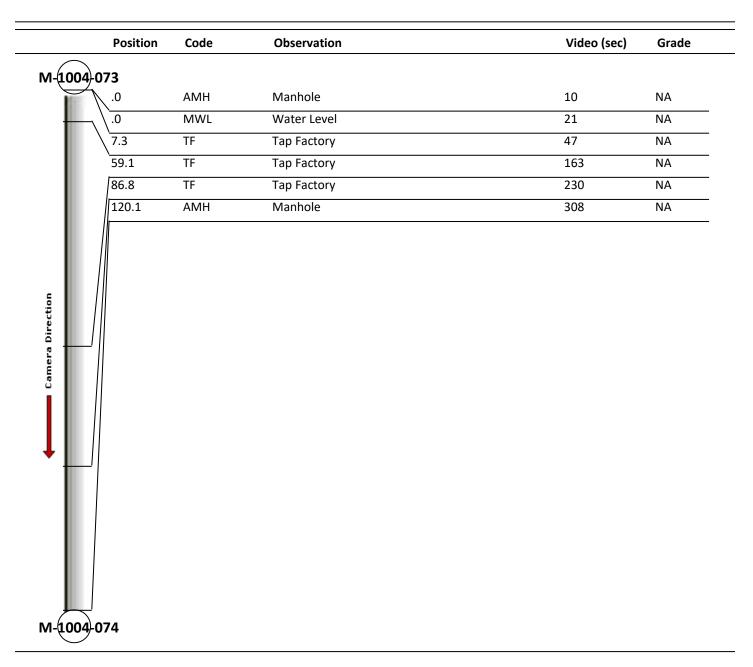




Code: Description:	AMH Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-1004-073



Code: MWL Description: Water Level

Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	5.000
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	




Code: Description:	TF Tap Factory
Distance (ft):	7.3
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	9
Clock To:	
1st Value:	4.000
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	
Remarks:	



Code:	TF
Description:	Tap Factory
Distance (ft):	59.1
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	9
Clock To:	
1st Value:	4.000
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	

Remarks:



TF Tap Factory
86.8
0
0
3
4.000



Code:	AMH
Description:	Manhole
Distance (ft):	120.1
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	

NO

M-1004-074

Within 8" of Joint:

Remarks:

Thursday, November 16, 2023
