

Date:	01/31/2023	Weather:		Coding:	PACP 7.0
Pipe Length (ft):	48.0	Owner:	City of Hobart	Pre Clean:	Heavy Cleaning
P.O.#:	YES502259	Surveyor:	S. Bucklin	PSR:	M-805-037.1-M-805-03
Customer:	City of Hobart	Clean Date:	11/30/2022	Shape:	С
Street:	South Liberty Place	2	Flow Control:	Not Controlled	1
City:	Hobart, IN		Year Renewed:		
Location:	Local rural streets	with light traffic	, t Tape/Media #:		
Purpose:	Routine Assessmer	nt	Dia/Height:	12"	
Use:	Sanitary Sewage Pi	ре	Material:	DIP	
Drain Area:			Lining:	None	
Category:	NA				
Comment:					
Location Details	:		Direction of Surve	ey: Upstream	
US MH:	M-805-037.1	DS MH:	M-805-037	Total Length Surveyed (ft): 46.9
0&M Index:	2.00	O&M Quick:	2200	O&M Rating:	4.00
tructural Index:	2.00	Structural Qu	uick: 2900	Structural Rating	18.00
Overall Index:	2.00	Overall Quic			22.00



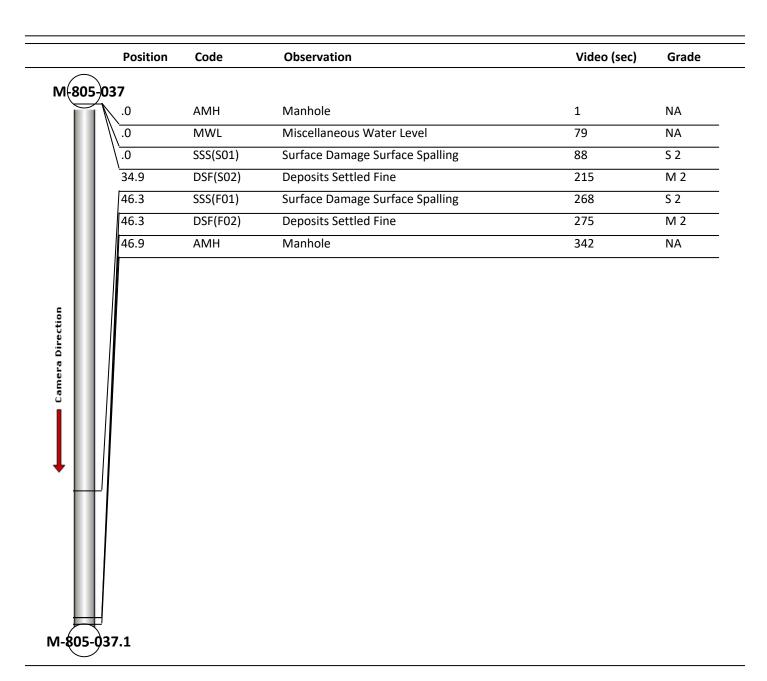

Code:	АМН
Description:	Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-805-037

Tuesday, April 25, 2023

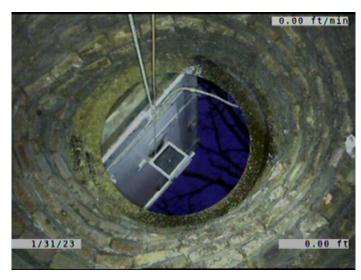

Code: Description:	MWL Miscellaneous Water Level
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	5.000
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	



Code: Description:	SSS Surface Damage Surface Spalling
Distance (ft): Structural Grade: O&M Grade: Clock Start/From: Clock To: 1st Value: 2nd Value: Value Percent: Continuous Index:	.0 2 0 7 5
Within 8" of Joint: Remarks:	YES



Code:	DSF
Description:	Deposits Settled Fine
Distance (ft):	34.9
Distance (ft):	54.9
Structural Grade:	0
O&M Grade:	2
Clock Start/From:	5
Clock To:	7
1st Value:	
2nd Value:	
Value Percent:	5.000
Continuous Index:	S02
Within 8" of Joint:	YES
Remarks:	



Distance (ft):46.3Structural Grade:2O&M Grade:0Clock Start/From:7Clock To:51st Value:-2nd Value:-Value Percent:F01Within 8" of Joint:YESRemarks:-	Code: Description:	SSS Surface Damage Surface Spalling
	Structural Grade: O&M Grade: Clock Start/From: Clock To: 1st Value: 2nd Value: Value Percent: Continuous Index: Within 8" of Joint:	2 0 7 5 F01



Code:	DSF
Description:	Deposits Settled Fine
Distance (ft):	46.3
Structural Grade:	0
O&M Grade:	2
Clock Start/From:	5
Clock To:	7
1st Value:	
2nd Value:	
Value Percent:	5.000
Continuous Index:	F02
Within 8" of Joint:	YES
Remarks:	



Code: Description:	AMH Manhole
Distance (ft):	46.9
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-805-037.1
