


Profile/Photo Observation Report




Date:	11/03/2021	Weather:		Coding:	PACP 7.0
Pipe Length (ft):	27.7	Owner:	City of Hobart	Pre Clean:	No Pre-Cleaning
P.O.#:	YES502259	Surveyor:	S. Bucklin	PSR:	
Customer:	City of Hobart	Clean Date:		Shape:	C

Street:	West Cleveland Avenue	Flow Control:	Not Controlled
City:	Hobart, IN	Year Renewed:	
Location:	Local rural streets with light traffic, t	Tape/Media #:	
Purpose:	Routine Assessment	Dia/Height:	15"
Use:	Sanitary Sewage Pipe	Material:	VCP
Drain Area:		Lining:	None
Category:	NA		
Comment:			
Location Details:		Direction of Survey:	Upstream
US MH:	UNK WABASH ST	DS MH:	M-404-002.1
		Total Length Surveyed (ft):	27.7

O&M Index:	2.16	O&M Quick:	4431	O&M Rating:	41.00
Structural Index:	0.00	Structural Quick:	0000	Structural Rating:	0.00
Overall Index:	2.16	Overall Quick:	4431	Overall Rating:	41.00

	Position	Code	Observation	Video (sec)	Grade
	.0	AMH	Manhole	1	NA
	.0	MWL	Miscellaneous Water Level	41	NA
	1.2	DSF(S01)	Deposits Settled Fine	87	M 2
	1.7	DAE	Deposits Attached Encrustation	135	M 2
	1.7	IDJ	Infiltration Dripper Joint	146	M 3
	4.3	RFJ	Roots Fine Joint	216	M 1
	4.3	IRJ	Infiltration Runner Joint	229	M 4
	7.5	RFJ	Roots Fine Joint	305	M 1
	7.5	IRJ	Infiltration Runner Joint	320	M 4
	7.5	DAE	Deposits Attached Encrustation	336	M 2
	10.4	IRJ	Infiltration Runner Joint	432	M 4
	10.4	RFJ	Roots Fine Joint	475	M 1
	10.4	DAE	Deposits Attached Encrustation	490	M 2
	10.4	RFJ	Roots Fine Joint	515	M 1
	13.4	RFJ	Roots Fine Joint	584	M 1
	16.1	MMC	Miscellaneous Material Change	699	NA
	16.1	RFJ	Roots Fine Joint	729	M 1
	21.7	MGO	Miscellaneous General Observation	800	NA
	26.8	RBL	Roots Ball Lateral	868	M 4
	27.7	DSF(F01)	Deposits Settled Fine	979	M 2
	27.7	AMH	Manhole	1042	NA

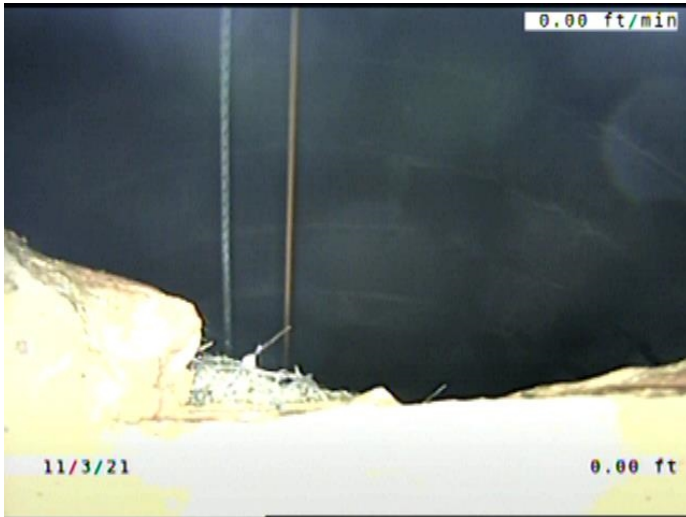

Code: **AMH**
 Description: **Manhole**

Distance (ft): **.0**
 Structural Grade: **0**
 O&M Grade: **0**
 Clock Start/From:
 Clock To:
 1st Value:
 2nd Value:
 Value Percent:
 Continuous Index:
 Within 8" of Joint: **NO**
 Remarks: **M-404-002.1**




Code: **MWL**
 Description: **Miscellaneous Water Level**

Distance (ft): **.0**
 Structural Grade: **0**
 O&M Grade: **0**
 Clock Start/From:
 Clock To:
 1st Value:
 2nd Value:
 Value Percent: **5.000**
 Continuous Index:
 Within 8" of Joint: **NO**
 Remarks:




Code: **DSF**
 Description: **Deposits Settled Fine**

Distance (ft): **1.2**
 Structural Grade: **0**
 O&M Grade: **2**
 Clock Start/From: **5**
 Clock To: **7**
 1st Value:
 2nd Value:
 Value Percent: **5.000**
 Continuous Index: **S01**
 Within 8" of Joint: **YES**
 Remarks:

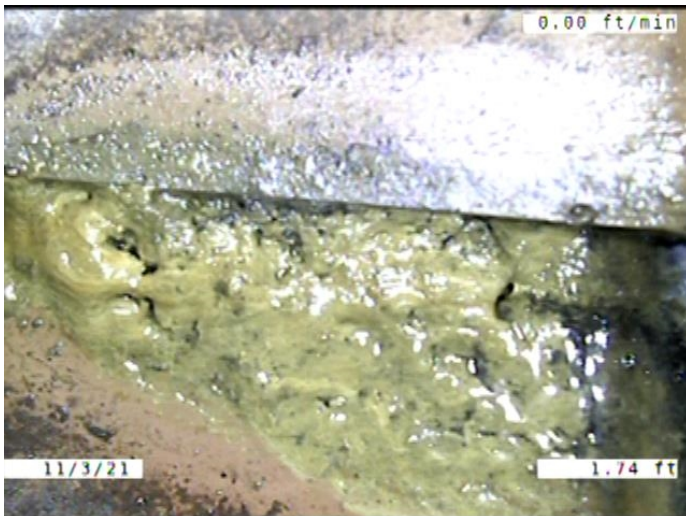


Code: **DAE**
 Description: **Deposits Attached Encrustation**

Distance (ft): **1.7**
 Structural Grade: **0**
 O&M Grade: **2**
 Clock Start/From: **3**
 Clock To: **4**
 1st Value:
 2nd Value:
 Value Percent: **5.000**
 Continuous Index:
 Within 8" of Joint: **YES**
 Remarks:

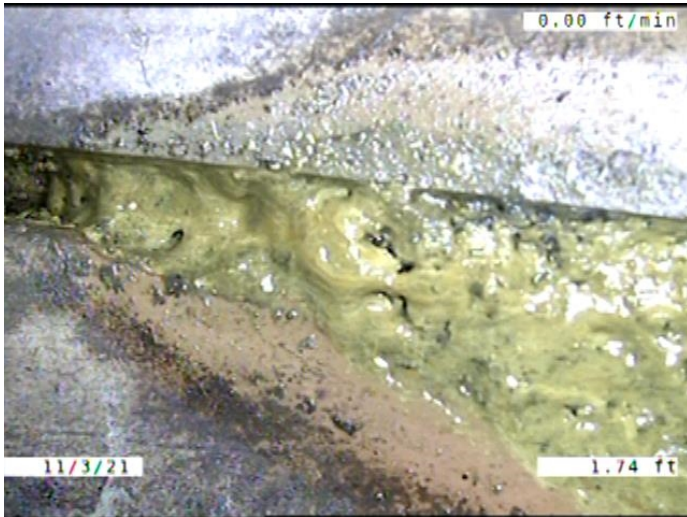


Code: **IDJ**
 Description: **Infiltration Dripper Joint**

Distance (ft): **1.7**
 Structural Grade: **0**
 O&M Grade: **3**
 Clock Start/From: **3**
 Clock To:
 1st Value:
 2nd Value:
 Value Percent:
 Continuous Index:
 Within 8" of Joint: **YES**
 Remarks:

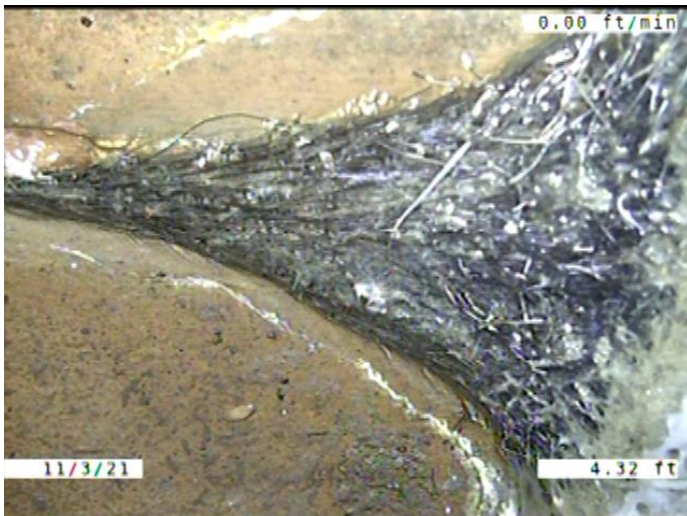


Code: **RFJ**
 Description: **Roots Fine Joint**

Distance (ft): **4.3**
 Structural Grade: **0**
 O&M Grade: **1**
 Clock Start/From: **9**
 Clock To: **4**
 1st Value:
 2nd Value:
 Value Percent:
 Continuous Index:
 Within 8" of Joint: **YES**
 Remarks:

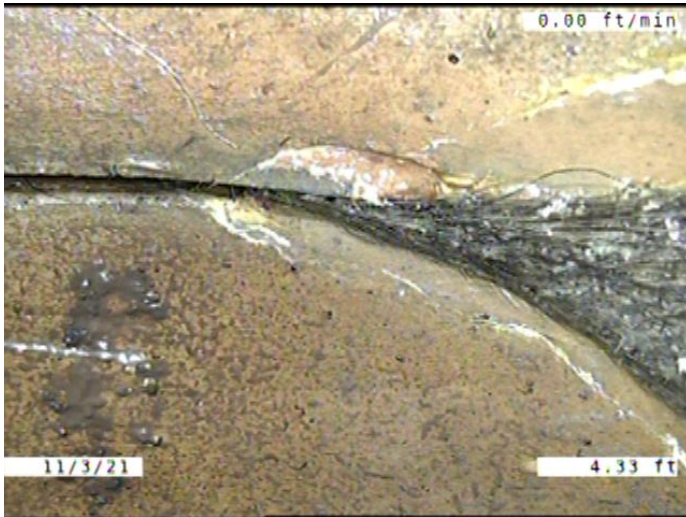


Code: **IRJ**
 Description: **Infiltration Runner Joint**

Distance (ft): **4.3**
 Structural Grade: **0**
 O&M Grade: **4**
 Clock Start/From: **3**
 Clock To:
 1st Value:
 2nd Value:
 Value Percent:
 Continuous Index:
 Within 8" of Joint: **YES**
 Remarks:

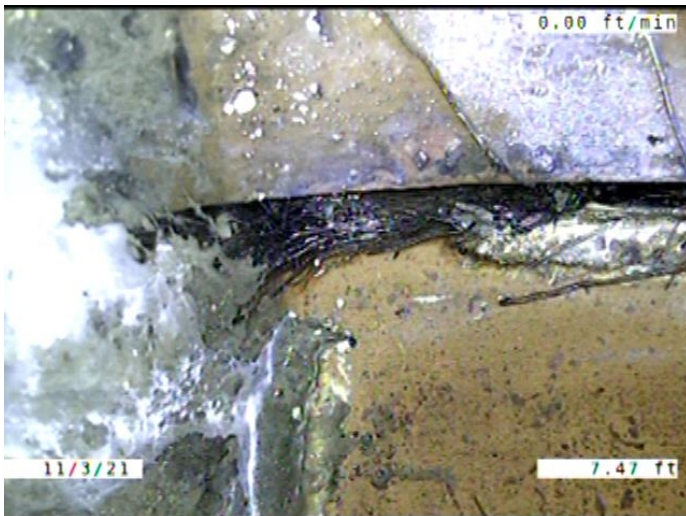


Code: **RFJ**
 Description: **Roots Fine Joint**

Distance (ft): **7.5**
 Structural Grade: **0**
 O&M Grade: **1**
 Clock Start/From: **8**
 Clock To: **4**
 1st Value:
 2nd Value:
 Value Percent:
 Continuous Index:
 Within 8" of Joint: **YES**
 Remarks:

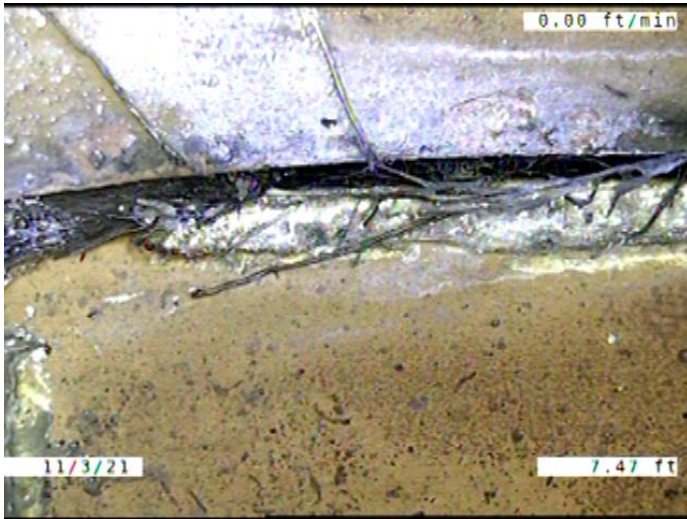


Code: **IRJ**
 Description: **Infiltration Runner Joint**

Distance (ft): **7.5**
 Structural Grade: **0**
 O&M Grade: **4**
 Clock Start/From: **9**
 Clock To:
 1st Value:
 2nd Value:
 Value Percent:
 Continuous Index:
 Within 8" of Joint: **YES**
 Remarks:

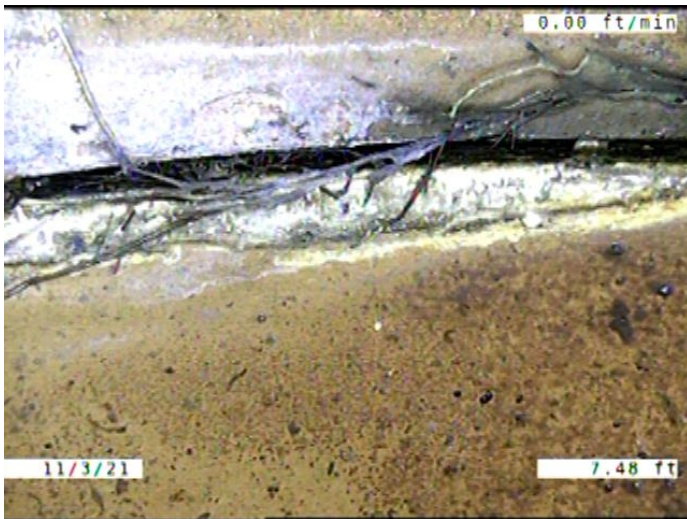

Code: **DAE**
 Description: **Deposits Attached Encrustation**

Distance (ft): **7.5**
 Structural Grade: **0**
 O&M Grade: **2**
 Clock Start/From: **8**
 Clock To: **10**
 1st Value:
 2nd Value:
 Value Percent: **5.000**
 Continuous Index:
 Within 8" of Joint: **YES**
 Remarks:

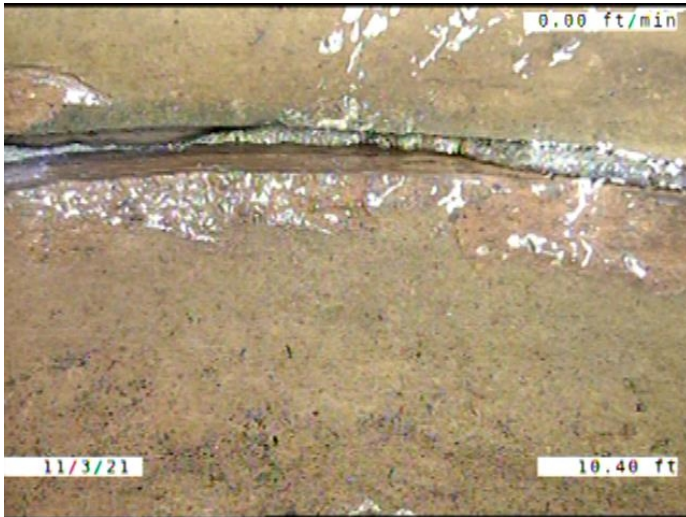


Code: **IRJ**
 Description: **Infiltration Runner Joint**

Distance (ft): **10.4**
 Structural Grade: **0**
 O&M Grade: **4**
 Clock Start/From: **12**
 Clock To: **1**
 1st Value:
 2nd Value:
 Value Percent:
 Continuous Index:
 Within 8" of Joint: **YES**
 Remarks:




Code: **RFJ**
 Description: **Roots Fine Joint**

Distance (ft): **10.4**
 Structural Grade: **0**
 O&M Grade: **1**
 Clock Start/From: **8**
 Clock To: **10**
 1st Value:
 2nd Value:
 Value Percent:
 Continuous Index:
 Within 8" of Joint: **YES**
 Remarks:

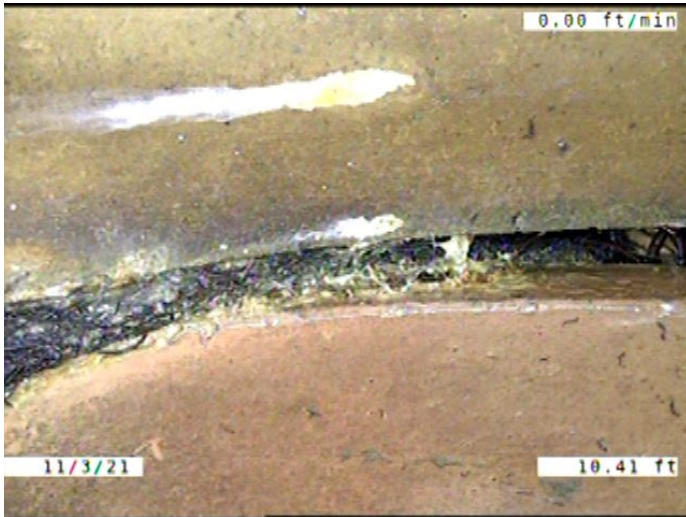

Code: **DAE**
 Description: **Deposits Attached Encrustation**

Distance (ft): **10.4**
 Structural Grade: **0**
 O&M Grade: **2**
 Clock Start/From: **8**
 Clock To: **9**
 1st Value:
 2nd Value:
 Value Percent: **5.000**
 Continuous Index:
 Within 8" of Joint: **YES**
 Remarks:

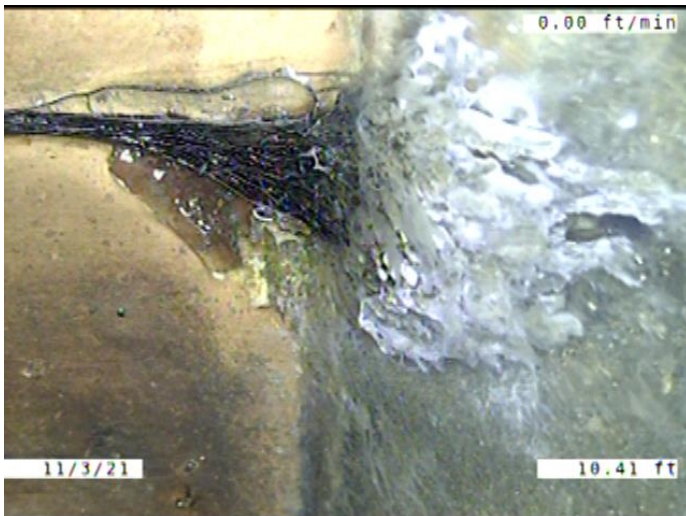


Code: **RFJ**
 Description: **Roots Fine Joint**

Distance (ft): **10.4**
 Structural Grade: **0**
 O&M Grade: **1**
 Clock Start/From: **2**
 Clock To: **4**
 1st Value:
 2nd Value:
 Value Percent:
 Continuous Index:
 Within 8" of Joint: **YES**
 Remarks:




Code: **RFJ**
 Description: **Roots Fine Joint**

Distance (ft): **13.4**
 Structural Grade: **0**
 O&M Grade: **1**
 Clock Start/From: **8**
 Clock To: **4**
 1st Value:
 2nd Value:
 Value Percent:
 Continuous Index:
 Within 8" of Joint: **YES**
 Remarks:

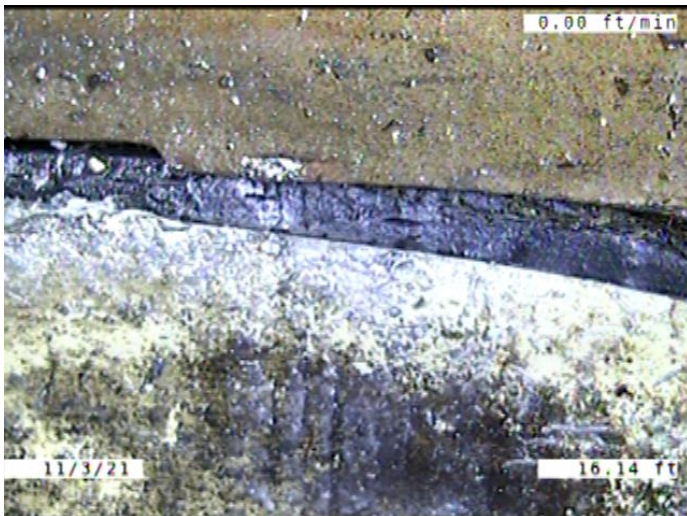


Code: **MMC**
 Description: **Miscellaneous Material Change**

Distance (ft): **16.1**
 Structural Grade: **0**
 O&M Grade: **0**
 Clock Start/From:
 Clock To:
 1st Value:
 2nd Value:
 Value Percent:
 Continuous Index:
 Within 8" of Joint: **NO**
 Remarks: **VCP TO PVC**

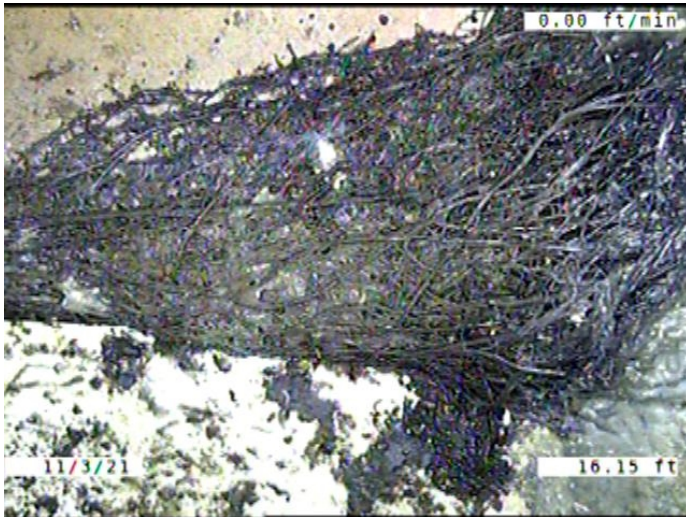


Code: **RFJ**
 Description: **Roots Fine Joint**

Distance (ft): **16.1**
 Structural Grade: **0**
 O&M Grade: **1**
 Clock Start/From: **3**
 Clock To: **4**
 1st Value:
 2nd Value:
 Value Percent:
 Continuous Index:
 Within 8" of Joint: **YES**
 Remarks:

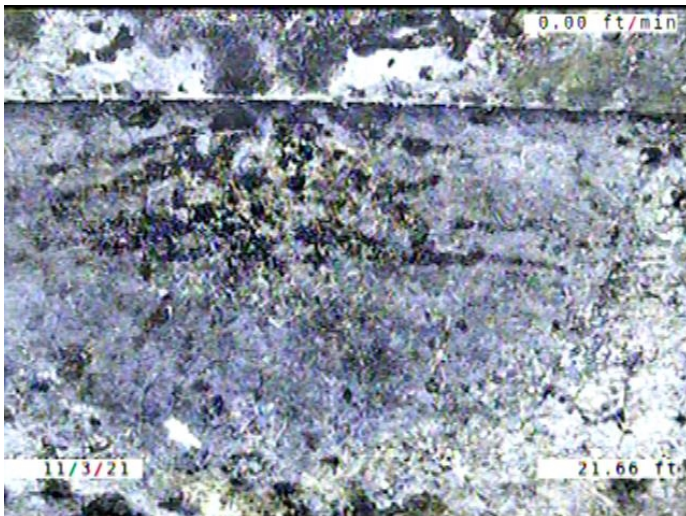


Code: **MGO**
 Description: **Miscellaneous General Observation**

Distance (ft): **21.7**
 Structural Grade: **0**
 O&M Grade: **0**
 Clock Start/From:
 Clock To:
 1st Value:
 2nd Value:
 Value Percent:
 Continuous Index:
 Within 8" of Joint: **NO**
 Remarks: **JOINT/ PIPES NOT PUSHED ALL THE WAY TOGETHER WHEN INSTALLED**

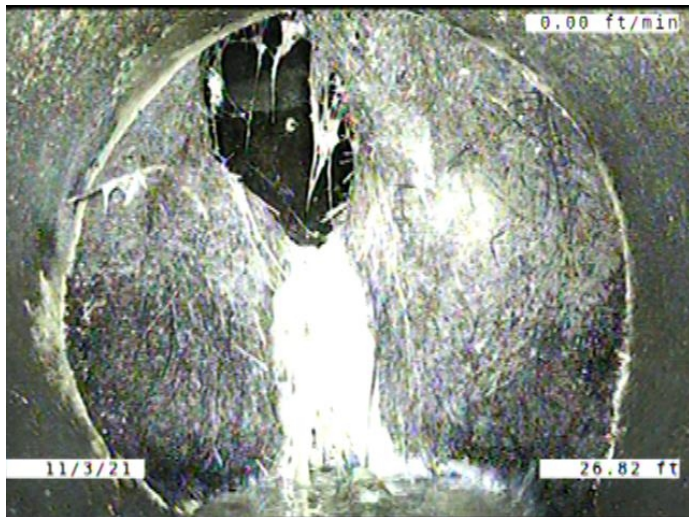


Code: **RBL**
 Description: **Roots Ball Lateral**

Distance (ft): **26.8**
 Structural Grade: **0**
 O&M Grade: **4**
 Clock Start/From: **7**
 Clock To: **5**
 1st Value:
 2nd Value:
 Value Percent: **95.000**
 Continuous Index:
 Within 8" of Joint: **NO**
 Remarks: **Entering from MH**

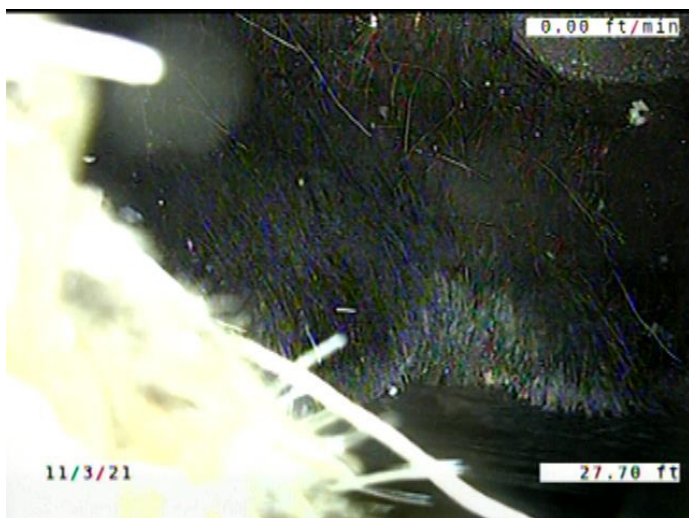

Code: **DSF**
 Description: **Deposits Settled Fine**

Distance (ft): **27.7**
 Structural Grade: **0**
 O&M Grade: **2**
 Clock Start/From: **5**
 Clock To: **7**
 1st Value:
 2nd Value:
 Value Percent: **5.000**
 Continuous Index: **F01**
 Within 8" of Joint: **YES**
 Remarks:

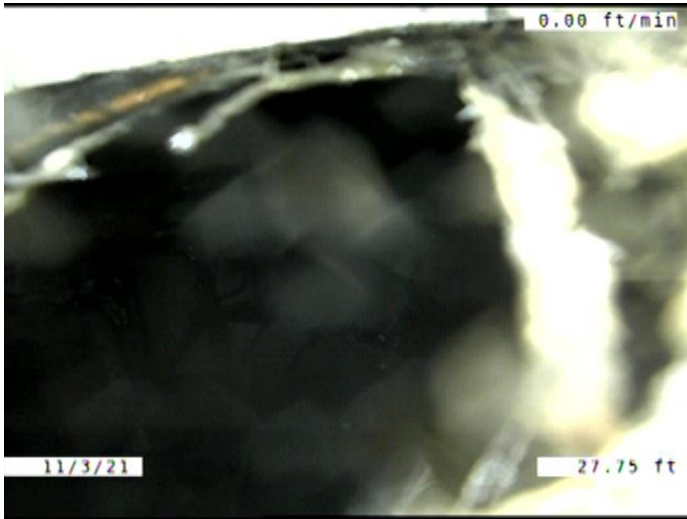

Code:	AMH
Description:	Manhole
Distance (ft):	27.7
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	UNK WABASH ST
