
Date: Pipe Length (f	04/25/2018	Weather: Owner:	City of Hobart	Coding: Pre Clean:	PACP 6.0 No Pre-Cleaning
P.O.#:	76	Surveyor:	M. Pielacha	PSR:	P-405-045-044
Customer:	City of Hobart	Clean Date:		Shape:	C
Street:	3rd Street		Flow Control:	Not Controlled	Ł
City:	Hobart, IN		Year Renewed:		
Location:	Light Highway		Tape/Media #:	DEP 76	
Purpose:	Routine Assessme	nt	Dia/Height:	15"	
Use:	Sanitary		Material:	СР	
Drain Area:			Lining:		
Category:	NA				
Comment:	YES501824 Submit	tal 2			
Location Deta	ils:		Direction of Surve	y: Upstream	
US MH:	M-405-045	DS MH:	M-405-044	Total Length Surveyed (ft): 11.1
0&M Index:	3.00	O&M Quick:	3200	O&M Rating:	6.00
tructural Index: 0.00		Structural Qu	ick: 0000		0.00
Verall Index: 3.00		Overall Quick			6.00





Code: Description:	AMH Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-405-044

Thursday, May 4, 2023

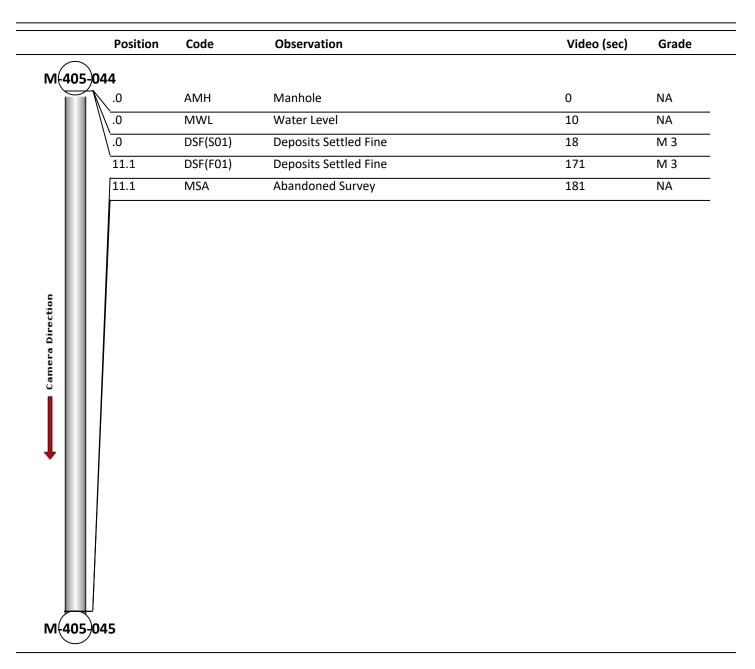

Code:	MWL
Description:	Water Level
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	10.000
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	



Code: Description:	DSF Deposits Settled Fine
Distance (ft): Structural Grade: O&M Grade: Clock Start/From: Clock To: 1st Value: 2nd Value: Value Percent: Continuous Index:	.0 0 3 5 7 15.000 S01
Within 8" of Joint: Remarks:	YES



DSF
Deposits Settled Fine
11.1
0
3
5
7
15.000
F01
NO



Code: Description:	MSA Abandoned Survey
Distance (ft):	11.1
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	Deep sediment
