
Profile/Ph	oto Observatio	n Report			RedZone
Date: Pipe Length (ft P.O.#: Customer:	04/12/2018): 144.4	Weather: Owner: Surveyor: Clean Date:	NA Jen Costello 01/01/1900	Coding: Pre Clean: PSR: Shape:	PACP 6.0 No Pre-Cleaning P-407-005-006 C
Street:	LAKESIDE DR		Flow Control:	Not Controlle	d
City:	Hobart, IN		Year Renewed:		
Location:	Yard		Tape/Media #:		
Purpose:	Routine Assessme	ent	Dia/Height:	10"	
Use:	Sanitary		Material:	PVC	
Drain Area:	NA		Lining:		
Category:	NA				
Comment:	Flow direction is r	Flow direction is marked wrong.			
Location Detai	ls:		Direction of Surv	vey: Upstream	
US MH:	M-407-006	DS MH:	M-407-005	Total Length Surveyed (ft	:): 135.3
D&M Index:	0.00	O&M Quick:	000	0 O&M Rating:	0.00
Structural Index:	0.00	Structural Q	uick: 000		0.00
Overall Index:	0.00	Overall Quic	k: 000	0 Overall Rating:	0.00






Code: Description:	AMH Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-407-005

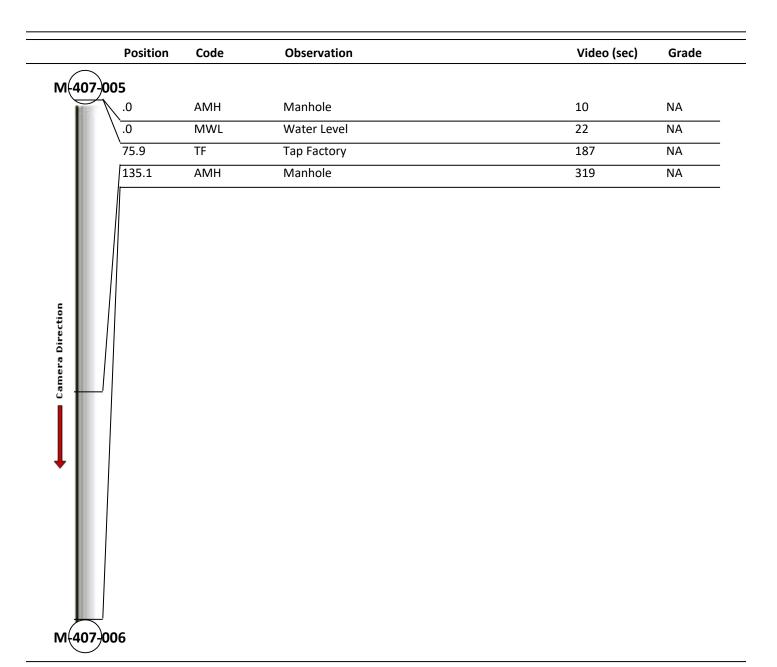


Code: MWL Description: Water Level

Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	5.000
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	



Code: Description:	TF Tap Factory
Distance (ft):	75.9
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	9
Clock To:	
1st Value:	4.000
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	
Remarks:	



Code:AMHDescription:Manhole

Distance (ft):	135.1
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-407-006
