
Date:	04/10/2018	Weather:		Coding:	PACP 6.0
Pipe Length (ft):	200.9	Owner:	NA	Pre Clean:	Not Known
P.O.#:		Surveyor:	Byrd Fitzgerald	PSR:	P-503-012-011
Customer:		Clean Date:	01/01/1900	Shape:	С
Street:	W 40th ave		Flow Control:	Not Controlled	
City:	Hobart, IN		Year Renewed:		
Location:	Other		Tape/Media #:		
Purpose:	Not Known		Dia/Height:	10"	
Use:	Sanitary		Material:	PVC	
Drain Area:	NA		Lining:		
Category:	NA				
Comment:					
Location Details	:		Direction of Survey	: Downstream	
US MH:	M-503-011	DS MH:	M-503-012	Total Length Surveyed (ft)	38.8
D&M Index:	2.00	O&M Quick:	2600	O&M Rating:	12.00
Structural Index:	0.00	Structural Qu	uick: 0000	Structural Rating:	0.00
Overall Index:	2.00	Overall Quic		Overall Rating:	12.00





Code: Description:	AMH Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-503-011

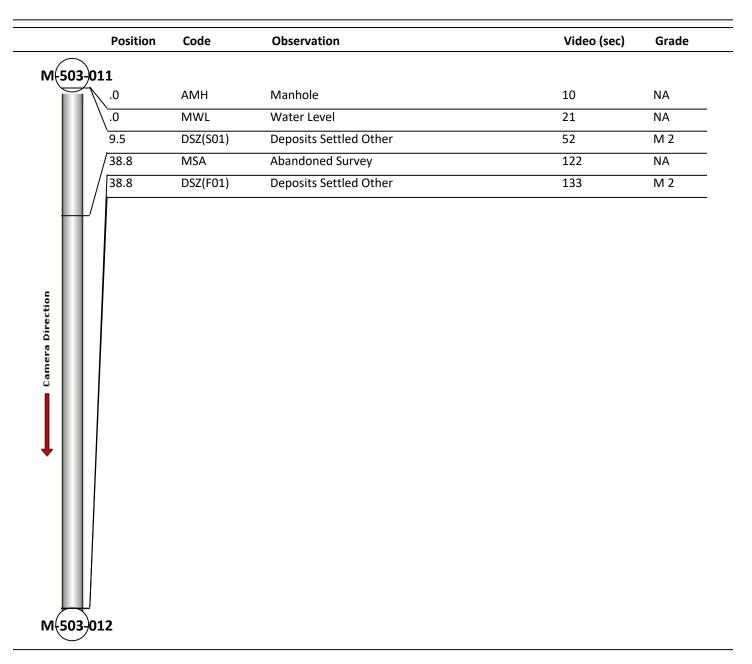

Code: MWL Description: Water Level

Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	5.000
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	



Code:	DSZ
Description:	Deposits Settled Other

Distance (ft):	9.5
Structural Grade:	0
O&M Grade:	2
Clock Start/From:	6
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	5.000
Continuous Index:	S01
Within 8" of Joint:	NO
Remarks:	tissue



Code:MSADescription:Abandoned Survey

38.8
0
0
NO
no blockage

DSZ

Deposits Settled Other



Distance (ft):	38.8
Structural Grade:	0
O&M Grade:	2
Clock Start/From:	6
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	5.000
Continuous Index:	F01
Within 8" of Joint:	NO
Remarks:	tissue

Code:

Description:
