

Profile/Photo Observation Report




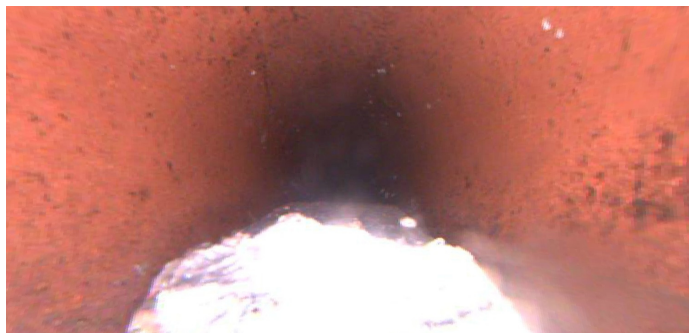
Date:	04/07/2018	Weather:		Coding:	PACP 6.0
Pipe Length (ft):	190.2	Owner:	NA	Pre Clean:	Not Known
P.O.#:		Surveyor:	Byrd Fitzgerald	PSR:	P-503-035-036
Customer:		Clean Date:	01/01/1900	Shape:	C

Street:	ALLEY BETWEEN N COLORADO ST &	Flow Control:	Not Controlled
City:	Hobart, IN	Year Renewed:	
Location:	Other	Tape/Media #:	
Purpose:	Not Known	Dia/Height:	10"
Use:	Sanitary	Material:	VCP
Drain Area:	NA	Lining:	
Category:	NA		
Comment:			

Location Details:		Direction of Survey:	Upstream
US MH:	M-503-036	DS MH:	M-503-035
		Total Length Surveyed (ft):	30.6

O&M Index:	3.00	O&M Quick:	3600	O&M Rating:	18.00
Structural Index:	0.00	Structural Quick:	0000	Structural Rating:	0.00
Overall Index:	3.00	Overall Quick:	3600	Overall Rating:	18.00


	Position	Code	Observation	Video (sec)	Grade
	.0	AMH	Manhole	10	NA
	.0	MWL	Water Level	21	NA
	.0	DSC(S01)	Deposits Settled Compacted	32	M 3
	30.6	MSA	Abandoned Survey	105	NA
	30.6	DSC(F01)	Deposits Settled Compacted	116	M 3



Code: **AMH**
 Description: **Manhole**


Distance (ft): **.0**
 Structural Grade: **0**
 O&M Grade: **0**
 Clock Start/From:
 Clock To:
 1st Value:
 2nd Value:
 Value Percent:
 Continuous Index:
 Within 8" of Joint: **NO**
 Remarks: **M-503-035**

Code:	MWL
Description:	Water Level

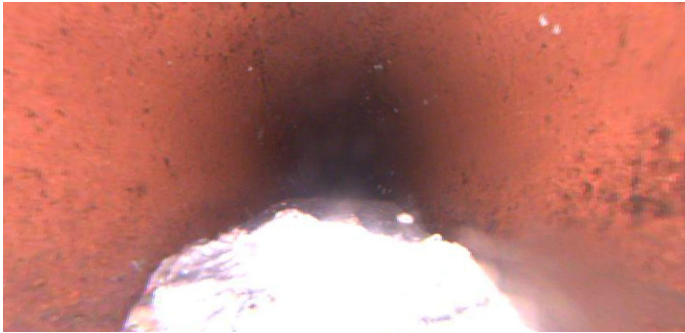


Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	5.000
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	

Code:	DSC
Description:	Deposits Settled Compacted

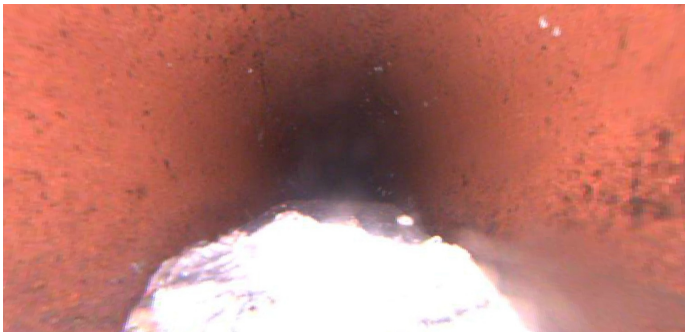


Distance (ft):	.0
Structural Grade:	0
O&M Grade:	3
Clock Start/From:	6
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	15.000
Continuous Index:	S01
Within 8" of Joint:	NO
Remarks:	block of concrete/ashpalt??

Code: **MSA**
Description: **Abandoned Survey**

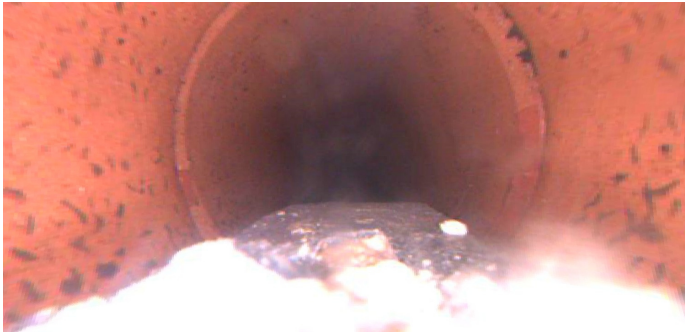

Distance (ft): **30.6**
Structural Grade: **0**
O&M Grade: **0**
Clock Start/From:
Clock To:
1st Value:
2nd Value:
Value Percent:
Continuous Index:
Within 8" of Joint: **NO**
Remarks: **dsc**

Code: **DSC**
Description: **Deposits Settled Compacted**

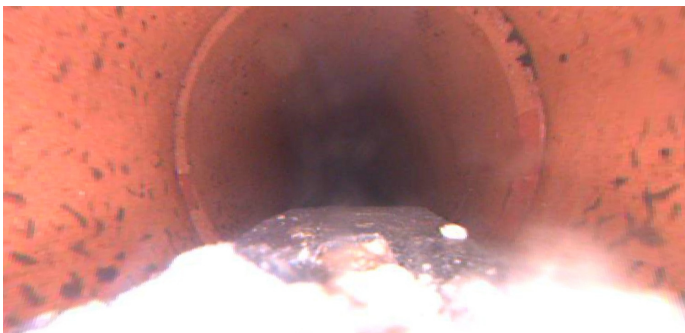

Distance (ft): **30.6**
Structural Grade: **0**
O&M Grade: **3**
Clock Start/From: **6**
Clock To:
1st Value:
2nd Value:
Value Percent: **15.000**
Continuous Index: **F01**
Within 8" of Joint: **NO**
Remarks: **block of concrete/ashpalt??**
