

Date:	<b>04/14/2018</b>	Weather:	City of the	<b>-</b>	Coding:	PACP 6.0
Pipe Length (ft P.O.#:	.): 48-2	Owner: Surveyor:	City of Hol M. Pielach		Pre Clean: PSR:	No Pre-Cleaning M-504-027-M-504-02
Customer:	Gity of Hobart	Clean Date:		a	Shape:	C
Street:	Cleveland Avenue		Flow Contro	ol:	Not Controlled	l
City:	Hobart, IN		Year Renew	ed:		
Location:	Light Highway		Tape/Media	n #:	<b>DEP 48</b>	
Purpose:	<b>Routine Assessment</b>		Dia/Height:		18"	
Use:	Sanitary		Material:		VCP	
Drain Area:			Lining:			
Category:	NA					
Comment:						
Location Detai	ls:		Direction of	Survey:	Downstream	
US MH:	M-504-027	DS MH:	M-504-026		Total Length Surveyed (ft)	): <b>160.5</b>
0&M Index:	0.00	O&M Quick:		0000	O&M Rating:	0.00
tructural Index	0.00		uick: 0000		Structural Rating:	0.00
Overall Index:	0.00	Overall Quicl		0000	Overall Rating:	0.00



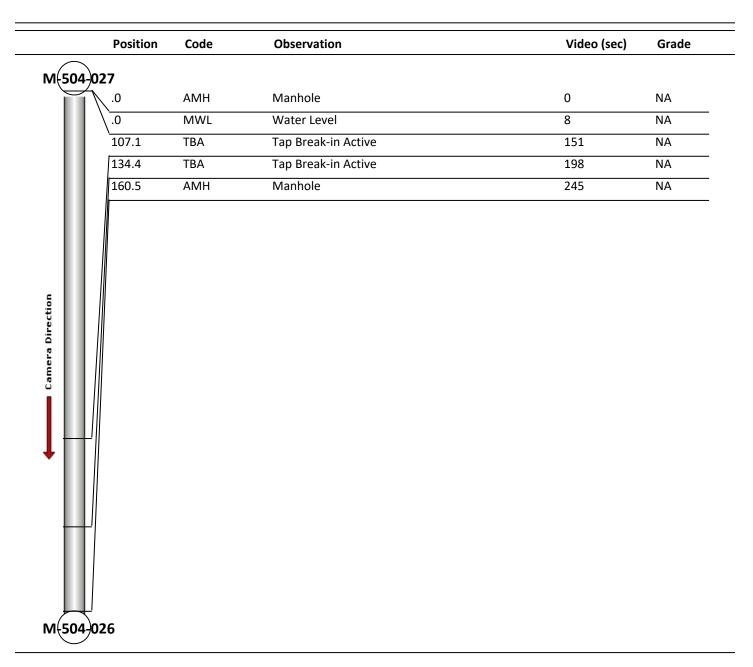

Code: Description:	AMH Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-504-027

Thursday, May 4, 2023

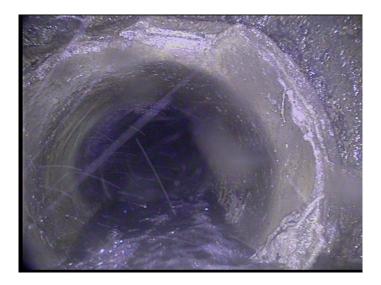


Code:	MWL
Description:	Water Level
	•
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	5.000
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	



Code: Description:	TBA Tap Break-in Active
Distance (ft):	107.1
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	2
Clock To:	
1st Value:	4.000
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	



Code: Description:	TBA Tap Break-in Active
Distance (ft):	134.4
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	2
Clock To:	
1st Value:	4.000
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	

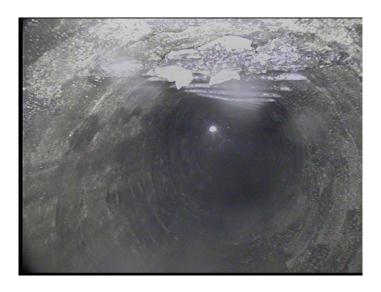

Description: Manhole
Distance (ft): <b>160.5</b>
Structural Grade: 0
O&M Grade: <b>0</b>
Clock Start/From:
Clock To:
1st Value:
2nd Value:
Value Percent:
Continuous Index:
Within 8" of Joint: NO
Remarks: <b>M-504-026</b>
