

						ROBOTICS
Date:	04/10/2018	Weather:			Coding:	PACP 6.0
Pipe Length (ft)	):	Owner:	City of Hoba	rt	Pre Clean:	No Pre-Cleaning
P.O.#:	25-1	Surveyor:	M. Pielacha		PSR:	M-504-071-M-504-070
Customer:	City of Hobart	Clean Date:			Shape:	С
Street:	Off Virginia Street		Flow Control:		Not Controlled	
City:	Hobart, IN		Year Renewed	l:		
Location:	Light Highway		Tape/Media #	:	DEP 25	
Purpose:	Routine Assessmen	t	Dia/Height:		18"	
Use:	Sanitary		Material:		VCP	
Drain Area:			Lining:			
Category:	NA					
Comment:						
Location Detail	s:		Direction of Su	urvey:	Upstream	
US MH:	M-504-071	DS MH:	M-504-070	Tota	Length Surveyed (ft)	3.8
0&M Index:	3.00	O&M Quick:	3	100	O&M Rating:	3.00
tructural Index:	0.00	Structural Qu	uick: 0	000	Structural Rating:	0.00
)verall Index:	3.00	Overall Quicl		100	Overall Rating:	3.00



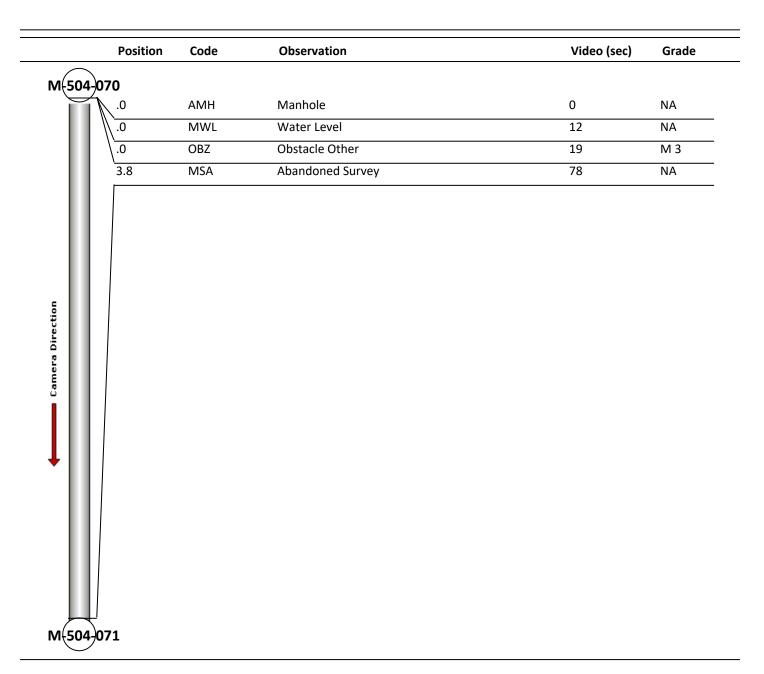

Code: Description:	AMH Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-504-070

Friday, October 1, 2021

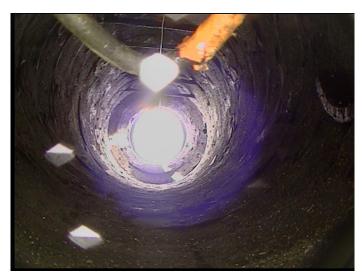

Code:	MWL
Description:	Water Level
Distance (ft):	0
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	15.000
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	



Code: Description:	OBZ Obstacle Other
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	3
Clock Start/From:	5
Clock To:	7
1st Value:	
2nd Value:	
Value Percent:	20.000
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	Debris



Code: Description:	MSA Abandoned Survey
Distance (ft):	3.8
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	debris
