

| Date:             | 04/09/2018    | Weather:      |                   | Coding:                   | PACP 6.0       |
|-------------------|---------------|---------------|-------------------|---------------------------|----------------|
| Pipe Length (ft)  | : <b>78.7</b> | Owner:        | NA                | Pre Clean:                | Not Known      |
| P.O.#:            |               | Surveyor:     | Jen Costello      | PSR:                      | P-503-032-113  |
| Customer:         |               | Clean Date:   | 01/01/1900        | Shape:                    | С              |
| Street:           | W 40th ave    |               | Flow Control:     | Not Controlled            | 1              |
| City:             | Hobart, IN    |               | Year Renewed:     |                           |                |
| Location:         | Other         |               | Tape/Media #:     |                           |                |
| Purpose:          | Not Known     |               | Dia/Height:       | 10"                       |                |
| Use:              | Sanitary      |               | Material:         | СР                        |                |
| Drain Area:       | NA            |               | Lining:           |                           |                |
| Category:         | NA            |               |                   |                           |                |
| Comment:          |               |               |                   |                           |                |
| Location Detail   | s:            |               | Direction of Surv | ey: Downstream            |                |
| US MH:            | M-503-032     | DS MH:        | M-504-113         | Total Length Surveyed (ft | ): <b>14.6</b> |
| D&M Index:        | 0.00          | O&M Quick:    | 000               | 0 O&M Rating:             | 0.00           |
| Structural Index: | 3.20          | Structural Qu | uick: 413         |                           | 16.00          |
| Overall Index:    | 3.20          | Overall Quick | 44.2              |                           | 16.00          |



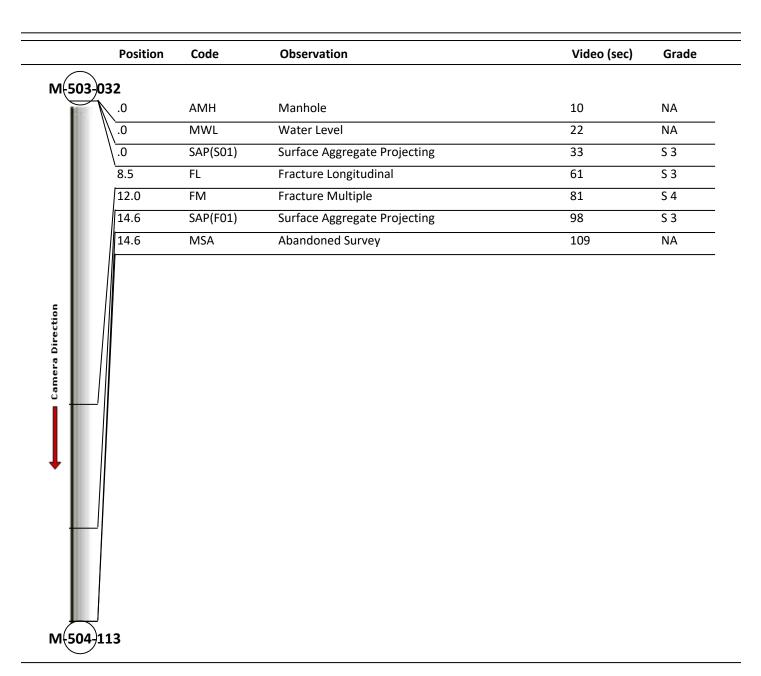

| Code:<br>Description: | AMH<br>Manhole |
|-----------------------|----------------|
| Distance (ft):        | .0             |
| Structural Grade:     | 0              |
| O&M Grade:            | 0              |
| Clock Start/From:     |                |
| Clock To:             |                |
| 1st Value:            |                |
| 2nd Value:            |                |
| Value Percent:        |                |
| Continuous Index:     |                |
| Within 8" of Joint:   | NO             |
| Remarks:              | M-503-032      |




Code: MWL Description: Water Level

| Distance (ft):      | .0    |
|---------------------|-------|
| Structural Grade:   | 0     |
| O&M Grade:          | 0     |
| Clock Start/From:   |       |
| Clock To:           |       |
| 1st Value:          |       |
| 2nd Value:          |       |
| Value Percent:      | 5.000 |
| Continuous Index:   |       |
| Within 8" of Joint: | NO    |
| Remarks:            |       |
|                     |       |


| Code:        | SAP                          |
|--------------|------------------------------|
| Description: | Surface Aggregate Projecting |

| Distance (ft):      | .0  |
|---------------------|-----|
| Structural Grade:   | 3   |
| O&M Grade:          | 0   |
| Clock Start/From:   | 8   |
| Clock To:           | 4   |
| 1st Value:          |     |
| 2nd Value:          |     |
| Value Percent:      |     |
| Continuous Index:   | S01 |
| Within 8" of Joint: |     |
| Remarks:            |     |



Code:FLDescription:Fracture Longitudinal

| Distance (ft):      | 8.5 |
|---------------------|-----|
| Structural Grade:   | 3   |
| O&M Grade:          | 0   |
| Clock Start/From:   | 3   |
| Clock To:           |     |
| 1st Value:          |     |
| 2nd Value:          |     |
| Value Percent:      |     |
| Continuous Index:   |     |
| Within 8" of Joint: | YES |
| Remarks:            |     |



| Code:<br>Description: | FM<br>Fracture Multiple |
|-----------------------|-------------------------|
|                       |                         |
| Distance (ft):        | 12.0                    |
| Structural Grade:     | 4                       |
| O&M Grade:            | 0                       |
| Clock Start/From:     | 12                      |
| Clock To:             | 1                       |
| 1st Value:            |                         |
| 2nd Value:            |                         |
| Value Percent:        |                         |
| Continuous Index:     |                         |
| Within 8" of Joint:   | YES                     |
| Remarks:              |                         |



Code:SAPDescription:Surface Aggregate Projecting

| Distance (ft):      | 14.6 |
|---------------------|------|
| Structural Grade:   | 3    |
| O&M Grade:          | 0    |
| Clock Start/From:   | 8    |
| Clock To:           | 4    |
| 1st Value:          |      |
| 2nd Value:          |      |
| Value Percent:      |      |
| Continuous Index:   | F01  |
| Within 8" of Joint: |      |
| Remarks:            |      |

Code:



| Description:        | Abandoned Survey   |
|---------------------|--------------------|
|                     |                    |
|                     |                    |
| Distance (ft):      | 14.6               |
| Structural Grade:   | 0                  |
| O&M Grade:          | 0                  |
| Clock Start/From:   |                    |
| Clock To:           |                    |
| 1st Value:          |                    |
| 2nd Value:          |                    |
| Value Percent:      |                    |
| Continuous Index:   |                    |
| Within 8" of Joint: | NO                 |
| Remarks:            | DEBRIS UNDER WATER |

MSA
