


		-				ROBOTICS
Date:	04/16/2018	Weather:			Coding:	PACP 6.0
Pipe Length (ft)	:	Owner:	City of Ho	bart	Pre Clean:	No Pre-Cleaning
P.O.#:	56-1	Surveyor:	M. Pielac	ha	PSR:	M-505-037-M-505-034
Customer:	City of Hobart	Clean Date:			Shape:	С
Street:	Colorado Street		Flow Contro	ol:	Not Controlled	l
City:	Hobart, IN		Year Renew	ved:		
Location:	Light Highway		Tape/Medi	a #:	DEP 56	
Purpose:	Routine Assessment		Dia/Height:	:	18"	
Use:	Sanitary		Material:		VCP	
Drain Area:			Lining:			
Category:	NA					
Comment:						
Location Details	5:		Direction o	f Survey:	Downstream	
US MH:	M-505-037	DS MH:	M-505-034		Total Length Surveyed (ft)): 165.2
0&M Index:	1.00	O&M Quick:		1100	O&M Rating:	1.00
tructural Index:	3.00	 Structural Qu	uick:	3100	Structural Rating:	3.00
)verall Index:	2.00	Overall Quicl		3111	Overall Rating:	4.00

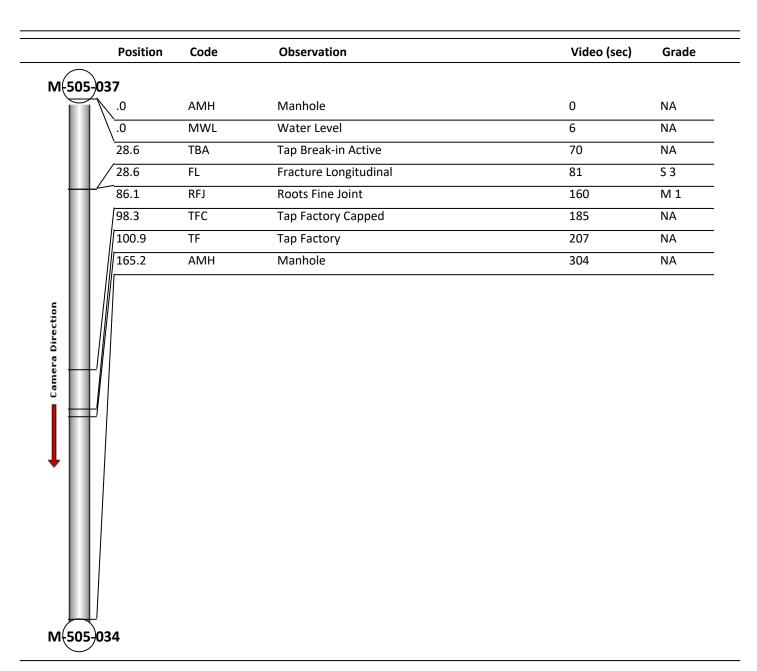

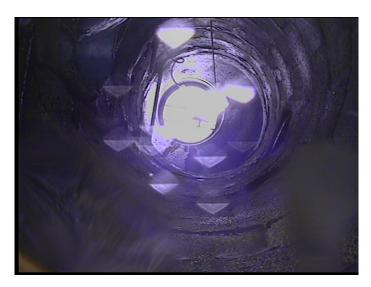

Code: Description:	AMH Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-505-037

Friday, October 1, 2021

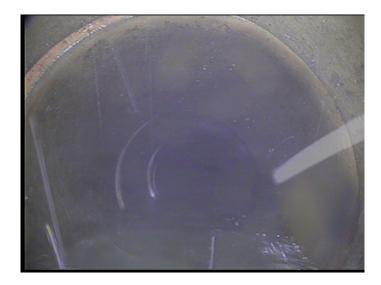

Code:	MWL
Description:	Water Level
Distance (ft):	.0
Distance (It).	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	20.000
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	



Code: Description:	TBA Tap Break-in Active
Distance (ft):	28.6
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	2
Clock To:	
1st Value:	4.000
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	



Code: Description:	FL Fracture Longitudinal
Distance (ft):	28.6
Structural Grade:	3
O&M Grade:	0
Clock Start/From:	2
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	YES
Remarks:	



Code: Description:	RFJ Roots Fine Joint
Distance (ft):	86.1
Structural Grade:	0
O&M Grade:	1
Clock Start/From:	12
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	YES
Remarks:	



Code: Description:	TFC Tap Factory Capped
Distance (ft):	98.3
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	10
Clock To:	
1st Value:	4.000
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	



Code: Description:	TF Tap Factory
Distance (ft):	100.9
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	2
Clock To:	
1st Value:	4.000
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	



Code: Description:	AMH Manhole
Distance (ft):	165.2
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-505-034
