Date:	04/16/2018	Weather:		_	Coding:	PACP 6.0
Pipe Length (ft)		Owner:	City of Ho		Pre Clean:	No Pre-Cleaning
P.O.#:	54-4	Surveyor:	M. Pielac	ha	PSR:	M-505-046-M-505-043
Customer:	City of Hobart	Clean Date:			Shape:	С
Street:	Colorado Street		Flow Contr	ol:	Not Controlled	
City:	Hobart, IN		Year Renev	ved:		
Location:	Light Highway		Tape/Medi	a #:	<b>DEP 54</b>	
Purpose:	Routine Assessment		Dia/Height	:	18"	
Use:	Sanitary		Material:		VCP	
Drain Area:			Lining:			
Category:	NA					
Comment:						
Location Detail	s:		Direction o	f Survey:	Downstream	
US MH:	M-505-046	DS MH:	M-505-043		Total Length Surveyed (ft)	: <b>163.9</b>
&M Index:	3.00	O&M Quick:		3300	O&M Rating:	9.00
tructural Index:	1.00		uick:	1100	Structural Rating:	1.00
)verall Index:	2.50	 Overall Quicl		3311	Overall Rating:	10.00

	Position	Code	Observation	Video (sec)	Grade
N(505-)0	046				
$\leq$	0.	AMH	Manhole	0	NA
	.0	MWL	Water Level	7	NA
	10.7	CC	Crack Circumferential	38	S 1
	56.9	RMJ(S01)	Roots Medium Joint	133	M 3
	73.5	RMJ(F01)	Roots Medium Joint	184	M 3
	120.2	MWL	Water Level	289	NA
	///163.9	AMH	Manhole	496	NA




Code: Description:	AMH Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-505-046

Thursday, May 4, 2023

\_



Code:	MWL
Description:	Water Level
Distance (ft):	.0
( )	
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	20.000
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	

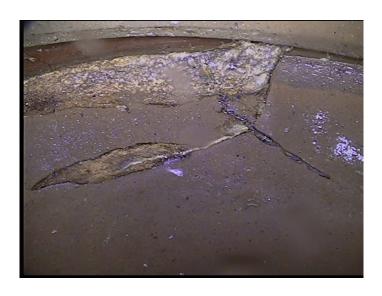

Code: Description:	CC Crack Circumferential
Distance (ft): Structural Grade: O&M Grade: Clock Start/From: Clock To: 1st Value: 2nd Value: Value Percent: Continuous Index:	10.7 1 0 9 11
Within 8" of Joint: Remarks:	YES




Code:	RMJ
Description:	<b>Roots Medium Joint</b>
Distance (ft):	56.9
Structural Grade:	0
O&M Grade:	3
Clock Start/From:	10
Clock To:	2
1st Value:	
2nd Value:	
Value Percent:	10.000
Continuous Index:	S01
Within 8" of Joint:	YES
Remarks:	



Code: Description:	RMJ Roots Medium Joint
Distance (ft): Structural Grade: O&M Grade: Clock Start/From: Clock To: 1st Value: 2nd Value: Value Percent: Continuous Index:	73.5 0 3 10 2 10.000 F01
Within 8" of Joint: Remarks:	YES



Code:	MWL
Description:	Water Level
Distance (ft):	120.2
Distance (ft):	120.2
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	45.000
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	

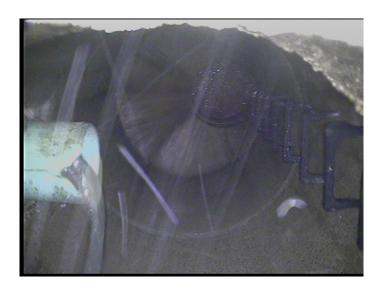

Code: Description:	AMH Manhole
Distance (ft):	163.9
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-505-043
