
Profile/Ph	oto Observation	Report				RedZone
Date: Pipe Length (ft P.O.#:	04/07/2018 ): 202.8	Weather: Owner: Surveyor:	NA Jen Costello		Coding: Pre Clean: PSR:	PACP 6.0 No Pre-Cleaning P-506-016-015
Customer:		Clean Date:	01/01/1900		Shape:	C
Street:	W 7TH PL		Flow Control:		Not Controlled	
City:	Hobart, IN		Year Renewed:			
Location:	Yard		Tape/Media #:			
Purpose:	Routine Assessme	nt	Dia/Height:		10"	
Use:	Sanitary		Material:		VCP	
Drain Area:	NA		Lining:			
Category:	NA					
Comment:	P_C DAE 16lf, flow	direction is mar	ked wrong.			
Location Detail	ls:		Direction of Sur	vey:	Upstream	
US MH:	M-506-015	DS MH:	M-506-016	Tota	ll Length Surveyed (ft)	: <b>18.0</b>
O&M Index:	2.00	O&M Quick:	21	00	O&M Rating:	2.00
Structural Index:	2.00	Structural Qu	uick: 22	00	Structural Rating:	4.00
Overall Index:	2.00	Overall Quick	<: <b>23</b>	00	Overall Rating:	6.00

D

1.77



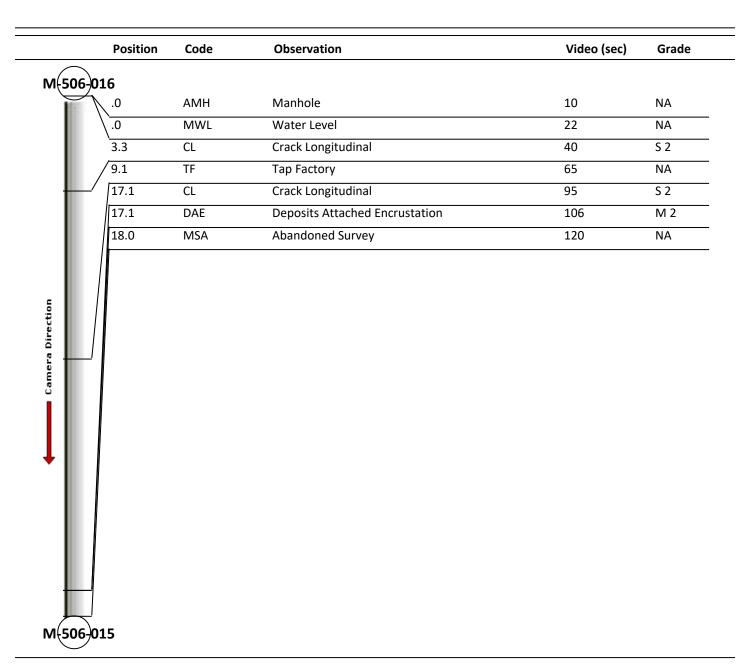


Code: Description:	AMH Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-506-016




Code: MWL Description: Water Level

Distance (ft): .0 Structural Grade: 0 O&M Grade: 0 Clock Start/From: Clock To: 1st Value: 2nd Value: Value Percent: 5.000 Continuous Index: Within 8" of Joint: NO Remarks:



CL	
Crack Longitudinal	


Distance (ft):	3.3
Structural Grade:	2
O&M Grade:	0
Clock Start/From:	1
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	YES
Remarks:	




Code:	TF
Description:	Tap Factory

Distance (ft):	9.1
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	3
Clock To:	
1st Value:	4.000
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	
Remarks:	

Remarks:



Code: Description:	CL Crack Longitudinal
Distance (ft):	17.1
Structural Grade:	2
O&M Grade:	0
Clock Start/From:	12
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	YES



Code:DAEDescription:Deposits Attached Encrustation

Distance (ft):	17.1
Structural Grade:	0
O&M Grade:	2
Clock Start/From:	8
Clock To:	4
1st Value:	
2nd Value:	
Value Percent:	10.000
Continuous Index:	
Within 8" of Joint:	YES
Remarks:	

Code:	
Description:	

MSA Abandoned Survey

Distance (ft):	18.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	dae
