

Profile/Ph	oto Observation	Report			RedZone
Date:	10/09/2018	Weather:		Coding:	PACP 6.0
Pipe Length (ft): 244.7	Owner:	NA	Pre Clean:	Not Known
P.O.#:		Surveyor:	Selasie Honu	PSR:	P-507-006-004
Customer:		Clean Date:	01/01/1900	Shape:	c
Street:	S DELAWARE ST		Flow Control:	Not Controlled	
City:	Hobart, IN		Year Renewed:		
Location:	Light Highway		Tape/Media #:		
Purpose:	Routine Assessmen	nt	Dia/Height:	12"	
Use:	Sanitary		Material:	VCP	
Drain Area:	NA		Lining:		
Category:	NA				
Comment:					
Location Detai	ls:		Direction of Survey	: Upstream	
US MH:	M-507-004	DS MH:	M-507-006	Total Length Surveyed (ft):	29.6
0&M Index:	3.00	O&M Quick:	3100	O&M Rating:	3.00
tructural Index:	2.00	Structural Qui	ck: 2100	Structural Rating:	2.00
Overall Index:	2.50	Overall Quick:		Overall Rating:	5.00



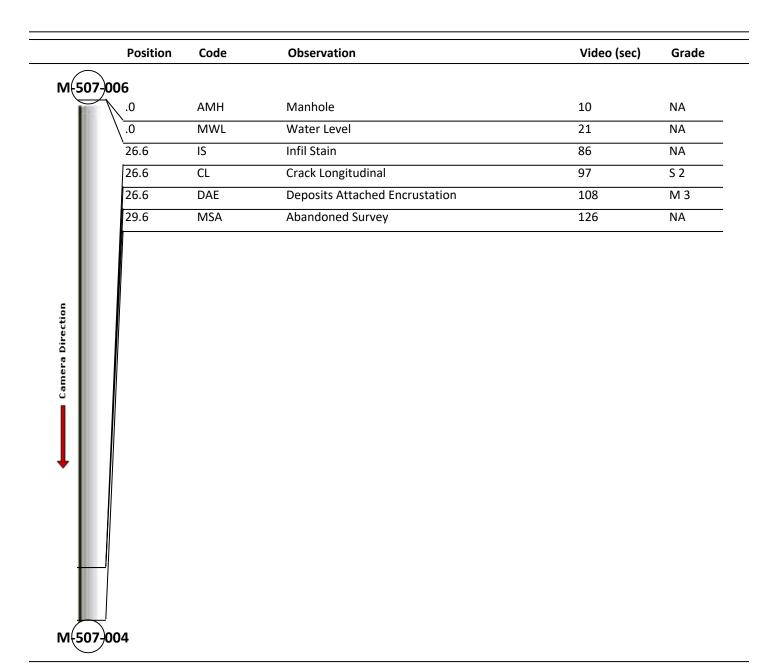


Code: Description:	AMH Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-507-006




Code: MWL Description: Water Level

Distance (ft): .0 Structural Grade: 0 O&M Grade: 0 Clock Start/From: Clock To: 1st Value: 2nd Value: Value Percent: 5.000 Continuous Index: Within 8" of Joint: NO Remarks:




Code: Description:	IS Infil Stain
Distance (ft):	26.6
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	8
Clock To:	4
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	YES
Remarks:	




Code:CLDescription:Crack Longitudinal

Distance (ft):	26.6
Structural Grade:	2
O&M Grade:	0
Clock Start/From:	1
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	YES
Remarks:	



Code:	DAE
Description:	Deposits Attached Encrustation

Distance (ft):	26.6
Structural Grade:	0
O&M Grade:	3
Clock Start/From:	8
Clock To:	4
1st Value:	
2nd Value:	
Value Percent:	20.000
Continuous Index:	
Within 8" of Joint:	YES
Remarks:	



Code: Description: MSA Abandoned Survey

Distance (ft):	29.6
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	camera stopped
