
Profile/Pho	oto Observation	Report			RedZon R 0 B 0 T I C S
Date:	03/28/2018	Weather:		Coding:	PACP 6.0
Pipe Length (ft)	: 218.0	Owner:	NA	Pre Clean:	No Pre-Cleaning
P.O.#:		Surveyor:	Selasie Honu	PSR:	
Customer:		Clean Date:	01/01/1900	Shape:	С
Street:	FOXCROFT STREET		Flow Control:	Not Controlled	
City:	Hobart, IN		Year Renewed:		
Location:	Yard		Tape/Media #:		
Purpose:	Routine Assessme	nt	Dia/Height:	12"	
Use:	Sanitary		Material:	VCP	
Drain Area:	NA		Lining:		
Category:	NA				
Comment:	R_M at 8 ft nothing	g visible rocks in	the tracks		
Location Details	5:		Direction of Surve	ey: Downstream	
US MH:	M-507-011	DS MH:	M-507-019A	Total Length Surveyed (ft):	9.4
D&M Index:	2.00	O&M Quick:	2400	O&M Rating:	8.00
Structural Index:	0.00	Structural Qu	uick: 0000	Structural Rating:	0.00
Overall Index:	2.00	Overall Quick	<: <b>2400</b>	Overall Rating:	8.00





Code: Description:	AMH Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-507-011

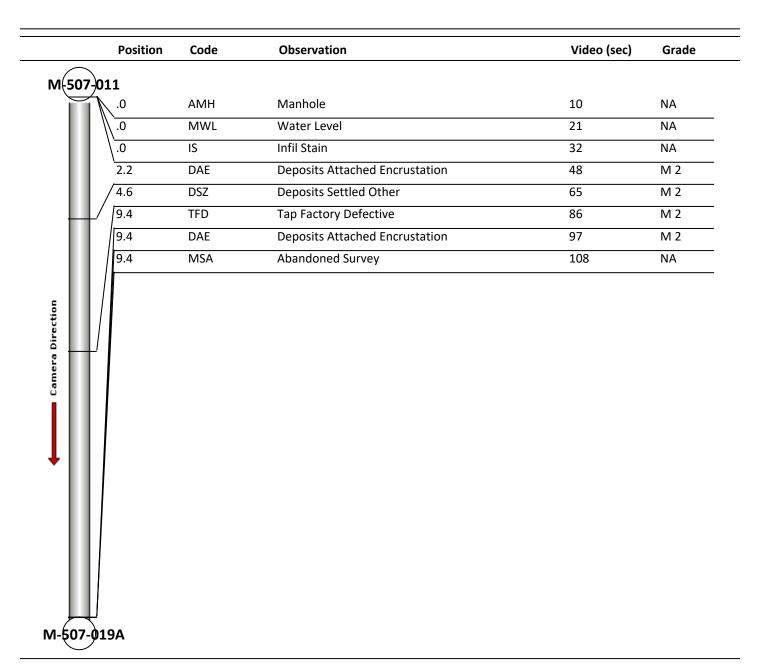

Code: MWL Description: Water Level

Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	5.000
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	



Code: Description:	IS Infil Stain
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	8
Clock To:	12
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	YES
Remarks:	



Code:DAEDescription:Deposits Attached Encrustation

Distance (ft):	2.2
Structural Grade:	0
O&M Grade:	2
Clock Start/From:	8
Clock To:	4
1st Value:	
2nd Value:	
Value Percent:	5.000
Continuous Index:	
Within 8" of Joint:	YES
Remarks:	

Code:	DSZ	
Description:	<b>Deposits Settled Other</b>	

Distance (ft):	4.6
Structural Grade:	0
O&M Grade:	2
Clock Start/From:	4
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	10.000
Continuous Index:	
Within 8" of Joint:	YES
Remarks:	mixed material



Code:TFDDescription:Tap Factory Defective

Distance (ft):	9.4
Structural Grade:	0
O&M Grade:	2
Clock Start/From:	3
Clock To:	
1st Value:	4.000
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	
Remarks:	DAE

Remarks: DAE

Description:

Deposits Attached Encrustation



Distance (ft):	9.4
Structural Grade:	0
O&M Grade:	2
Clock Start/From:	3
Clock To:	4
1st Value:	
2nd Value:	
Value Percent:	5.000
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	



Code: Description: MSA Abandoned Survey

Distance (ft):	9.4
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	camera stopped
