
Date:	05/02/2018	Weather:		Coding:	PACP 6.0
Pipe Length (f		Owner:	City of Hobart	Pre Clean:	Not Known
P.O.#:	284	Surveyor:	B. Helbling	PSR:	P-507-036.2-036.3
Customer:	City of Hobart	Clean Date:		Shape:	C
Street:	West 10th Street		Flow Control:	Not Controlled	1
City:	Hobart, IN		Year Renewed:		
Location:	Light Highway		Tape/Media #:	DEP284	
Purpose:	Routine Assessment		Dia/Height:	12"	
Use:	Sanitary		Material:	PVC	
Drain Area:			Lining:		
Category:	NA				
Comment:	5-21-2018				
Location Detai	ils:		Direction of Survey	/: Downstream	
US MH:	M-507-036.2	DS MH:	M-507-036.3	Total Length Surveyed (ft): 398.3
0&M Index:	0.00	O&M Quick:	0000	O&M Rating:	0.00
Structural Index		 Structural Qu	uick: 0000	Structural Rating:	0.00
Overall Index:	0.00	 Overall Quicl	. 0000	Overall Rating:	0.00





Code: Description:	AMH Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-507-036.2

Thursday, May 4, 2023

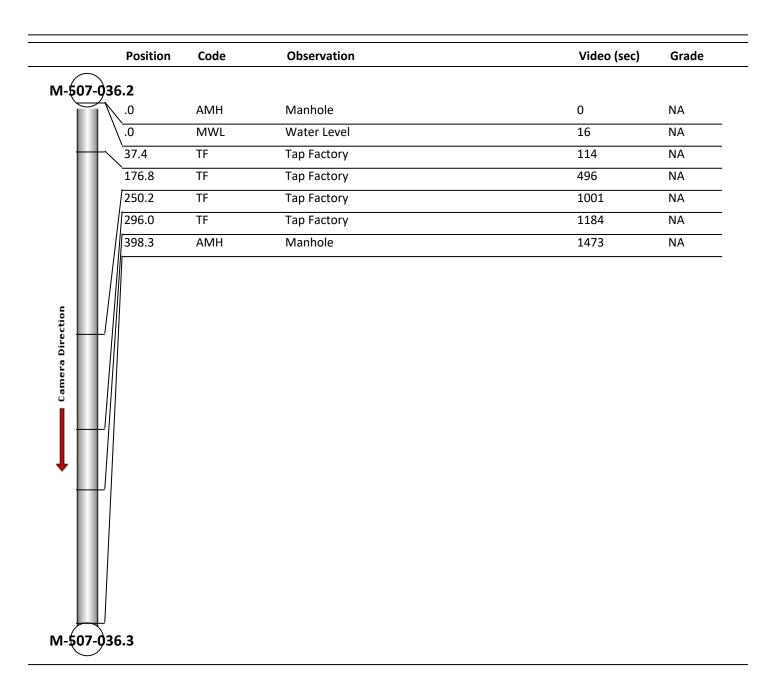

Code:	MWL
Description:	Water Level
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	5.000
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	



Code:	TF
Description:	Tap Factory
Distance (ft):	37.4
Structural Grade:	0
O&M Grade:	0
Clask Start (From:	10
Clock Start/From: Clock To: 1st Value: 2nd Value:	6.000
Value Percent: Continuous Index: Within 8" of Joint: Remarks:	NO



Code:	TF
Description:	Tap Factory
Distance (ft):	176.8
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	10
Clock To:	
1st Value:	6.000
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	



Code: Description:	TF Tap Factory
Distance (ft):	250.2
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	9
Clock To:	
1st Value:	6.000
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	



TF
Tap Factory
296.0
0
0
9
6.000
NO



AMH Manhole
398.3
0
0
NO
M-507-036.3
