
| Date: | 04/11/2018 | Weather: | | Coding: | PACP 6.0 |
|-------------------|------------|---------------|--------------------|----------------------------|---------------|
| Pipe Length (ft): | 246.6 | Owner: | NA | Pre Clean: | Not Known |
| P.O.#: | | Surveyor: | Jen Costello | PSR: | P-603-003-002 |
| Customer: | | Clean Date: | 01/01/1900 | Shape: | С |
| Street: | W 40th ave | | Flow Control: | Not Controlled | |
| City: | Hobart, IN | | Year Renewed: | | |
| Location: | Other | | Tape/Media #: | | |
| Purpose: | Not Known | | Dia/Height: | 10" | |
| Use: | Sanitary | | Material: | VCP | |
| Drain Area: | NA | | Lining: | | |
| Category: | NA | | | | |
| Comment: | | | | | |
| Location Details: | | | Direction of Surve | ey: Downstream | |
| US MH: | A-603-002 | DS MH: | M-603-003 | Total Length Surveyed (ft) | 2.3 |
| D&M Index: | 4.00 | O&M Quick: | 4100 | O&M Rating: | 4.00 |
| Structural Index: | 0.00 | Structural Qu | uick. 0000 | | 0.00 |
| Overall Index: | 4.00 | Overall Quicl | 44.00 | | 4.00 |





| Code: Description: | AMH Manhole |
|-----------------------|----------------|
| Distance (ft): | .0 |
| Structural Grade: | 0 |
| | • |
| O&M Grade: | 0 |
| Clock Start/From: | |
| Clock To: | |
| 1st Value: | |
| 2nd Value: | |
| Value Percent: | |
| Continuous Index: | |
| Within 8" of Joint: | NO |
| Remarks: | M-603-002 |

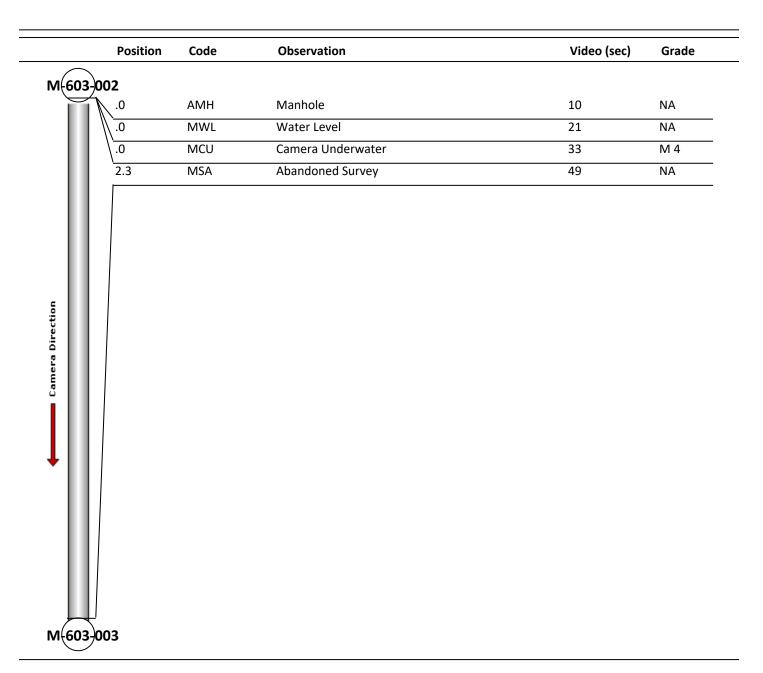

Code: Description:

Distance (ft): .0 Structural Grade: 0 O&M Grade: 0 Clock Start/From: Clock To: 1st Value: 2nd Value: Value Percent: 70.000 Continuous Index: Within 8" of Joint: NO Remarks:

MWL

Water Level



| Code: | MCU |
|--------------|-------------------|
| Description: | Camera Underwater |

| Distance (ft): | .0 |
|---------------------|----|
| Structural Grade: | 0 |
| O&M Grade: | 4 |
| Clock Start/From: | |
| Clock To: | |
| 1st Value: | |
| 2nd Value: | |
| Value Percent: | |
| Continuous Index: | |
| Within 8" of Joint: | NO |
| Remarks: | |



Code: MSA Description: Aban

MSA Abandoned Survey

| Distance (ft): | 2.3 |
|---------------------|-----|
| Structural Grade: | 0 |
| O&M Grade: | 0 |
| Clock Start/From: | |
| Clock To: | |
| 1st Value: | |
| 2nd Value: | |
| Value Percent: | |
| Continuous Index: | |
| Within 8" of Joint: | NO |
| Remarks: | mcu |
