

Date:	04/11/2018	Weather:		Coding:	PACP 6.0
Pipe Length (ft):	176.3	Owner:	NA	Pre Clean:	Not Known
P.O.#:		Surveyor:	Jen Costello	PSR:	P-603-027-026
Customer:		Clean Date:	01/01/1900	Shape:	С
Street:	W 40th ave		Flow Control:	Not Controlled	
City:	Hobart, IN		Year Renewed:		
Location:	Other		Tape/Media #:		
Purpose:	Not Known		Dia/Height:	8"	
Use:	Sanitary		Material:	VCP	
Drain Area:	NA		Lining:		
Category:	NA				
Comment:					
Location Details	:		Direction of Surve	y: Upstream	
US MH:	M-603-026	DS MH:	M-603-027	Total Length Surveyed (ft)	: 65.5
D&M Index:	2.00	O&M Quick:	2100	O&M Rating:	2.00
Structural Index:	0.00	Structural Qu	uick: 0000		0.00
Overall Index:	2.00	Overall Quic			2.00



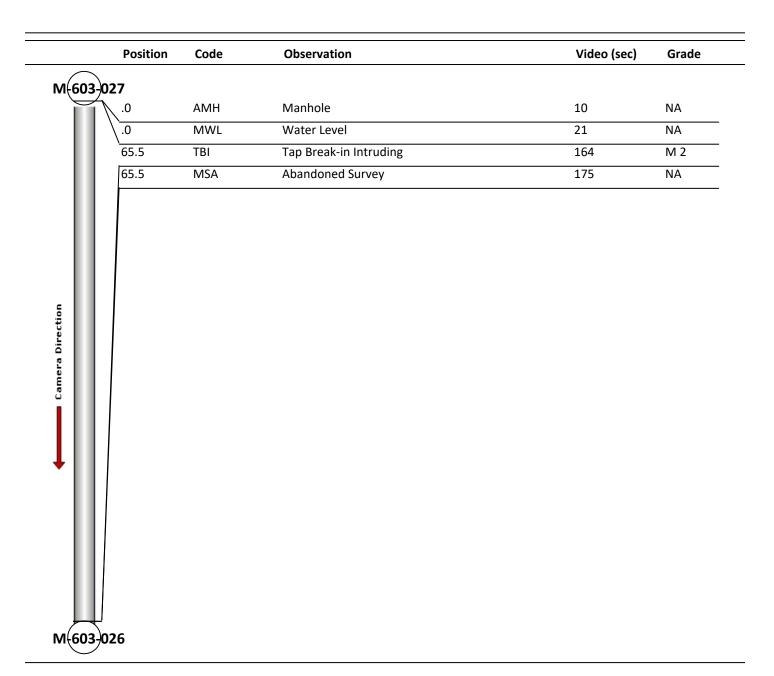


Code:	АМН
Description:	Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-603-026




Code: MWL Description: Water Level

.0
0
0
40.000
NO



Code: Description:	TBI Tap Break-in Intruding
Distance (ft):	65.5
Structural Grade:	0
O&M Grade:	2
Clock Start/From:	12
Clock To:	
1st Value:	4.000
2nd Value:	2.000
Value Percent:	
Continuous Index:	
Within 8" of Joint:	
Remarks:	



Code:MSADescription:Abandoned Survey

Distance (ft):	65.5
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	TBI
