
Profile/Ph	noto Observation	Report				RedZo
Date:	04/23/2018	Weather:			Coding:	PACP 6.0
Pipe Length (ft	t): 180.4	Owner:	NA		Pre Clean:	Not Known
P.O.#:		Surveyor:	Jen Costelle	D	PSR:	P-604-002-001
Customer:		Clean Date:	01/01/190	D	Shape:	с
Street:	W Cleveland Ave.		Flow Control	:	Not Controlled	
City:	Hobart, IN		Year Renewe	ed:		
Location:	Other		Tape/Media	#:		
Purpose:	Not Known		Dia/Height:		10"	
Use:	Sanitary		Material:		СР	
Drain Area:	NA		Lining:			
Category:	NA					
Comment:						
Location Detai	ils:		Direction of S	Survey:	Upstream	
US MH:	M-604-002	DS MH:	M-604-001	Тс	otal Length Surveyed (ft):	6.2
D&M Index:	0.00	O&M Quick:		0000	O&M Rating:	0.00
Structural Index	3.00	Structural Qu	uick:	3100	Structural Rating:	3.00
Overall Index:	3.00	Overall Quicl		3100	Overall Rating:	3.00





Code: Description:	AMH Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-604-001

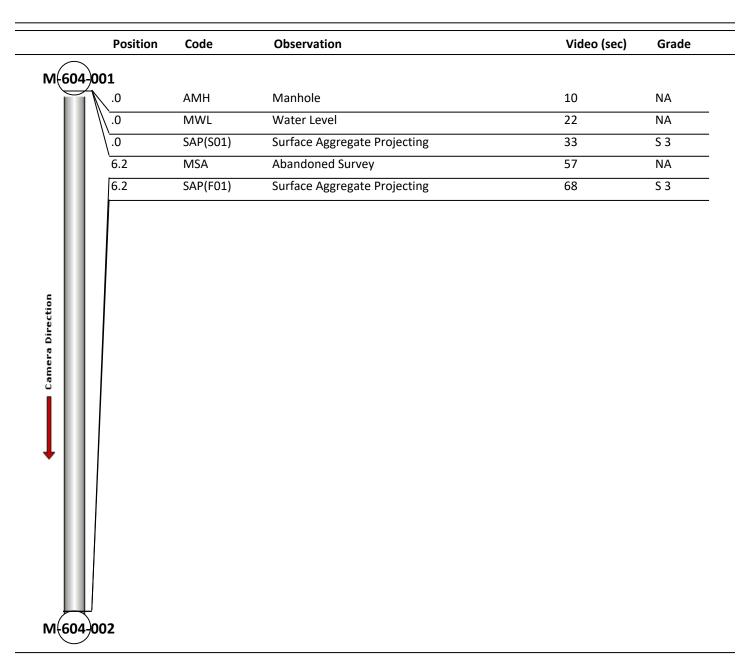

Code: MWL Description: Water Level

.0
0
0
30.000
NO



Code:	SAP
Description:	Surface Aggregate Projecting
Distance (ft):	.0

Distance (ft):	.0
Structural Grade:	3
O&M Grade:	0
Clock Start/From:	8
Clock To:	4
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	S01
Within 8" of Joint:	
Remarks:	



Code: Description:	MSA Abandoned Survey
Distance (ft):	6.2
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	debris under water

SAP

Surface Aggregate Projecting



Distance (ft):	6.2
Structural Grade:	3
O&M Grade:	0
Clock Start/From:	8
Clock To:	4
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	F01
Within 8" of Joint:	
Remarks:	

Code:

Description:
