
Date:	04/23/2018	Weather:			Coding:	PACP 6.0
Pipe Length (ft)	: 297.6	Owner:	NA		Pre Clean:	Not Known
P.O.#:		Surveyor:	Jen Costello		PSR:	P-604-007-006
Customer:		Clean Date:	01/01/1900		Shape:	С
Street:	Beverly Blvd.	Flow Control:		Not Controlled		
City:	Hobart, IN		Year Renewed:			
Location:	Other		Tape/Media #:			
Purpose:	Not Known		Dia/Height:		10"	
Use:	Sanitary		Material:		СР	
Drain Area:	NA		Lining:			
Category:	NA					
Comment:						
Location Details	5:		Direction of Sur	vey:	Downstream	
US MH:	M-604-006	DS MH:	M-604-007	Total Le	ngth Surveyed (ft)	3.5
0&M Index:	0.00	O&M Quick:	00	00	O&M Rating:	0.00
tructural Index: 3.00		Structural Qu	iick: 310		Structural Rating:	3.00
Verall Index: 3.00		Overall Quick	24		Overall Rating:	3.00





Code: Description:	AMH Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-604-006

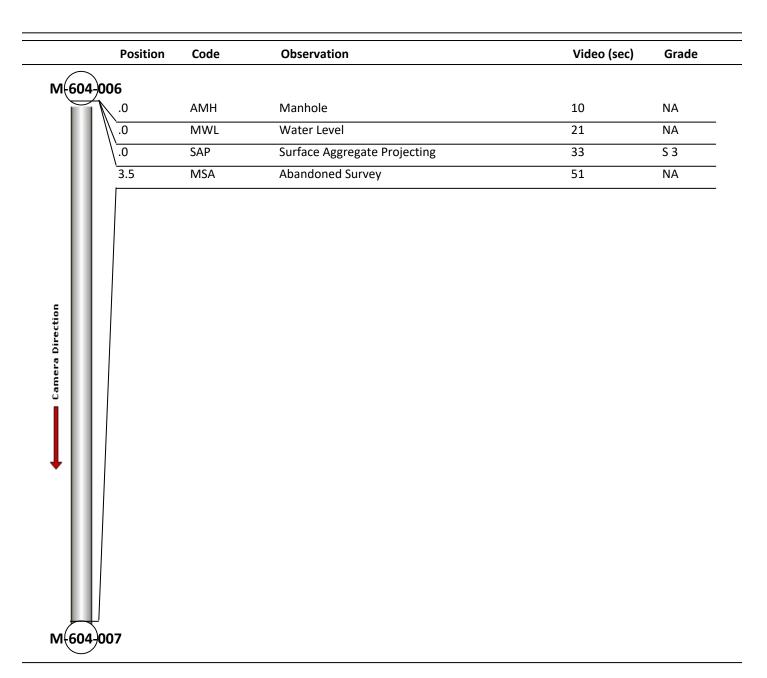

Code: MWL Description: Water Level

Distance (ft): .0 Structural Grade: 0 O&M Grade: 0 Clock Start/From: Clock To: 1st Value: 2nd Value: Value Percent: 40.000 Continuous Index: Within 8" of Joint: NO Remarks:



Code:	SAP
Description:	Surface Aggregate Projecting

Distance (ft):	.0
Structural Grade:	3
O&M Grade:	0
Clock Start/From:	8
Clock To:	4
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	
Remarks:	



Code:MSADescription:Abandoned Survey

Distance (ft):	3.5
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	debris under water

Tuesday, December 8, 2020
