
Date:	04/25/2018	Weather:		Co	ding: P	PACP 6.0
Pipe Length (ft):	215.7	Owner:	NA		-	Not Known
P.O.#:		Surveyor:	Jen Costello	PSF	R: P	P-604-073-072
Customer:		Clean Date:	01/01/1900	Sha	ape: C	2
Street:	Summerlin		Flow Control:	Not	t Controlled	
City:	Hobart, IN		Year Renewed:			
Location:	Light Highway		Tape/Media #:			
Purpose:	Not Known		Dia/Height:	12"	I	
Use:	Sanitary		Material:	VCI	P	
Drain Area:	NA		Lining:			
Category:	NA					
Comment:						
Location Details:			Direction of Su	rvey: Dov	wnstream	
US MH: N	M-604-073	DS MH:	M-604-072	Total Length S	urveyed (ft):	4.4
D&M Index:	3.00	O&M Quick:	31	00 _{O&M}	Rating:	3.00
Structural Index:	0.00	Structural Qu	uck: 00	~~	ural Rating:	0.00
Overall Index:	3.00	Overall Quicl	24	<u></u>	Il Rating:	3.00






Code: Description:	AMH Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-604-073

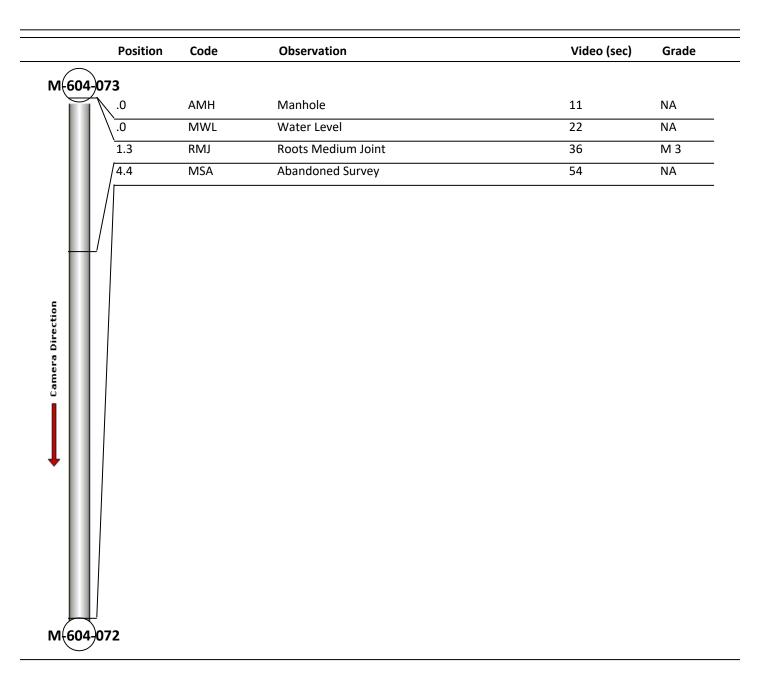


Code: MWL Description: Water Level

Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	30.000
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	



Code:	RMJ
Description:	Roots Medium Joint

Distance (ft):	1.3
Structural Grade:	0
O&M Grade:	3
Clock Start/From:	8
Clock To:	4
1st Value:	
2nd Value:	
Value Percent:	5.000
Continuous Index:	
Within 8" of Joint:	YES
Remarks:	



Code:MSADescription:Abandoned Survey

Distance (ft): 4.4 Structural Grade: 0 O&M Grade: 0 Clock Start/From: Clock To: 1st Value: 2nd Value: Value Percent: Continuous Index: Within 8" of Joint: NO Remarks: roots
