

# Profile/Photo Observation Report



Date:	11/20/2021	Weather:		Coding:	PACP 7.0
Pipe Length (ft):	166.7	Owner:	City of Hobart	Pre Clean:	Heavy Cleaning
P.O.#:	YES502259	Surveyor:	S. Bucklin	PSR:	P-604-096-095
Customer:	City of Hobart	Clean Date:	11/20/2021	Shape:	C


Street:	North Pennsylvania Street	Flow Control:	Not Controlled
City:	Hobart, IN	Year Renewed:	
Location:	Local rural streets with light traffic, t	Tape/Media #:	
Purpose:	Routine Assessment	Dia/Height:	12"
Use:	Sanitary Sewage Pipe	Material:	VCP
Drain Area:		Lining:	None
Category:	NA		
Comment:			
Location Details:		Direction of Survey:	Downstream
US MH:	M-604-095	DS MH:	M-604-096
		Total Length Surveyed (ft):	166.7

O&M Index:	1.83	O&M Quick:	4135	O&M Rating:	84.00
Structural Index:	3.29	Structural Quick:	514B	Structural Rating:	102.00
Overall Index:	2.42	Overall Quick:	514B	Overall Rating:	186.00

Position	Code	Observation	Video (sec)	Grade
.0	AMH	Manhole	1	NA
.0	MWL	Miscellaneous Water Level	60	NA
4.8	MMC	Miscellaneous Material Change	117	NA
4.8	HSV	Hole Soil Visible	167	S 5
6.3	TFA	Tap Factory Activity	197	NA
13.6	MMC	Miscellaneous Material Change	265	NA
13.6	FM(S02)	Fracture Multiple	285	S 4
13.6	B	Broken	307	S 4
19.3	DAE	Deposits Attached Encrustation	361	M 2
22.2	SSS	Surface Damage Surface Spalling	402	S 2
29.6	DAE	Deposits Attached Encrustation	479	M 2
31.7	DAE	Deposits Attached Encrustation	520	M 2
33.8	RFJ(S03)	Roots Fine Joint	579	M 1
46.0	RMJ	Roots Medium Joint	687	M 3
50.2	RMB	Roots Medium Barrel	757	M 4
52.3	RMJ	Roots Medium Joint	805	M 3
55.2	RML	Roots Medium Lateral	854	M 3
55.4	TFD	Tap Factory Defective	881	M 3
56.5	RMJ	Roots Medium Joint	906	M 3


65.0	DAE	Deposits Attached Encrustation	976	M 2
65.0	RFJ(F03)	Roots Fine Joint	988	M 1
66.8	MMC	Miscellaneous Material Change	1028	NA
66.9	FM(F02)	Fracture Multiple	1045	S 4
69.7	TF	Tap Factory	1068	NA
71.5	DSF(S04)	Deposits Settled Fine	1092	M 2
79.4	MMC	Miscellaneous Material Change	1147	NA
81.2	RFJ	Roots Fine Joint	1183	M 1
84.0	MWLS(S05)	Miscellaneous Water Level Sag	1213	S 2
85.2	RFJ	Roots Fine Joint	1237	M 1
85.2	CS	Crack Spiral	1255	S 2
87.2	MMC	Miscellaneous Material Change	1301	NA
94.7	TF	Tap Factory	1345	NA
110.2	MMC	Miscellaneous Material Change	1419	NA
122.5	RFJ	Roots Fine Joint	1479	M 1
122.5	FM(S06)	Fracture Multiple	1525	S 4
127.8	MWLS(F05)	Miscellaneous Water Level Sag	1566	S 2
136.9	DAE	Deposits Attached Encrustation	1642	M 2
138.9	RFJ	Roots Fine Joint	1691	M 1
145.1	RFJ	Roots Fine Joint	1754	M 1
149.3	RFJ	Roots Fine Joint	1800	M 1
151.4	MMC	Miscellaneous Material Change	1848	NA
151.5	FM(F06)	Fracture Multiple	1862	S 4
156.3	TF	Tap Factory	1892	NA
157.8	MMC	Miscellaneous Material Change	1937	NA
159.6	RFJ	Roots Fine Joint	1990	M 1
159.6	CM	Crack Multiple	2023	S 3
161.6	RFJ	Roots Fine Joint	2058	M 1
161.6	DAE	Deposits Attached Encrustation	2066	M 2
163.8	RFJ	Roots Fine Joint	2112	M 1
165.3	DSF(F04)	Deposits Settled Fine	2135	M 2
166.7	AMH	Manhole	2213	NA

M-604-096

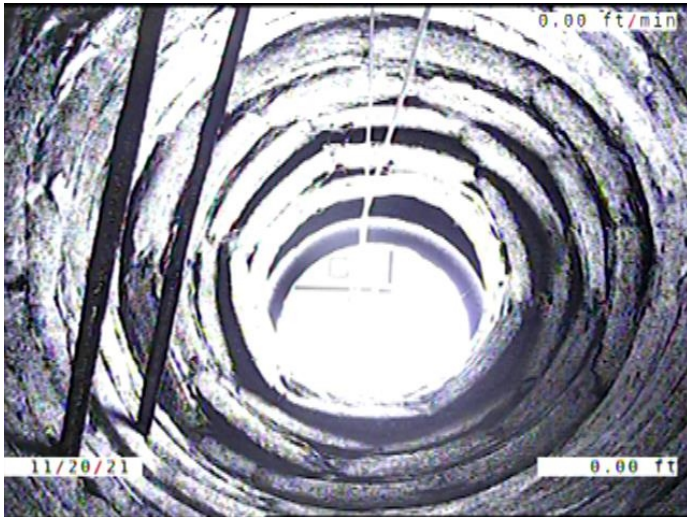


Code: **AMH**  
 Description: **Manhole**

Distance (ft): **.0**  
 Structural Grade: **0**  
 O&M Grade: **0**  
 Clock Start/From:  
 Clock To:  
 1st Value:  
 2nd Value:  
 Value Percent:  
 Continuous Index:  
 Within 8" of Joint: **NO**  
 Remarks: **M-604-095**

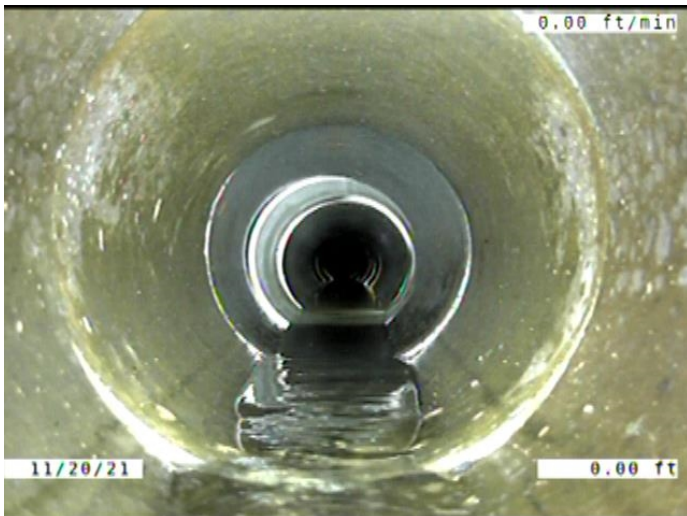


Code: **MWL**  
 Description: **Miscellaneous Water Level**

Distance (ft): **.0**  
 Structural Grade: **0**  
 O&M Grade: **0**  
 Clock Start/From:  
 Clock To:  
 1st Value:  
 2nd Value:  
 Value Percent: **5.000**  
 Continuous Index:  
 Within 8" of Joint: **NO**  
 Remarks:

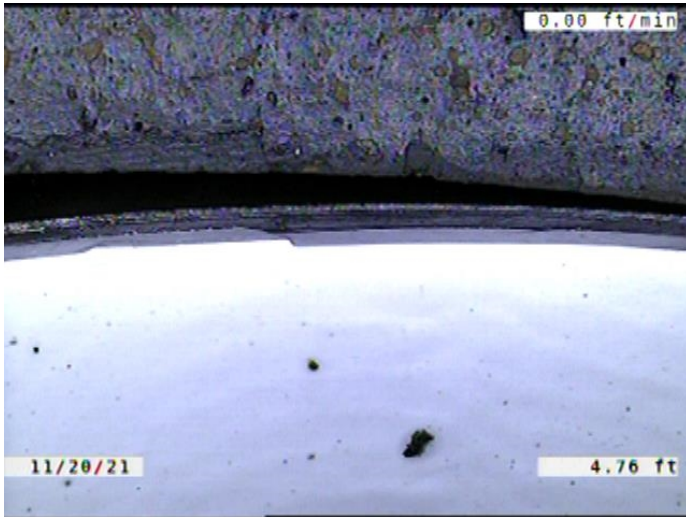

Code: **MMC**  
 Description: **Miscellaneous Material Change**

Distance (ft): **4.8**  
 Structural Grade: **0**  
 O&M Grade: **0**  
 Clock Start/From:  
 Clock To:  
 1st Value:  
 2nd Value:  
 Value Percent:  
 Continuous Index:  
 Within 8" of Joint: **NO**  
 Remarks: **VCP TO PVC**

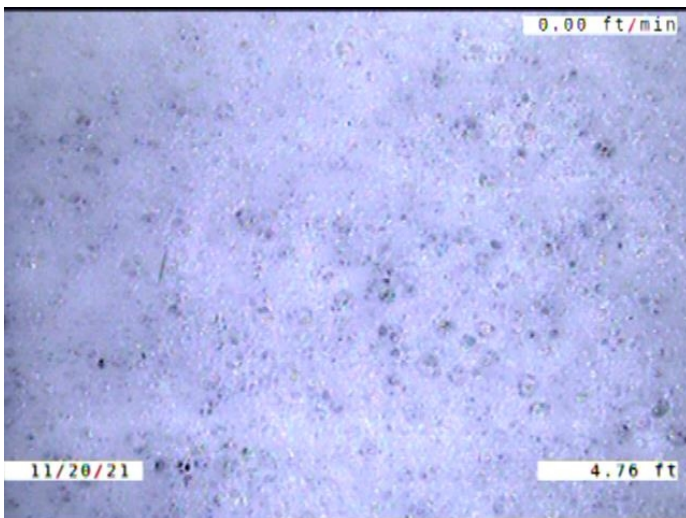

Code: **HSV**  
 Description: **Hole Soil Visible**


Distance (ft): **4.8**  
 Structural Grade: **5**  
 O&M Grade: **0**  
 Clock Start/From: **5**  
 Clock To: **7**  
 1st Value:  
 2nd Value:  
 Value Percent:  
 Continuous Index:  
 Within 8" of Joint: **YES**  
 Remarks: **LOOKS LIKE IT MIGHT STILL HAVE THE FERNCO UNDERNEATH IT.**






Code: **TFA**  
 Description: **Tap Factory Activity**

Distance (ft): **6.3**  
 Structural Grade: **0**  
 O&M Grade: **0**  
 Clock Start/From: **1**  
 Clock To:  
 1st Value: **4.000**  
 2nd Value:  
 Value Percent:  
 Continuous Index:  
 Within 8" of Joint: **YES**  
 Remarks:

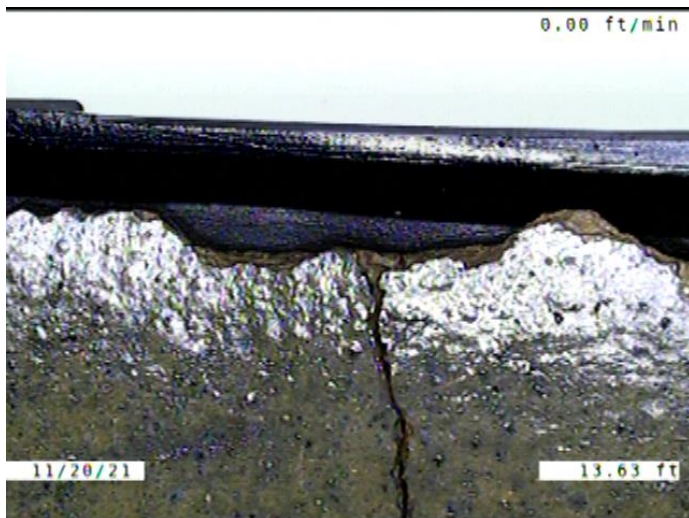

Code: **MMC**  
 Description: **Miscellaneous Material Change**

Distance (ft): **13.6**  
 Structural Grade: **0**  
 O&M Grade: **0**  
 Clock Start/From:  
 Clock To:  
 1st Value:  
 2nd Value:  
 Value Percent:  
 Continuous Index:  
 Within 8" of Joint: **NO**  
 Remarks: **PVC TO VCP**

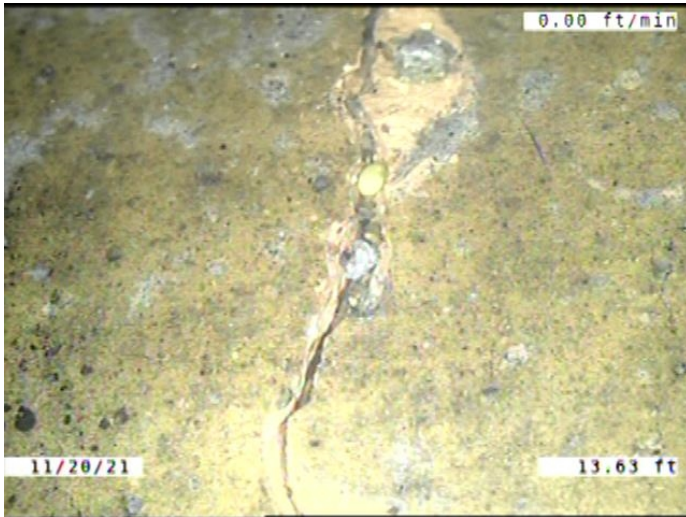

Code: **FM**  
 Description: **Fracture Multiple**

Distance (ft): **13.6**  
 Structural Grade: **4**  
 O&M Grade: **0**  
 Clock Start/From: **12**  
 Clock To: **12**  
 1st Value:  
 2nd Value:  
 Value Percent:  
 Continuous Index: **S02**  
 Within 8" of Joint: **YES**  
 Remarks:


---



Code: **B**  
 Description: **Broken**


Distance (ft): **13.6**  
 Structural Grade: **4**  
 O&M Grade: **0**  
 Clock Start/From: **9**  
 Clock To:  
 1st Value:  
 2nd Value:  
 Value Percent:  
 Continuous Index:  
 Within 8" of Joint: **YES**  
 Remarks:

---

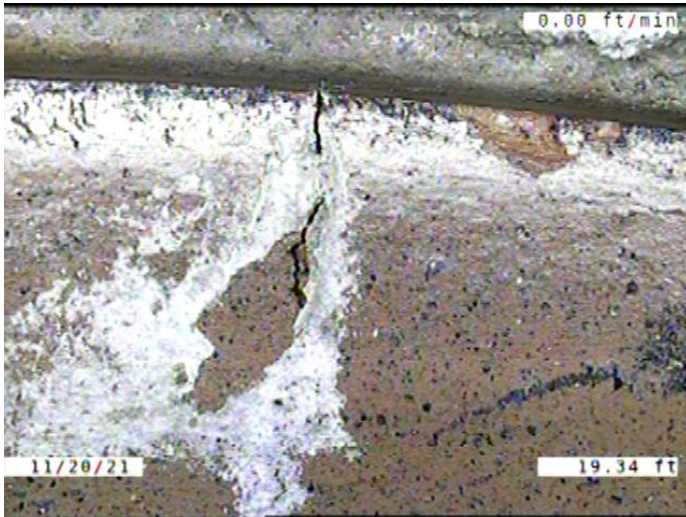

Code: **DAE**  
 Description: **Deposits Attached Encrustation**


Distance (ft): **19.3**  
 Structural Grade: **0**  
 O&M Grade: **2**  
 Clock Start/From: **8**  
 Clock To: **4**  
 1st Value:  
 2nd Value:  
 Value Percent: **5.000**  
 Continuous Index:  
 Within 8" of Joint: **YES**  
 Remarks:

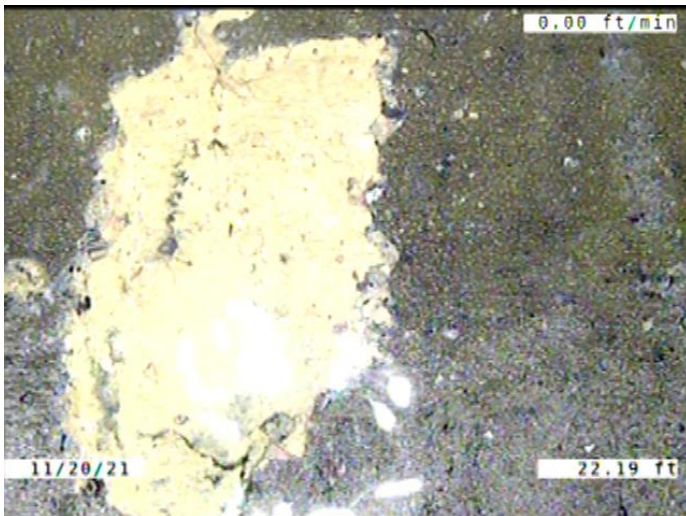

Code: **SSS**  
 Description: **Surface Damage Surface Spalling**


Distance (ft): **22.2**  
 Structural Grade: **2**  
 O&M Grade: **0**  
 Clock Start/From: **6**  
 Clock To:  
 1st Value:  
 2nd Value:  
 Value Percent:  
 Continuous Index:  
 Within 8" of Joint: **YES**  
 Remarks:



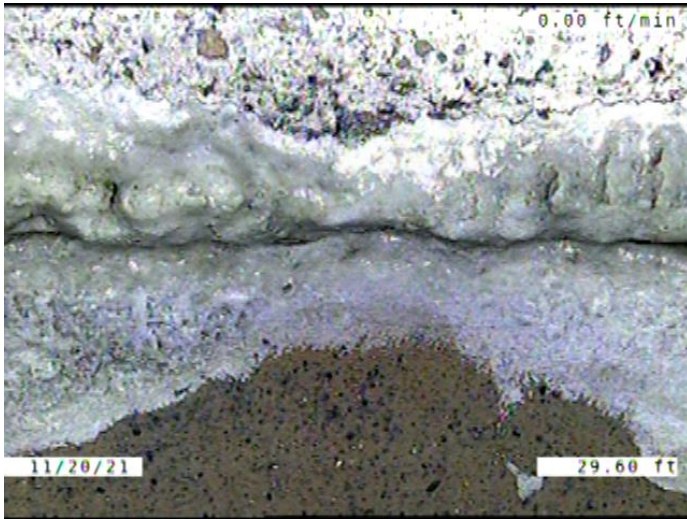

Code: **DAE**  
 Description: **Deposits Attached Encrustation**

Distance (ft): **29.6**  
 Structural Grade: **0**  
 O&M Grade: **2**  
 Clock Start/From: **8**  
 Clock To: **4**  
 1st Value:  
 2nd Value:  
 Value Percent: **5.000**  
 Continuous Index:  
 Within 8" of Joint: **YES**  
 Remarks:

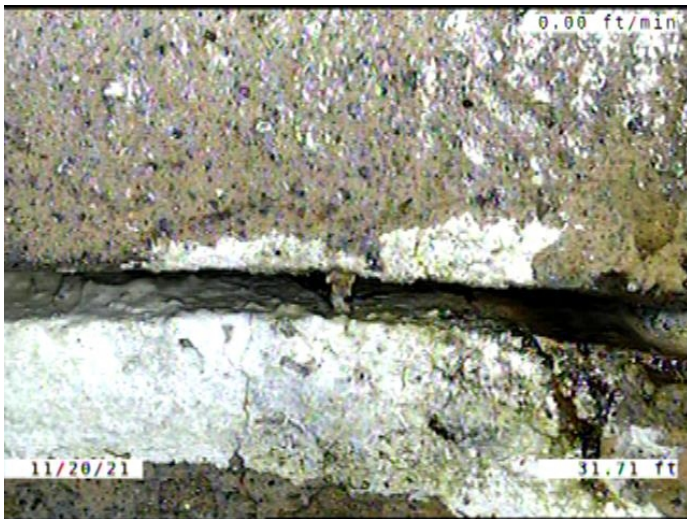


Code: **DAE**  
 Description: **Deposits Attached Encrustation**

Distance (ft): **31.7**  
 Structural Grade: **0**  
 O&M Grade: **2**  
 Clock Start/From: **1**  
 Clock To: **4**  
 1st Value:  
 2nd Value:  
 Value Percent: **5.000**  
 Continuous Index:  
 Within 8" of Joint: **YES**  
 Remarks:



Code: **RFJ**  
 Description: **Roots Fine Joint**


Distance (ft): **33.8**  
 Structural Grade: **0**  
 O&M Grade: **1**  
 Clock Start/From: **9**  
 Clock To: **3**  
 1st Value:  
 2nd Value:  
 Value Percent:  
 Continuous Index: **S03**  
 Within 8" of Joint: **YES**  
 Remarks:

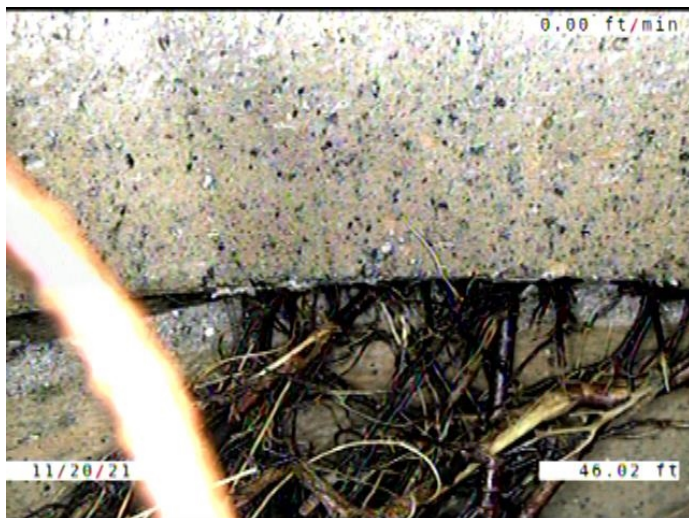

Code: **RMJ**  
 Description: **Roots Medium Joint**


Distance (ft): **46.0**  
 Structural Grade: **0**  
 O&M Grade: **3**  
 Clock Start/From: **10**  
 Clock To: **2**  
 1st Value:  
 2nd Value:  
 Value Percent: **5.000**  
 Continuous Index:  
 Within 8" of Joint: **YES**  
 Remarks:



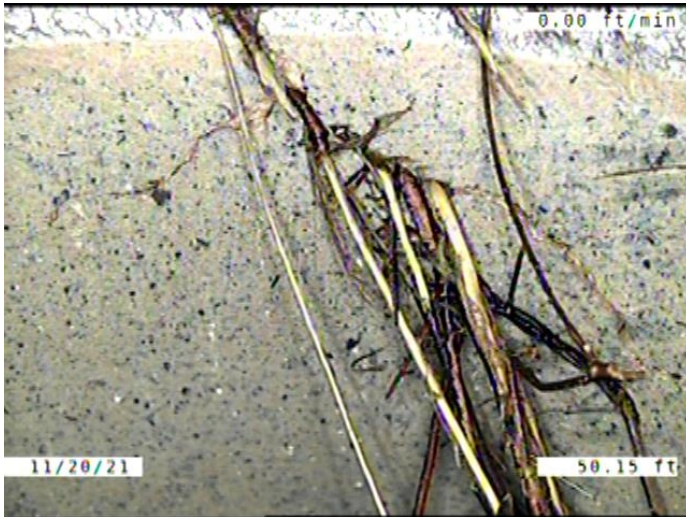


Code: **RMB**  
 Description: **Roots Medium Barrel**

Distance (ft): **50.2**  
 Structural Grade: **0**  
 O&M Grade: **4**  
 Clock Start/From: **8**  
 Clock To: **4**  
 1st Value:  
 2nd Value:  
 Value Percent: **10.000**  
 Continuous Index:  
 Within 8" of Joint: **NO**  
 Remarks:

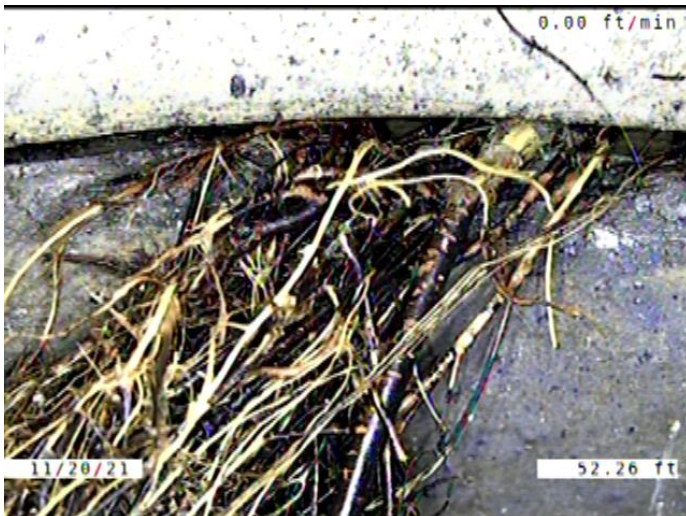


Code: **RMJ**  
 Description: **Roots Medium Joint**

Distance (ft): **52.3**  
 Structural Grade: **0**  
 O&M Grade: **3**  
 Clock Start/From: **8**  
 Clock To: **4**  
 1st Value:  
 2nd Value:  
 Value Percent: **10.000**  
 Continuous Index:  
 Within 8" of Joint: **YES**  
 Remarks:

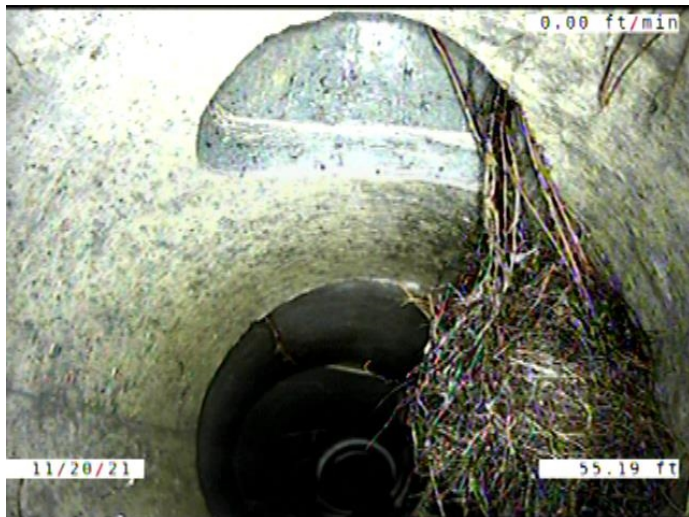

Code: **RML**  
 Description: **Roots Medium Lateral**

Distance (ft): **55.2**  
 Structural Grade: **0**  
 O&M Grade: **3**  
 Clock Start/From: **1**  
 Clock To: **2**  
 1st Value:  
 2nd Value:  
 Value Percent: **15.000**  
 Continuous Index:  
 Within 8" of Joint: **NO**  
 Remarks:

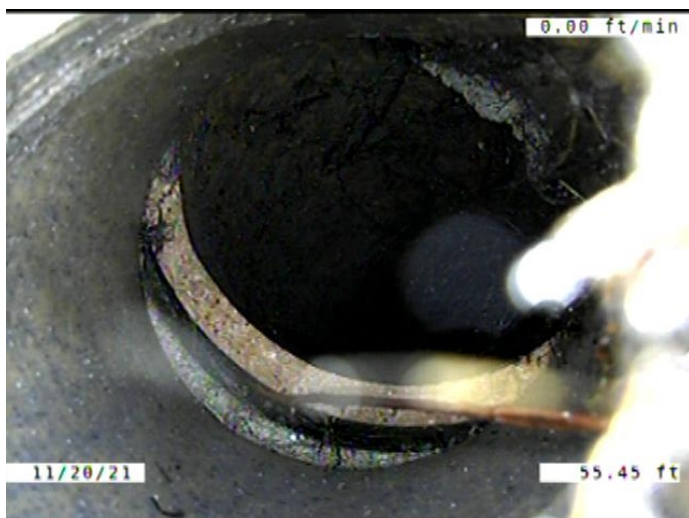


Code: **TFD**  
 Description: **Tap Factory Defective**

Distance (ft): **55.4**  
 Structural Grade: **0**  
 O&M Grade: **3**  
 Clock Start/From: **1**  
 Clock To:  
 1st Value: **4.000**  
 2nd Value:  
 Value Percent:  
 Continuous Index:  
 Within 8" of Joint: **YES**  
 Remarks: **BROKEN. OFFSET. ROOTS GROWING IN THE JOINT AND IN THE TAP INTO**



Code: **RMJ**  
 Description: **Roots Medium Joint**


Distance (ft): **56.5**  
 Structural Grade: **0**  
 O&M Grade: **3**  
 Clock Start/From: **8**  
 Clock To: **4**  
 1st Value:  
 2nd Value:  
 Value Percent: **5.000**  
 Continuous Index:  
 Within 8" of Joint: **YES**  
 Remarks:

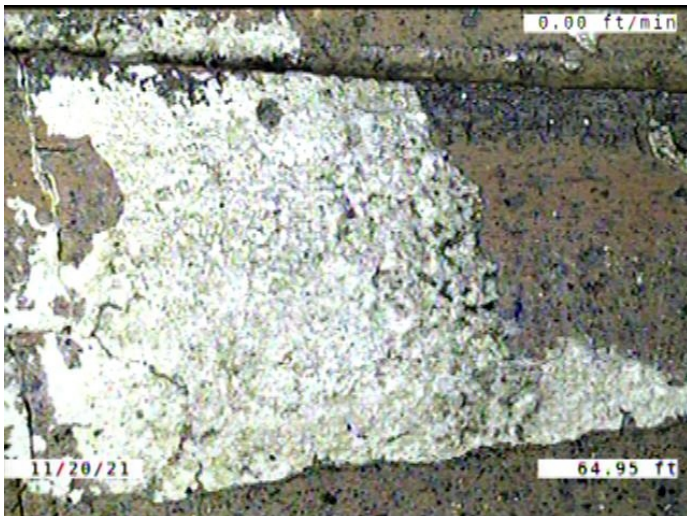

Code: **DAE**  
 Description: **Deposits Attached Encrustation**

Distance (ft): **65.0**  
 Structural Grade: **0**  
 O&M Grade: **2**  
 Clock Start/From: **8**  
 Clock To: **4**  
 1st Value:  
 2nd Value:  
 Value Percent: **5.000**  
 Continuous Index:  
 Within 8" of Joint: **YES**  
 Remarks:




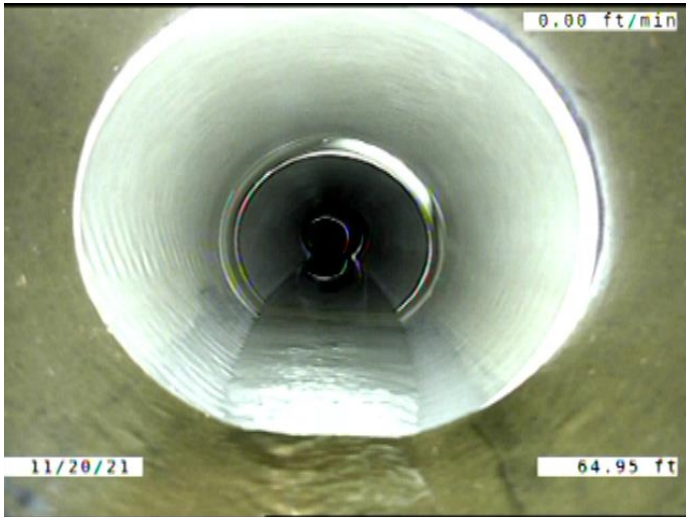

Code: **RFJ**  
Description: **Roots Fine Joint**

Distance (ft): **65.0**  
Structural Grade: **0**  
O&M Grade: **1**  
Clock Start/From: **9**  
Clock To: **3**  
1st Value:  
2nd Value:  
Value Percent:  
Continuous Index: **F03**  
Within 8" of Joint: **YES**  
Remarks:


---

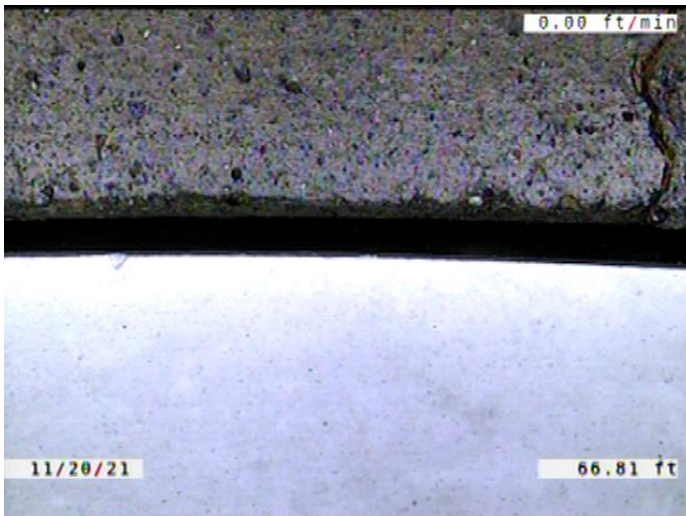

Code: **MMC**  
Description: **Miscellaneous Material Change**


Distance (ft): **66.8**  
Structural Grade: **0**  
O&M Grade: **0**  
Clock Start/From:  
Clock To:  
1st Value:  
2nd Value:  
Value Percent:  
Continuous Index:  
Within 8" of Joint: **NO**  
Remarks: **VCP TO PVC**

---

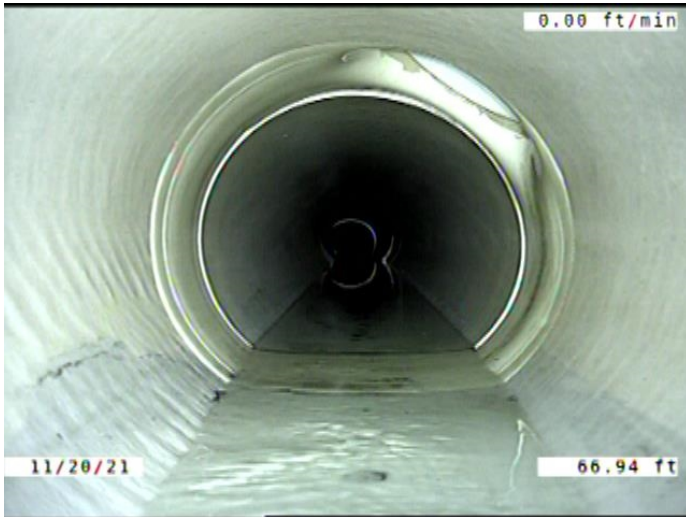

Code: **FM**  
 Description: **Fracture Multiple**

Distance (ft): **66.9**  
 Structural Grade: **4**  
 O&M Grade: **0**  
 Clock Start/From: **12**  
 Clock To: **12**  
 1st Value:  
 2nd Value:  
 Value Percent:  
 Continuous Index: **F02**  
 Within 8" of Joint: **YES**  
 Remarks:

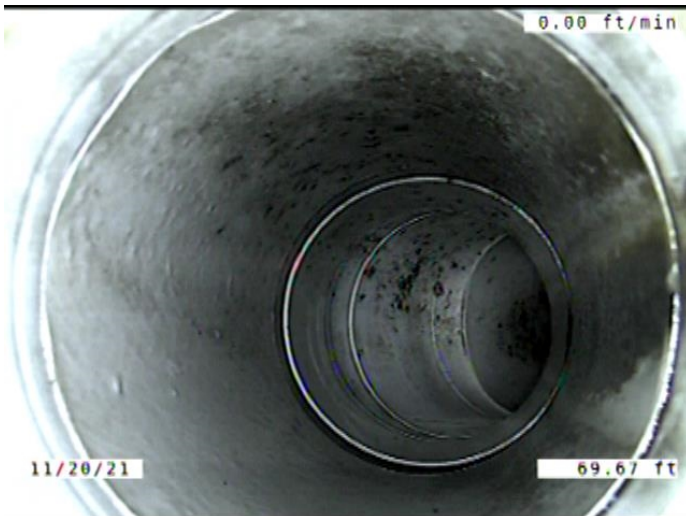

Code: **TF**  
 Description: **Tap Factory**


Distance (ft): **69.7**  
 Structural Grade: **0**  
 O&M Grade: **0**  
 Clock Start/From: **1**  
 Clock To:  
 1st Value: **4.000**  
 2nd Value:  
 Value Percent:  
 Continuous Index:  
 Within 8" of Joint: **YES**  
 Remarks:






Code: **DSF**  
 Description: **Deposits Settled Fine**

Distance (ft): **71.5**  
 Structural Grade: **0**  
 O&M Grade: **2**  
 Clock Start/From: **5**  
 Clock To: **7**  
 1st Value:  
 2nd Value:  
 Value Percent: **5.000**  
 Continuous Index: **S04**  
 Within 8" of Joint: **YES**  
 Remarks:

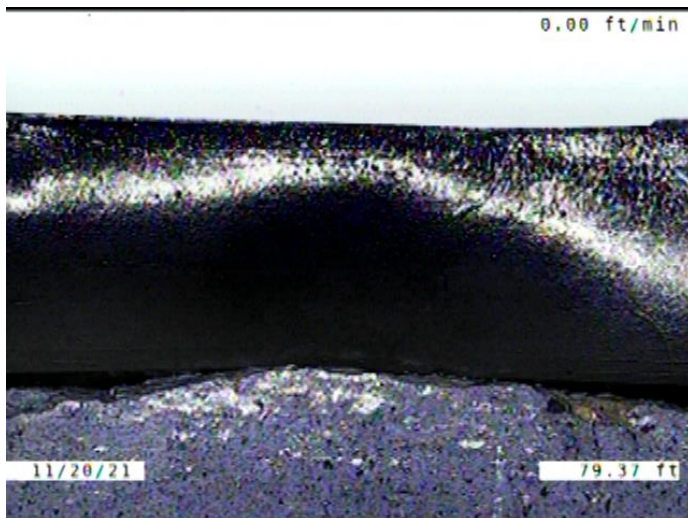


Code: **MMC**  
 Description: **Miscellaneous Material Change**

Distance (ft): **79.4**  
 Structural Grade: **0**  
 O&M Grade: **0**  
 Clock Start/From:  
 Clock To:  
 1st Value:  
 2nd Value:  
 Value Percent:  
 Continuous Index:  
 Within 8" of Joint: **NO**  
 Remarks: **PVC TO VCP**

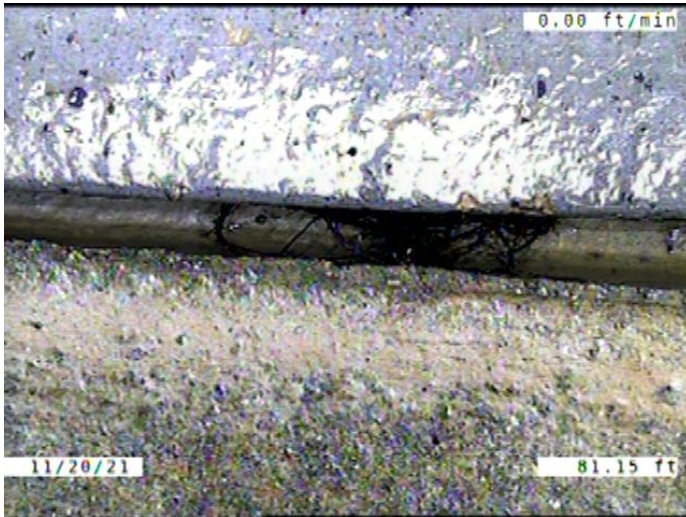


Code: **RFJ**  
 Description: **Roots Fine Joint**

Distance (ft): **81.2**  
 Structural Grade: **0**  
 O&M Grade: **1**  
 Clock Start/From: **10**  
 Clock To: **2**  
 1st Value:  
 2nd Value:  
 Value Percent:  
 Continuous Index:  
 Within 8" of Joint: **YES**  
 Remarks:

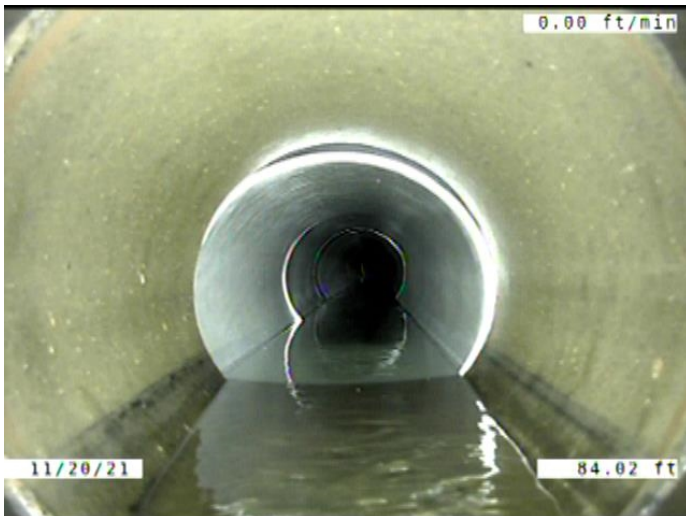


Code: **MWLS**  
 Description: **Miscellaneous Water Level Sag**

Distance (ft): **84.0**  
 Structural Grade: **2**  
 O&M Grade: **0**  
 Clock Start/From:  
 Clock To:  
 1st Value:  
 2nd Value:  
 Value Percent: **5.000**  
 Continuous Index: **S05**  
 Within 8" of Joint: **NO**  
 Remarks:

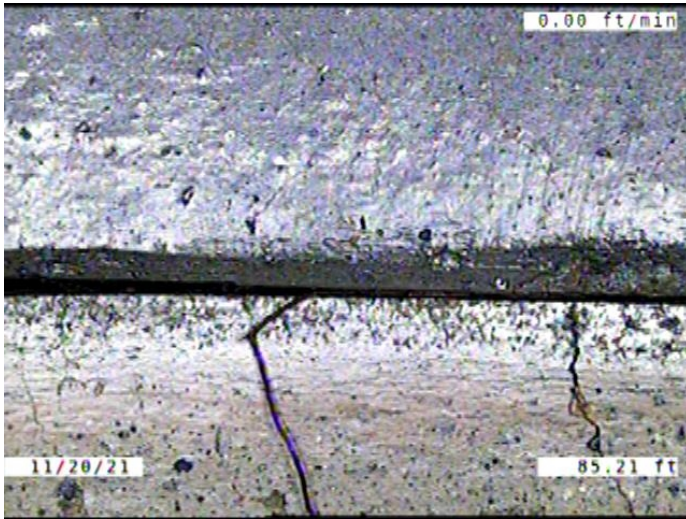

Code: **RFJ**  
 Description: **Roots Fine Joint**

Distance (ft): **85.2**  
 Structural Grade: **0**  
 O&M Grade: **1**  
 Clock Start/From: **12**  
 Clock To:  
 1st Value:  
 2nd Value:  
 Value Percent:  
 Continuous Index:  
 Within 8" of Joint: **YES**  
 Remarks:

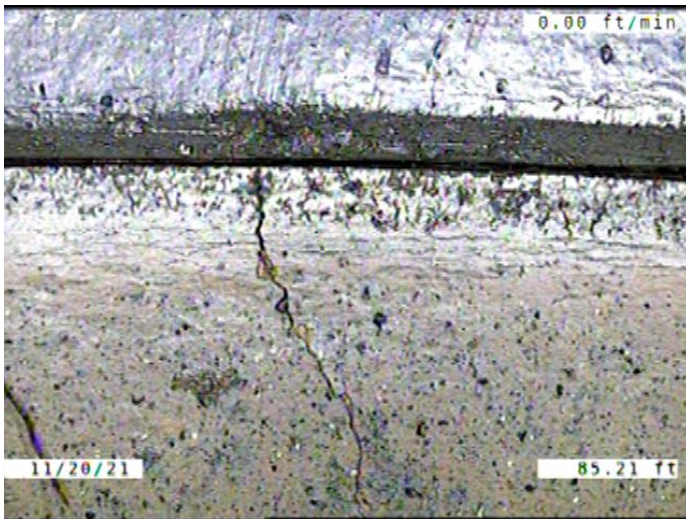

Code: **CS**  
 Description: **Crack Spiral**


Distance (ft): **85.2**  
 Structural Grade: **2**  
 O&M Grade: **0**  
 Clock Start/From: **12**  
 Clock To: **1**  
 1st Value:  
 2nd Value:  
 Value Percent:  
 Continuous Index:  
 Within 8" of Joint: **YES**  
 Remarks:






Code: **MMC**  
 Description: **Miscellaneous Material Change**

Distance (ft): **87.2**  
 Structural Grade: **0**  
 O&M Grade: **0**  
 Clock Start/From:  
 Clock To:  
 1st Value:  
 2nd Value:  
 Value Percent:  
 Continuous Index:  
 Within 8" of Joint: **NO**  
 Remarks: **VCP TO PVC**

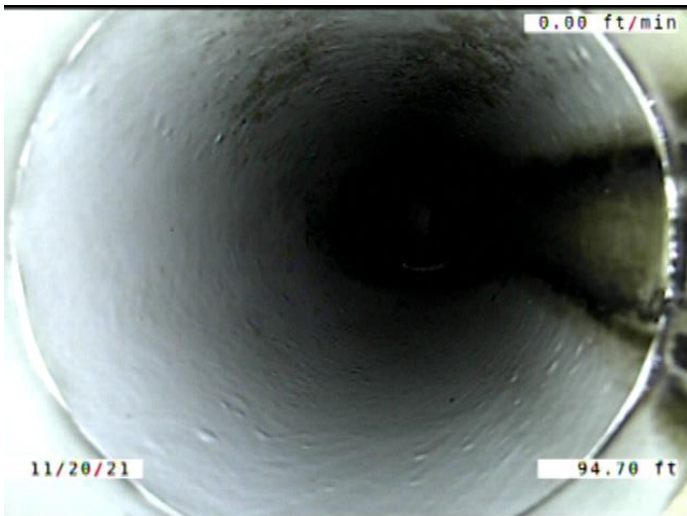


Code: **TF**  
 Description: **Tap Factory**

Distance (ft): **94.7**  
 Structural Grade: **0**  
 O&M Grade: **0**  
 Clock Start/From: **1**  
 Clock To:  
 1st Value: **4.000**  
 2nd Value:  
 Value Percent:  
 Continuous Index:  
 Within 8" of Joint: **YES**  
 Remarks:

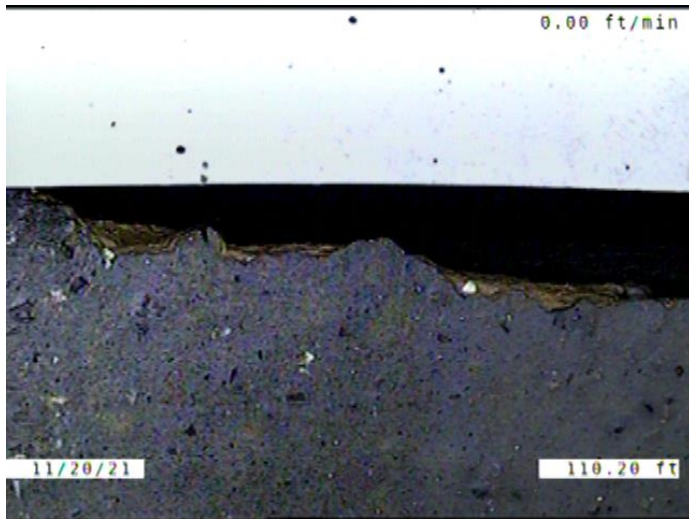

Code: **MMC**  
 Description: **Miscellaneous Material Change**


Distance (ft): **110.2**  
 Structural Grade: **0**  
 O&M Grade: **0**  
 Clock Start/From:  
 Clock To:  
 1st Value:  
 2nd Value:  
 Value Percent:  
 Continuous Index:  
 Within 8" of Joint: **NO**  
 Remarks: **PVC TO VCP**

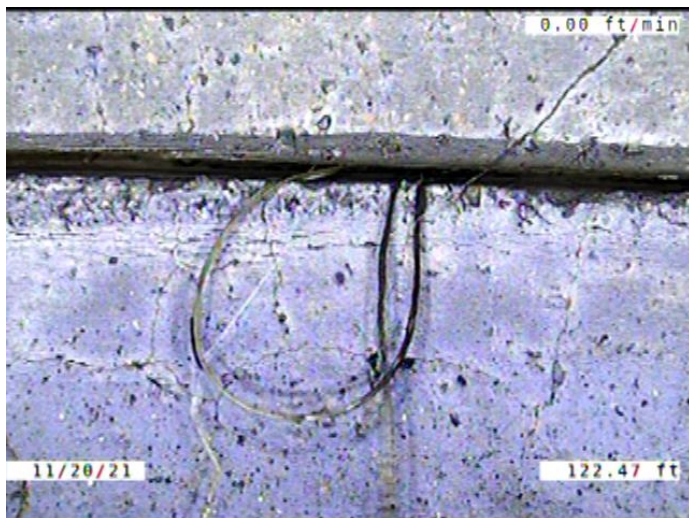

Code: **RFJ**  
 Description: **Roots Fine Joint**

Distance (ft): **122.5**  
 Structural Grade: **0**  
 O&M Grade: **1**  
 Clock Start/From: **12**  
 Clock To: **1**  
 1st Value:  
 2nd Value:  
 Value Percent:  
 Continuous Index:  
 Within 8" of Joint: **YES**  
 Remarks:



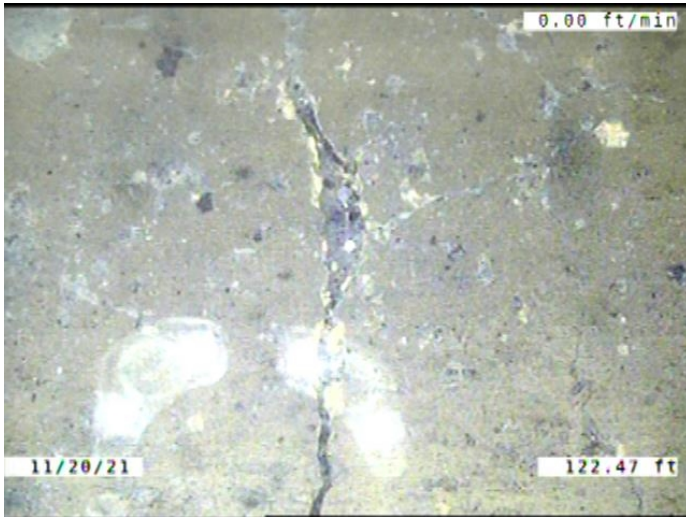

Code: **FM**  
 Description: **Fracture Multiple**

Distance (ft): **122.5**  
 Structural Grade: **4**  
 O&M Grade: **0**  
 Clock Start/From: **12**  
 Clock To: **12**  
 1st Value:  
 2nd Value:  
 Value Percent:  
 Continuous Index: **S06**  
 Within 8" of Joint: **YES**  
 Remarks:


---



Code: **MWLS**  
 Description: **Miscellaneous Water Level Sag**

Distance (ft): **127.8**  
 Structural Grade: **2**  
 O&M Grade: **0**  
 Clock Start/From:  
 Clock To:  
 1st Value:  
 2nd Value:  
 Value Percent: **5.000**  
 Continuous Index: **F05**  
 Within 8" of Joint: **NO**  
 Remarks:


---

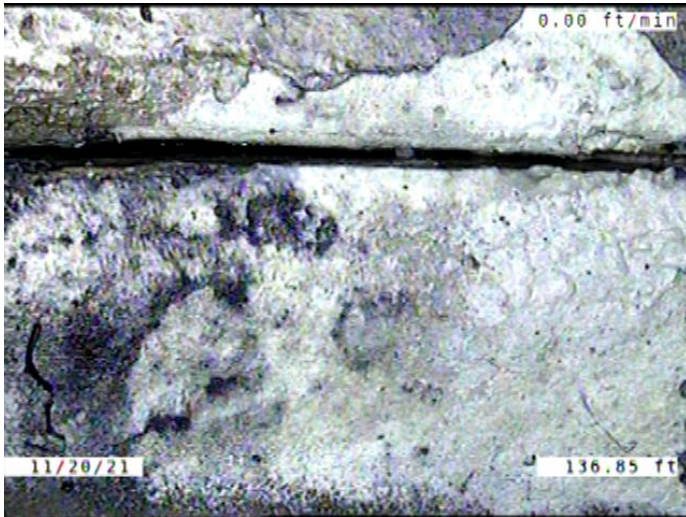

Code: **DAE**  
 Description: **Deposits Attached Encrustation**

Distance (ft): **136.9**  
 Structural Grade: **0**  
 O&M Grade: **2**  
 Clock Start/From: **8**  
 Clock To: **11**  
 1st Value:  
 2nd Value:  
 Value Percent: **5.000**  
 Continuous Index:  
 Within 8" of Joint: **YES**  
 Remarks:


---

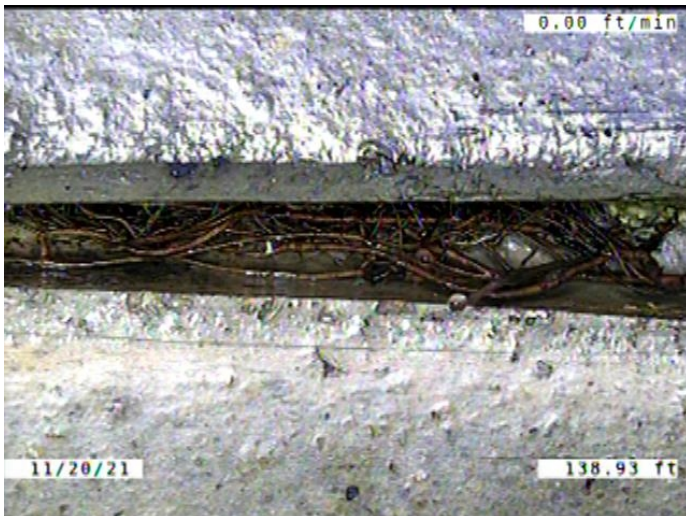

Code: **RFJ**  
 Description: **Roots Fine Joint**


Distance (ft): **138.9**  
 Structural Grade: **0**  
 O&M Grade: **1**  
 Clock Start/From: **9**  
 Clock To: **11**  
 1st Value:  
 2nd Value:  
 Value Percent:  
 Continuous Index:  
 Within 8" of Joint: **YES**  
 Remarks:

---

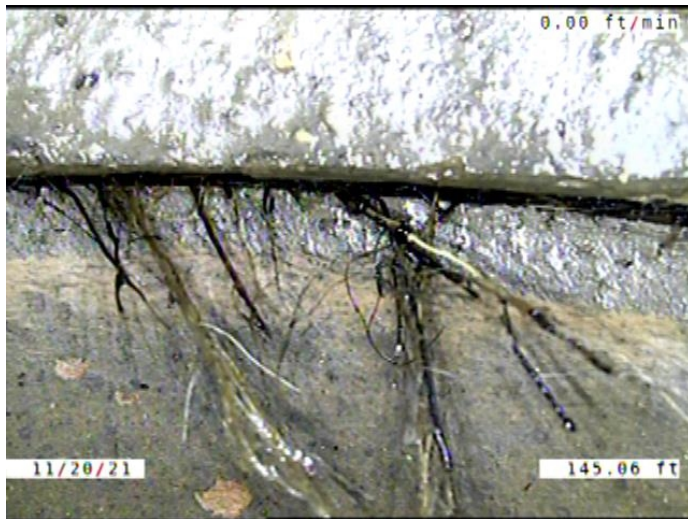

Code: **RFJ**  
 Description: **Roots Fine Joint**


Distance (ft): **145.1**  
 Structural Grade: **0**  
 O&M Grade: **1**  
 Clock Start/From: **9**  
 Clock To: **3**  
 1st Value:  
 2nd Value:  
 Value Percent:  
 Continuous Index:  
 Within 8" of Joint: **YES**  
 Remarks:

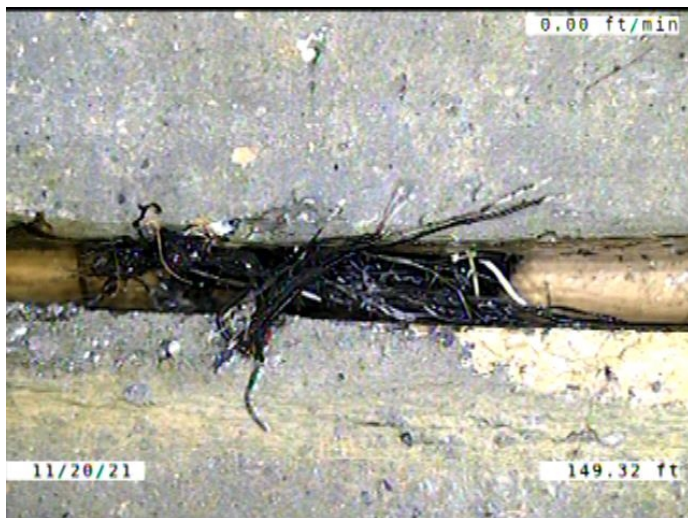


Code: **RFJ**  
 Description: **Roots Fine Joint**

Distance (ft): **149.3**  
 Structural Grade: **0**  
 O&M Grade: **1**  
 Clock Start/From: **9**  
 Clock To: **3**  
 1st Value:  
 2nd Value:  
 Value Percent:  
 Continuous Index:  
 Within 8" of Joint: **YES**  
 Remarks:




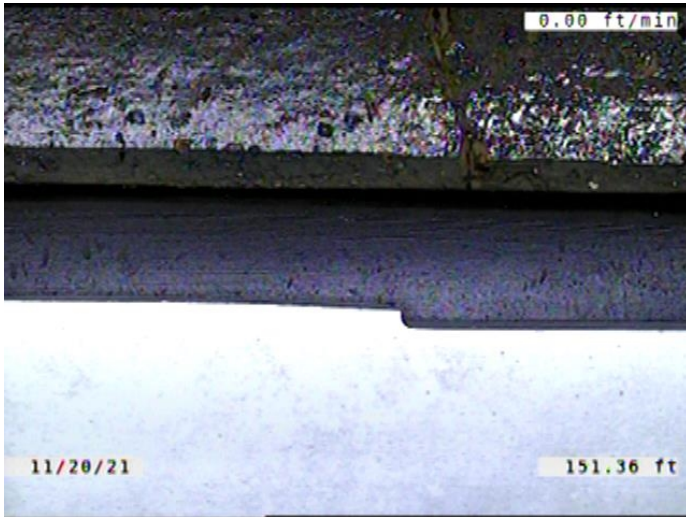

Code:	<b>MMC</b>
Description:	<b>Miscellaneous Material Change</b>
Distance (ft):	<b>151.4</b>
Structural Grade:	<b>0</b>
O&M Grade:	<b>0</b>
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	<b>NO</b>
Remarks:	<b>VCP TO PVC</b>

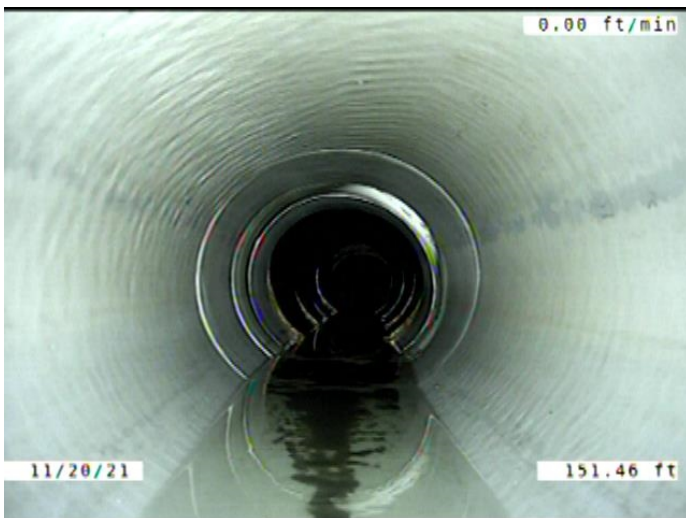


Code:	<b>FM</b>
Description:	<b>Fracture Multiple</b>
Distance (ft):	<b>151.5</b>
Structural Grade:	<b>4</b>
O&M Grade:	<b>0</b>
Clock Start/From:	<b>12</b>
Clock To:	<b>12</b>
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	<b>F06</b>
Within 8" of Joint:	<b>YES</b>
Remarks:	

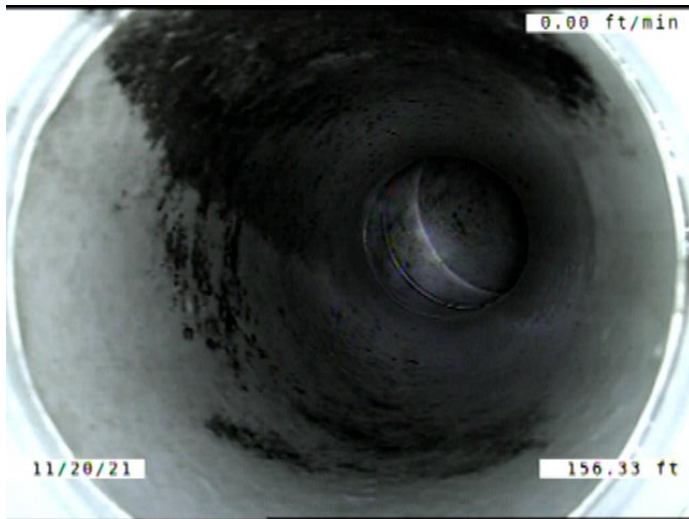

Code: **TF**  
Description: **Tap Factory**


Distance (ft): **156.3**  
Structural Grade: **0**  
O&M Grade: **0**  
Clock Start/From: **1**  
Clock To:  
1st Value: **4.000**  
2nd Value:  
Value Percent:  
Continuous Index:  
Within 8" of Joint: **YES**  
Remarks:

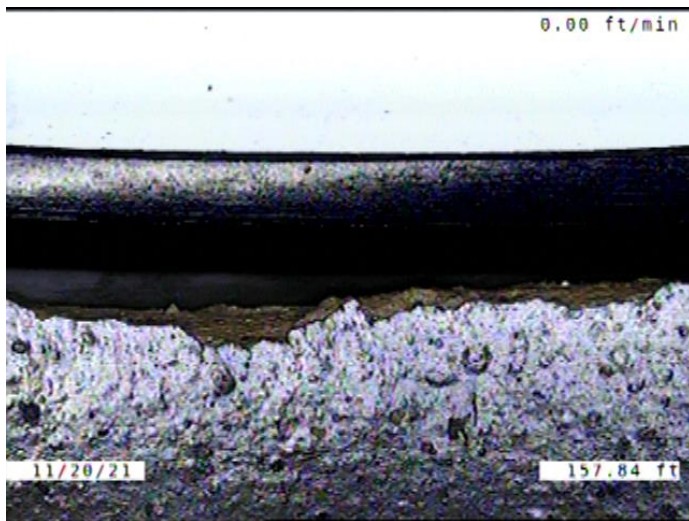

Code: **MMC**  
Description: **Miscellaneous Material Change**

Distance (ft): **157.8**  
Structural Grade: **0**  
O&M Grade: **0**  
Clock Start/From:  
Clock To:  
1st Value:  
2nd Value:  
Value Percent:  
Continuous Index:  
Within 8" of Joint: **NO**  
Remarks: **PVC TO VCP**




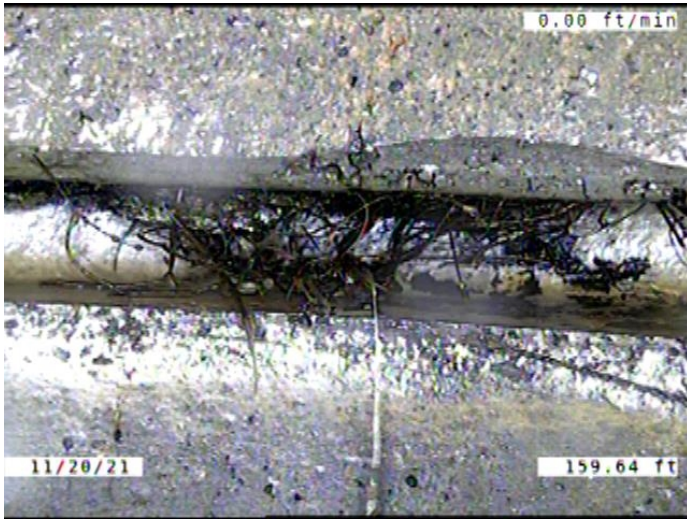

Code: **RFJ**  
Description: **Roots Fine Joint**

Distance (ft): **159.6**  
Structural Grade: **0**  
O&M Grade: **1**  
Clock Start/From: **9**  
Clock To: **3**  
1st Value:  
2nd Value:  
Value Percent:  
Continuous Index:  
Within 8" of Joint: **YES**  
Remarks:


---

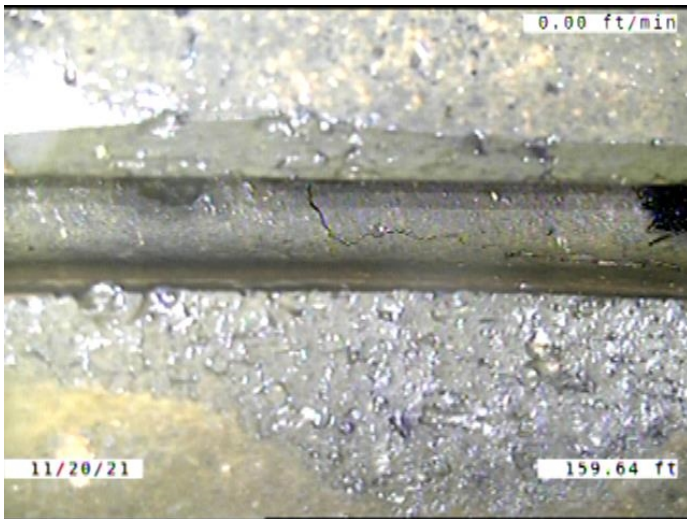

Code: **CM**  
Description: **Crack Multiple**


Distance (ft): **159.6**  
Structural Grade: **3**  
O&M Grade: **0**  
Clock Start/From: **9**  
Clock To: **3**  
1st Value:  
2nd Value:  
Value Percent:  
Continuous Index:  
Within 8" of Joint: **YES**  
Remarks:

---

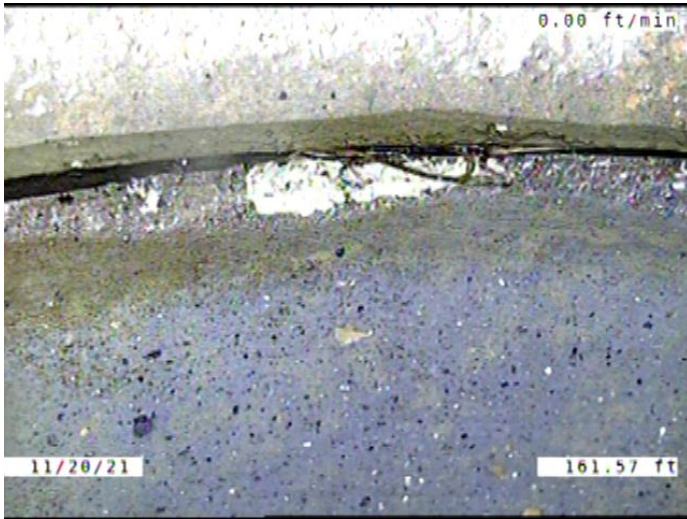


Code: **RFJ**  
Description: **Roots Fine Joint**

Distance (ft): **161.6**  
Structural Grade: **0**  
O&M Grade: **1**  
Clock Start/From: **10**  
Clock To:  
1st Value:  
2nd Value:  
Value Percent:  
Continuous Index:  
Within 8" of Joint: **YES**  
Remarks:

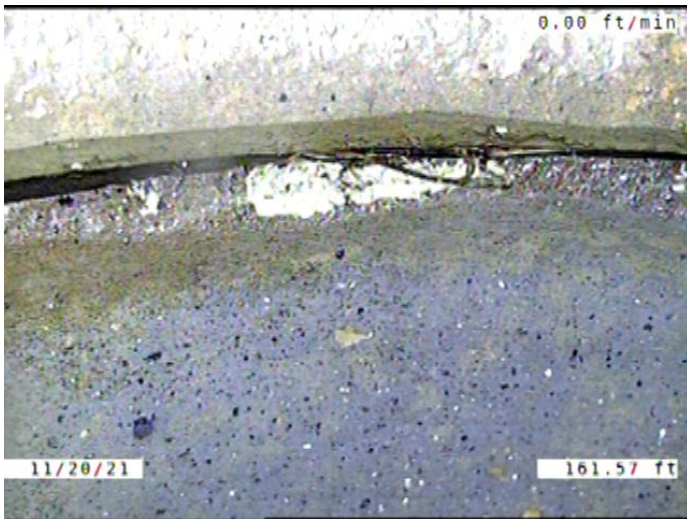


Code: **DAE**  
Description: **Deposits Attached Encrustation**

Distance (ft): **161.6**  
Structural Grade: **0**  
O&M Grade: **2**  
Clock Start/From: **10**  
Clock To:  
1st Value:  
2nd Value:  
Value Percent: **5.000**  
Continuous Index:  
Within 8" of Joint: **YES**  
Remarks:

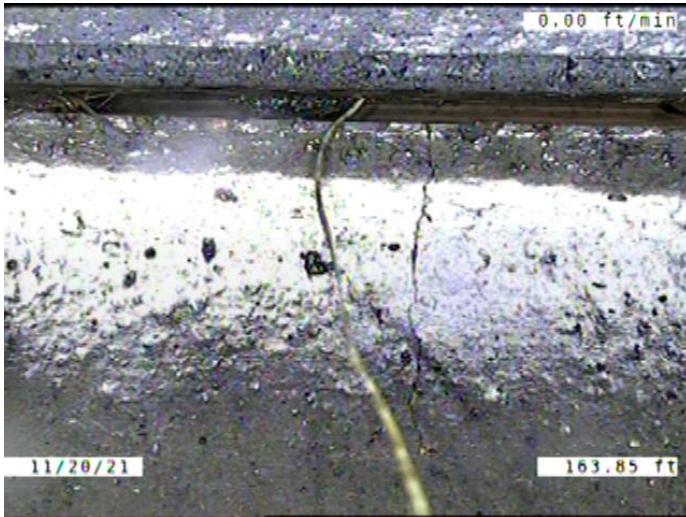

Code: **RFJ**  
 Description: **Roots Fine Joint**


Distance (ft): **163.8**  
 Structural Grade: **0**  
 O&M Grade: **1**  
 Clock Start/From: **9**  
 Clock To: **3**  
 1st Value:  
 2nd Value:  
 Value Percent:  
 Continuous Index:  
 Within 8" of Joint: **YES**  
 Remarks:

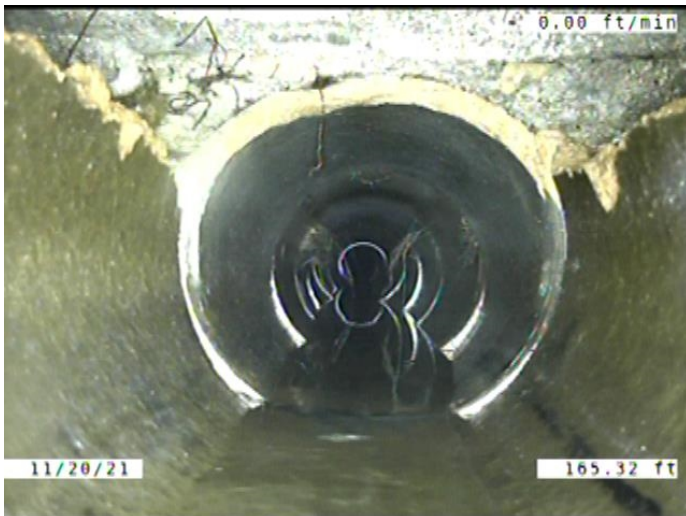

Code: **DSF**  
 Description: **Deposits Settled Fine**

Distance (ft): **165.3**  
 Structural Grade: **0**  
 O&M Grade: **2**  
 Clock Start/From: **5**  
 Clock To: **7**  
 1st Value:  
 2nd Value:  
 Value Percent: **5.000**  
 Continuous Index: **F04**  
 Within 8" of Joint: **YES**  
 Remarks:



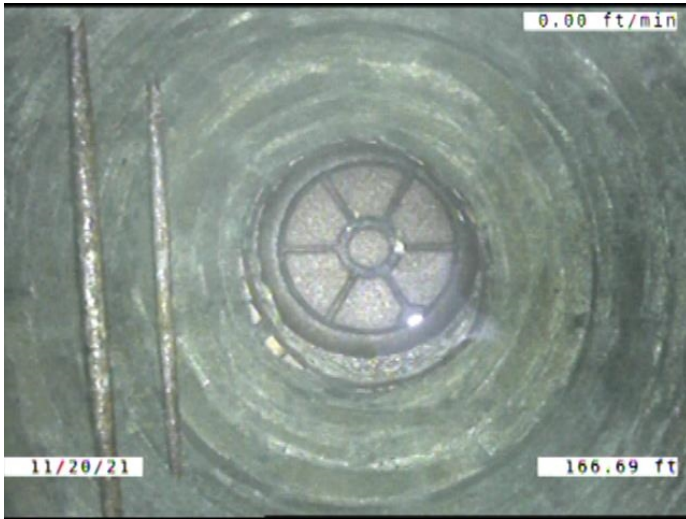

Code:	<b>AMH</b>
Description:	<b>Manhole</b>
Distance (ft):	<b>166.7</b>
Structural Grade:	<b>0</b>
O&M Grade:	<b>0</b>
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	<b>NO</b>
Remarks:	<b>M-604-096</b>
