
| Profile/Ph | oto Observation | Report | | | RedZon |
|------------------|------------------|---------------|--------------------|----------------------------|----------------|
| Date: | 03/26/2018 | Weather: | | Coding: | PACP 6.0 |
| Pipe Length (ft | :): 211.9 | Owner: | NA | Pre Clean: | Not Known |
| P.O.#: | | Surveyor: | Justin Gonzales | PSR: | P-703-007-006 |
| Customer: | | Clean Date: | 01/01/1900 | Shape: | C |
| Street: | EDGEWATER DR | | Flow Control: | Not Controlled | |
| City: | Hobart, IN | | Year Renewed: | | |
| Location: | Other | | Tape/Media #: | | |
| Purpose: | Not Known | | Dia/Height: | 10" | |
| Use: | Sanitary | | Material: | PVC | |
| Drain Area: | NA | | Lining: | | |
| Category: | NA | | | | |
| Comment: | | | | | |
| Location Detai | ls: | | Direction of Surve | ey: Downstream | |
| US MH: | M-703-006 | DS MH: | M-703-007 | Total Length Surveyed (ft) | : 205.8 |
| 0&M Index: | 2.00 | O&M Quick: | 2G00 | O&M Rating: | 82.00 |
| tructural Index: | 0.00 | Structural Qu | ick: 0000 | | 0.00 |
| Overall Index: | 2.00 | Overall Quick | | | 82.00 |





| AMH Manhole |
|----------------|
| .0 |
| 0 |
| 0 |
| |
| |
| |
| |
| |
| |
| NO |
| M-703-006 |
| |

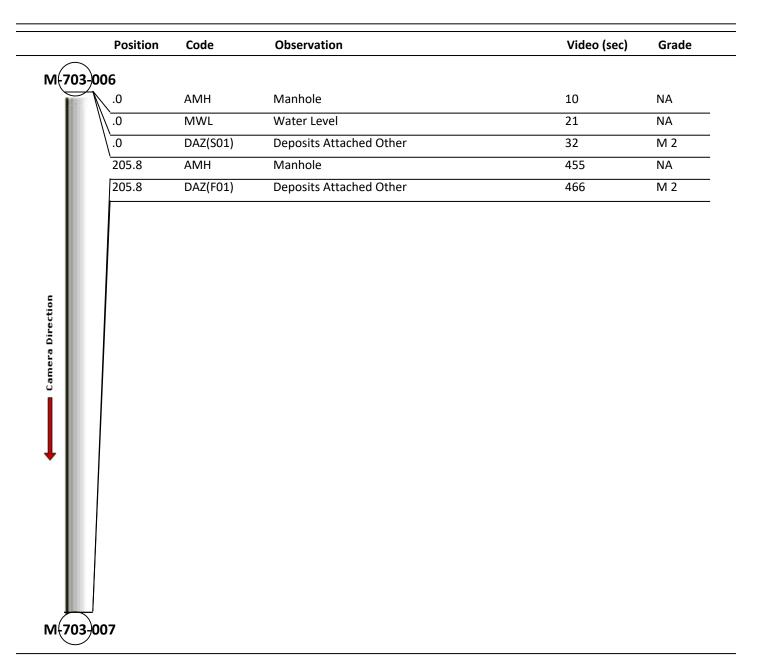

Code: MWL Description: Water Level

| Distance (ft): | .0 |
|---------------------|-------|
| Structural Grade: | 0 |
| O&M Grade: | 0 |
| Clock Start/From: | |
| Clock To: | |
| 1st Value: | |
| 2nd Value: | |
| Value Percent: | 5.000 |
| Continuous Index: | |
| Within 8" of Joint: | NO |
| Remarks: | |
| | |



| Code: | DAZ |
|--------------|-------------------------|
| Description: | Deposits Attached Other |

| Distance (ft): Structural Grade: O&M Grade: Clock Start/From: Clock To: 1st Value: | .0 0 2 7 5 |
|---|-------------------------------|
| 2nd Value: Value Percent: Continuous Index: Within 8" of Joint: Remarks: | 5.000 S01 YES WANDER |



Code: AMH Description: Manhole

Distance (ft): 205.8 Structural Grade: 0 O&M Grade: 0 Clock Start/From: Clock To: 1st Value: 2nd Value: Value Percent: Continuous Index: Within 8" of Joint: NO Remarks: M-703-007

Code: Description: DAZ Deposits Attached Other



| Distance (ft): | 205.8 |
|---------------------|--------|
| Structural Grade: | 0 |
| O&M Grade: | 2 |
| Clock Start/From: | 7 |
| Clock To: | 5 |
| 1st Value: | |
| 2nd Value: | |
| Value Percent: | 5.000 |
| Continuous Index: | F01 |
| Within 8" of Joint: | YES |
| Remarks: | WANDER |
