Profile/Photo Observation Report



Date: 04/25/2018 Weather: **PACP 4.2** Coding: Pipe Length (ft): 300.1 Owner: **City of Hobart** Pre Clean: No Pre-Cleaning P.O.#: 2004 Surveyor: SAN PSR: P-703-042-035 Customer: **Red Zone** Clean Date: Shape: 504 Deerpath Ct Flow Control: **Not Controlled** Street: City: **Hobart In** Year Renewed: Yard Tape/Media #: Deliverable 1 Location: Purpose: **Routine Assessment** Dia/Height: **PVC** Use: Sanitary Material: Northeast Lining: Drain Area: NA Category: Comment: 434-1/DSMH # on video is incorrect due to a manhole that was not shown on mapping. **Location Details: Edge of street** Direction of Survey: **Downstream** US MH: M-703-042 Total Length Surveyed (ft): DS MH: M-703-042A 300.1

O&M Index:	2.83	O&M Quick:	3521	O&M Rating:	17.00
Structural Index:	2.00	— Structural Quick:	2500	Structural Rating:	10.00
Overall Index:	2.45	Overall Quick:	3526	Overall Rating:	27.00
-	•			_	_

	2 .0 .0 .0 7.2 13.8 16.6 20.0	AMH MWL DSF TF	Manhole Water Level Deposits Settled Fine Tap Factory	18 29 97 138	NA NA M 2
	.0 .0 7.2 13.8 16.6	MWL DSF TF	Water Level Deposits Settled Fine	29 97	NA M 2
	7.2 13.8 16.6	DSF TF	Deposits Settled Fine	97	M 2
	13.8 16.6	TF			
	16.6		Tap Factory	138	
		TF		130	NA
11/1	20.0	***	Tap Factory	165	NA
\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\	20.0	TF	Tap Factory	198	NA
- 11	28.2	TF	Tap Factory	233	NA
H \ \\	30.8	TF	Tap Factory	259	NA
	93.8	TF	Tap Factory	389	NA
	100.5	TF	Tap Factory	420	NA
	170.5	TF	Tap Factory	591	NA
	180.1	TF	Tap Factory	626	NA
	243.2	TF	Tap Factory	764	NA
	245.9	TF	Tap Factory	813	NA
	276.3	MWLS(S02)	Water Level Sag	895	S 2
	282.7	MWL	Water Level	914	NA
	300.1	MWLS(F02)	Water Level Sag	1035	S 2
	300.1	AMH	Manhole	1110	NA



Code:	AMH
Description:	Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-703-042



Deposits Settled Fine

Code: MWL Description: **Water Level**

Distance (ft): .0 Structural Grade: 0 O&M Grade: 0 Clock Start/From:

Clock To: 1st Value: 2nd Value:

0.000 Value Percent:

Continuous Index:

Within 8" of Joint: NO

Remarks:

Code: DSF

Description: **Deposits Settled Fine**

Distance (ft): 7.2 Structural Grade: 0 O&M Grade: 2 Clock Start/From: 6

Clock To: 1st Value: 2nd Value:

Value Percent: 10.000

Continuous Index:

Within 8" of Joint: NO

Remarks:



Code: **TF**

Description: Tap Factory

Distance (ft): 13.8
Structural Grade: 0

O&M Grade: 0

Clock Start/From: 3

Clock To:

1st Value: **4.000**

2nd Value: Value Percent: Continuous Index:

Within 8" of Joint:

Remarks:

NO



Code: TF

Description: Tap Factory

Distance (ft): 16.6
Structural Grade: 0

O&M Grade: 0

Clock Start/From: 9

Clock To:

1st Value: **4.000**

2nd Value: Value Percent: Continuous Index:

Within 8" of Joint: NO

Remarks:



Code: TF

Description: **Tap Factory**

Distance (ft): 20.0 Structural Grade: 0 O&M Grade: 0 Clock Start/From: 9

Clock To:

1st Value: 4.000

2nd Value: Value Percent: Continuous Index:

Within 8" of Joint:

Remarks:

NO



Code: TF

Description: **Tap Factory**

Distance (ft): 28.2 Structural Grade: 0 O&M Grade: 0 Clock Start/From: 3

Clock To:

4.000 1st Value:

2nd Value: Value Percent: Continuous Index:

Within 8" of Joint: NO

Remarks:



Code: TF Description: **Tap Factory**

Distance (ft): 30.8 Structural Grade: 0 O&M Grade: 0 Clock Start/From: 3

Clock To:

1st Value: 4.000

2nd Value: Value Percent: Continuous Index:

Within 8" of Joint:

Remarks:

NO



Code: TF

Description: **Tap Factory**

Distance (ft): 93.8 Structural Grade: 0 O&M Grade: 0 Clock Start/From: 3

Clock To:

1st Value: 4.000

2nd Value: Value Percent: Continuous Index:

Within 8" of Joint:

Remarks:

NO



Code: TF Description: **Tap Factory**

Distance (ft): 100.5 Structural Grade: 0 O&M Grade: 0 Clock Start/From: 9

Clock To:


1st Value: 4.000

2nd Value: Value Percent: Continuous Index:

Within 8" of Joint:

Remarks:

NO

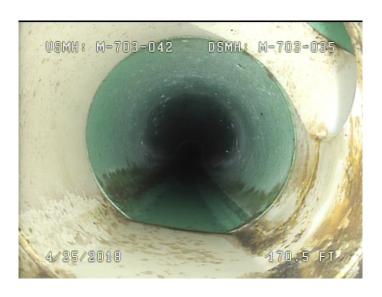

Code: TF

Description: **Tap Factory**

Distance (ft): 170.5 Structural Grade: 0 O&M Grade: 0 Clock Start/From: 1

Clock To:

1st Value: 4.000

2nd Value: Value Percent: Continuous Index:

Within 8" of Joint: NO

Remarks:



Code: **TF**

Description: Tap Factory

Distance (ft): 180.1
Structural Grade: 0
O&M Grade: 0
Clock Start/From: 10

Clock To:

1st Value: **4.000**

2nd Value: Value Percent: Continuous Index:

Within 8" of Joint:

Remarks:

NO



Code: TF

Description: Tap Factory

Distance (ft): 243.2
Structural Grade: 0
O&M Grade: 0
Clock Start/From: 11

Clock To:

1st Value: **4.000**

2nd Value: Value Percent: Continuous Index:

Within 8" of Joint: NO

Remarks:



Code: TF

Description: **Tap Factory**

Distance (ft): 245.9 Structural Grade: 0 O&M Grade: 0 Clock Start/From: 1

Clock To:

1st Value: 4.000

2nd Value: Value Percent: Continuous Index:

Within 8" of Joint:

Remarks:

NO



Code: **MWLS**

Description: **Water Level Sag**

Distance (ft): 276.3 Structural Grade: 2 O&M Grade: 3

Clock Start/From:

Clock To: 1st Value: 2nd Value:

Value Percent: 15.000 Continuous Index: S02 Within 8" of Joint: NO

Remarks:



Code: MWL Description: **Water Level**

Distance (ft): 282.7 Structural Grade: 0 0 O&M Grade:

Clock Start/From:

Clock To: 1st Value: 2nd Value:

Value Percent: 25.000

Continuous Index:

Within 8" of Joint:

Remarks:

NO



Code: **MWLS**

Description: **Water Level Sag**

Distance (ft): 300.1 Structural Grade: 2 O&M Grade: 3

Clock Start/From:

Clock To: 1st Value: 2nd Value:

Value Percent: 15.000 Continuous Index: F02 Within 8" of Joint: NO

Remarks:



Code: AMH
Description: Manhole

Distance (ft): 300.1
Structural Grade: 0

O&M Grade: 0

Clock Start/From:

Clock To: 1st Value: 2nd Value: Value Percent: Continuous Index:

Within 8" of Joint: NO

Remarks: M-703-042A
