


Profile/Ph	oto Observation	Report			RedZone
Date:	04/09/2018	Weather:		Coding:	PACP 6.0
Pipe Length (ft)	: 334.4	Owner:	NA	Pre Clean:	Not Known
P.O.#:		Surveyor:	Byrd Fitzgerald	PSR:	P-704-016-014
Customer:		Clean Date:	01/01/1900	Shape:	С
Street:	N MICHIGAN AVE		Flow Control:	Not Controlled	l
City:	Hobart, IN		Year Renewed:		
Location:	Other		Tape/Media #:		
Purpose:	Not Known		Dia/Height:	8"	
Use:	Sanitary		Material:	VCP	
Drain Area:	NA		Lining:		
Category:	NA				
Comment:					
Location Detail	s:		Direction of Surv	vey: Downstream	
US MH:	M-704-016	DS MH:	M-704-014	Total Length Surveyed (ft)	): <b>30.4</b>
0&M Index:	0.00	O&M Quick:	000	00 O&M Rating:	0.00
tructural Index:	0.00	Structural Qu	iick: 000		0.00
Overall Index:	0.00	Overall Quick	c: 000	00 Overall Rating:	0.00

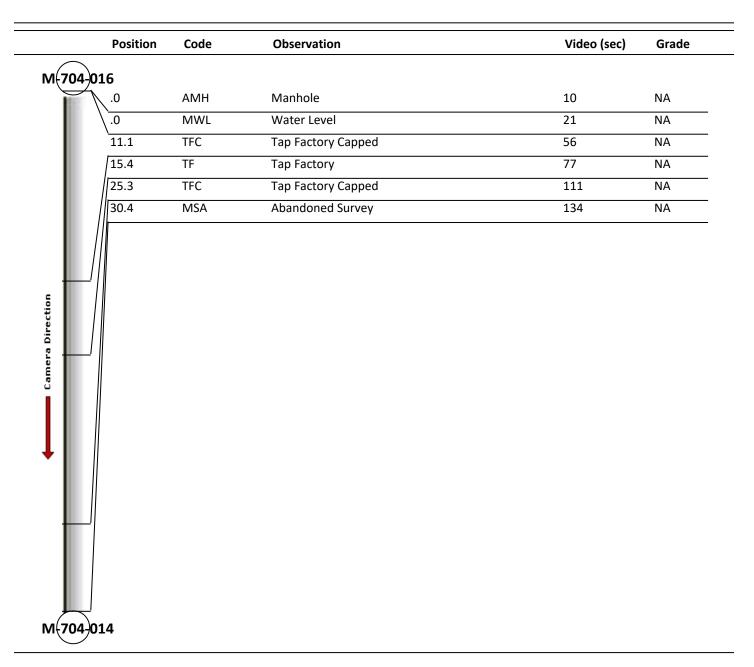



Code: Description:	AMH Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-704-016



Code: MWL Description: Water Level

.0
0
0
5.000
NO



Code: Description:	TFC Tap Factory Capped
Distance (ft):	11.1
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	10
Clock To:	
1st Value:	4.000
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	YES
Remarks:	



Code:	TF
Description:	Tap Factory

Distance (ft):	15.4
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	3
Clock To:	
1st Value:	8.000
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	
Remarks:	



Code:	TFC
Description:	Tap Factory Capped
Distance (ft):	25.3
Structural Grade:	0
O&M Grade:	0
Clock Start/From: Clock To: 1st Value: 2nd Value:	3 4.000
Value Percent: Continuous Index: Within 8" of Joint: Remarks:	YES



Code:MSADescription:Aban

MSA Abandoned Survey

Distance (ft):	30.4
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	no blockage
