
Date:	04/19/2018	Weather:		Coding:	PACP 6.0
Pipe Length (ft		Owner:	NA	Pre Clean:	Not Known
P.O.#:		Surveyor:	Byrd Fitzgerald	PSR:	P-706-041-040
Customer:		Clean Date:	01/01/1900	Shape:	С
Street:	Capitol		Flow Control:	Not Controlled	l
City:	Hobart, IN		Year Renewed:		
Location:	Light Highway		Tape/Media #:		
Purpose:	Maintenance Relat	ted	Dia/Height:	12"	
Use:	Sanitary		Material:	PVC	
Drain Area:	NA		Lining:	Cured in Place	
Category:	NA				
Comment:	Debris at 106'.				
Location Detai	ls:		Direction of Surve	ey: Downstream	
US MH:	M-706-040	DS MH:	M-706-041	Total Length Surveyed (ft): 107.2
D&M Index:	2.00	O&M Quick:	2C00	O&M Rating:	42.00
Structural Index	0.00	Structural Qu	uick: 0000		0.00
Overall Index:	2.00	Overall Quic			42.00





Code: Description:	AMH Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-706-040

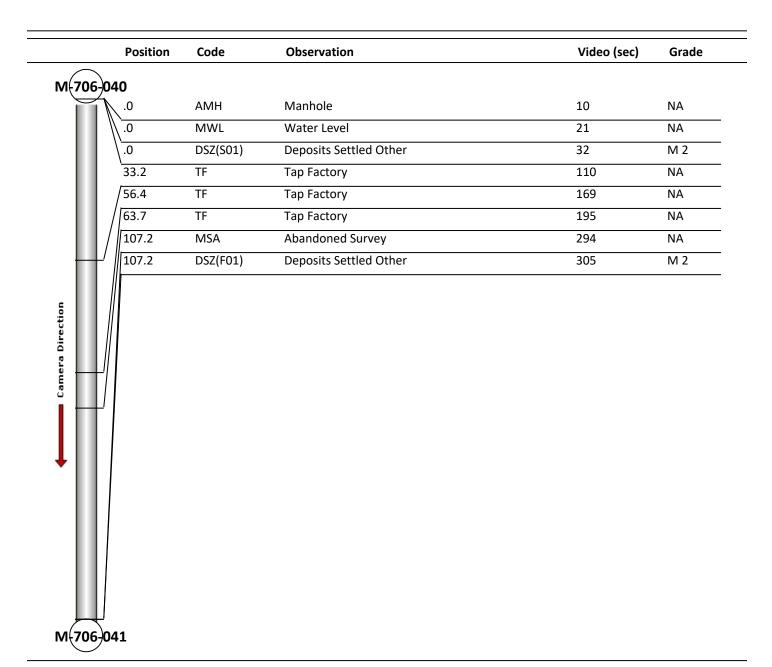

Code: MWL Description: Water Level

Distance (ft): .0 Structural Grade: 0 O&M Grade: 0 Clock Start/From: Clock To: 1st Value: 2nd Value: Value Percent: 5.000 Continuous Index: Within 8" of Joint: NO Remarks:



Code:	DSZ
Description:	Deposits Settled Other

Distance (ft):	.0
Structural Grade:	0
O&M Grade:	2
Clock Start/From:	6
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	5.000
Continuous Index:	S01
Within 8" of Joint:	NO
Remarks:	tissue/debris



Code:	TF
Description:	Tap Factory
Distance (ft):	33.2
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	11
Clock To:	
1st Value:	4.000
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	YES
Remarks:	



Code: Description:	TF Tap Factory
Distance (ft):	56.4
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	2
Clock To:	
1st Value:	4.000
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	YES
Remarks:	



Code:	TF
Description:	Tap Factory
	60 7
Distance (ft):	63.7
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	2
Clock To:	
1st Value:	4.000
2nd Value:	
Value Percent:	
a	

Continuous Index: Within 8" of Joint: YES

Remarks:



Code:	MSA
Description:	Abandoned Survey

Distance (ft):	107.2
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	no blockage



Code:DSZDescription:Deposits Settled Other

Distance (ft):	107.2
Structural Grade:	0
O&M Grade:	2
Clock Start/From:	6
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	5.000
Continuous Index:	F01
Within 8" of Joint:	NO
Remarks:	tissue/debris
