
Date:	04/03/2018	Weather:		Coding:	PACP 6.0
Pipe Length (ft		Owner:	NA	Pre Clean:	Not Known
P.O.#:		Surveyor:	Jen Costello	PSR:	P-708-110-109
Customer:		Clean Date:	01/01/1900	Shape:	C
Street:	Bracken		Flow Control:	Not Controlled	1
City:	Hobart, IN		Year Renewed:		
Location:	Sidewalk		Tape/Media #:		
Purpose:	Maintenance Rela	ted	Dia/Height:	8"	
Use:	Sanitary		Material:	PVC	
Drain Area:	NA		Lining:	Cured in Place	
Category:	NA				
Comment:					
Location Detail	s:		Direction of Surv	ey: Downstream	
US MH:	M-708-110	DS MH:	M-708-109	Total Length Surveyed (ft): 10.9
D&M Index:	2.00	O&M Quick:	220	0 O&M Rating:	4.00
Structural Index:	0.00	Structural Q	uick: 000		0.00
Overall Index:	2.00	Overall Quic		0 Overall Rating:	4.00





Code: Description:	AMH Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-708-110

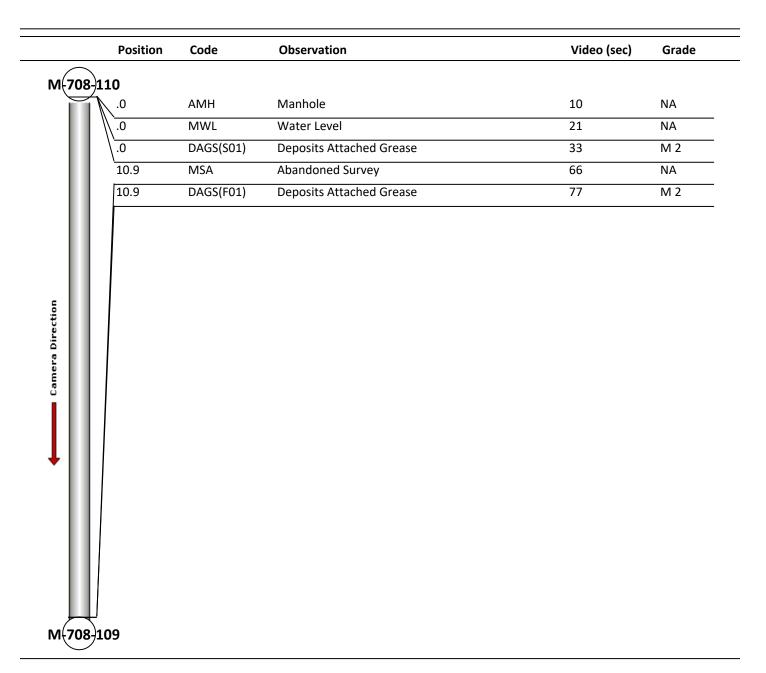

Code: Description:

Within 8" of Joint:

Remarks:

Distance (ft): .0 Structural Grade: 0 O&M Grade: 0 Clock Start/From: Clock To: 1st Value: 2nd Value: Value Percent: 5.000 Continuous Index:


MWL

Water Level

Code:	DAGS
Description:	Deposits Attached Grease

NO

Distance (ft):	.0
Structural Grade:	0
O&M Grade:	2
Clock Start/From:	7
Clock To:	5
1st Value:	
2nd Value:	
Value Percent:	5.000
Continuous Index:	S01
Within 8" of Joint:	NO
Remarks:	



Code:MSADescription:Abandoned Survey

Distance (ft):	10.9
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	overturned

Code: Description: DAGS Deposits Attached Grease



Distance (ft):	10.9
Structural Grade:	0
O&M Grade:	2
Clock Start/From:	7
Clock To:	5
1st Value:	
2nd Value:	
Value Percent:	5.000
Continuous Index:	F01
Within 8" of Joint:	NO
Remarks:	
