
					ROBOTIC
Date:	04/02/2018	Weather:		Coding:	PACP 6.0
Pipe Length (ft	:): 85.2	Owner:	NA	Pre Clean:	Not Known
P.O.#:		Surveyor:	Jen Costello	PSR:	P-708-127-126
Customer:		Clean Date:	01/01/1900	Shape:	С
Street:	Redbud		Flow Control:	Not Controlled	
City:	Hobart, IN		Year Renewed:		
Location:	Sidewalk		Tape/Media #:		
Purpose:	Maintenance Rela	ted	Dia/Height:	8"	
Use:	Sanitary		Material:	PVC	
Drain Area:	NA		Lining:	Cured in Place	
Category:	NA				
Comment:	Flow direction wro	ong.			
Location Detai	ls:		Direction of Surve	y: Downstream	
US MH:	M-708-126	DS MH:	M-708-127	Total Length Surveyed (ft)	: 78.8
D&M Index:	0.00	O&M Quick:	0000	O&M Rating:	0.00
Structural Index	0.00	Structural Qu	uick: 0000	Structural Rating:	0.00
Overall Index:	0.00	Overall Quicl		Overall Rating:	0.00






Code: Description:	AMH Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-708-126

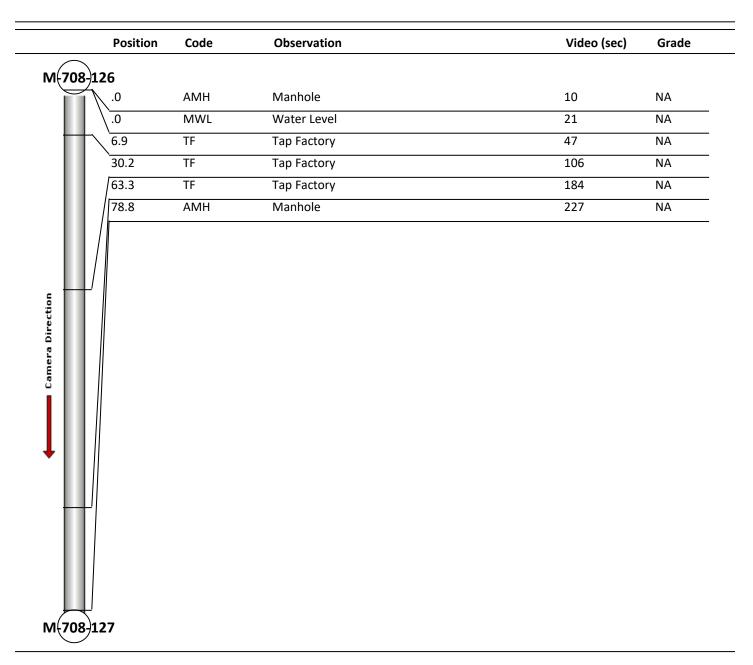


Code: MWL Description: Water Level

Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	5.000
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	



TF Tap Factory
6.9
0
0
3
4.000




Code:	TF
Description:	Tap Factory

Distance (ft):	30.2
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	3
Clock To:	
1st Value:	4.000
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	
Remarks:	



Code: Description:	TF Tap Factory
Distance (ft):	63.3
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	3
Clock To:	
1st Value:	4.000
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	
Remarks:	



Code:	AMH
Description:	Manhole

Distance (ft):	78.8
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-708-127
