

| Profile/Ph | oto Observation | Report | | | | RedZone |
|------------------|-------------------|-------------------|------------------|--------------|----------------|---------------|
| Date: | 10/12/2018 | Weather: | | Co | oding: F | PACP 6.0 |
| Pipe Length (ft |): 80.1 | Owner: | NA | Pr | e Clean: 🛛 🛚 | Not Known |
| P.O.#: | | Surveyor: | Selasie Honu | PS | SR: F | P-708-128-127 |
| Customer: | | Clean Date: | 01/01/1900 | Sh | nape: (| C |
| Street: | Magnolia Dr. | | Flow Control: | No | ot Controlled | |
| City: | Hobart, IN | | Year Renewed: | | | |
| Location: | Light Highway | | Tape/Media #: | | | |
| Purpose: | Routine Assessmen | t | Dia/Height: | 8" | | |
| Use: | Sanitary | | Material: | PV | 'C | |
| Drain Area: | NA | | Lining: | | | |
| Category: | NA | | | | | |
| Comment: | | | | | | |
| Location Detai | ls: | | Direction of Sur | vey: Up | ostream | |
| US MH: | M-708-127 | DS MH: | M-708-128 | Total Length | Surveyed (ft): | 83.1 |
| 0&M Index: | 0.00 | O&M Quick: | 00 | 00 O&M | I Rating: | 0.00 |
| tructural Index: | 0.00 | Structural Qu | ick: 000 | 00 Struc | tural Rating: | 0.00 |
| Overall Index: | 0.00 | Overall Quick | . 000 | 00 Overa | all Rating: | 0.00 |



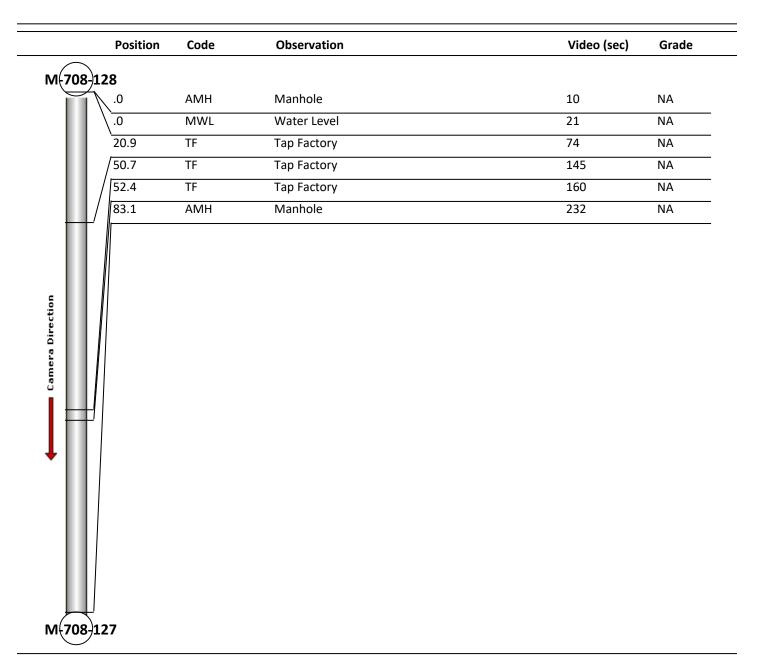


| Code: | АМН |
|---------------------|-----------|
| Description: | Manhole |
| | |
| Distance (ft): | .0 |
| Structural Grade: | 0 |
| O&M Grade: | 0 |
| Clock Start/From: | |
| Clock To: | |
| 1st Value: | |
| 2nd Value: | |
| Value Percent: | |
| Continuous Index: | |
| Within 8" of Joint: | NO |
| Remarks: | M-708-128 |



Code: MWL Description: Water Level

| Distance (ft): | .0 |
|---------------------|-------|
| Structural Grade: | 0 |
| O&M Grade: | 0 |
| Clock Start/From: | |
| Clock To: | |
| 1st Value: | |
| 2nd Value: | |
| Value Percent: | 5.000 |
| Continuous Index: | |
| Within 8" of Joint: | NO |
| Remarks: | |
| | |



| Code: Description: | TF Tap Factory |
|-----------------------|-------------------|
| | |
| Distance (ft): | 20.9 |
| Structural Grade: | 0 |
| O&M Grade: | 0 |
| Clock Start/From: | 9 |
| Clock To: | |
| 1st Value: | 4.000 |
| 2nd Value: | |
| Value Percent: | |
| Continuous Index: | |
| Within 8" of Joint: | |
| Remarks: | |



| Code: | TF |
|--------------|-------------|
| Description: | Tap Factory |

| Distance (ft): | 50.7 |
|---------------------|-------|
| Structural Grade: | 0 |
| O&M Grade: | 0 |
| Clock Start/From: | 9 |
| Clock To: | |
| 1st Value: | 4.000 |
| 2nd Value: | |
| Value Percent: | |
| Continuous Index: | |
| Within 8" of Joint: | |
| Remarks: | |



| TF Tap Factory |
|-------------------|
| 52.4 |
| 0 |
| 0 |
| 3 |
| |
| 4.000 |
| |
| |
| |
| |
| |
| |



| Code: | AMH |
|--------------|---------|
| Description: | Manhole |

| Distance (ft): | 83.1 |
|---------------------|-----------|
| Structural Grade: | 0 |
| O&M Grade: | 0 |
| Clock Start/From: | |
| Clock To: | |
| 1st Value: | |
| 2nd Value: | |
| Value Percent: | |
| Continuous Index: | |
| Within 8" of Joint: | NO |
| Remarks: | M-708-127 |
| | |
