
Profile/Ph	oto Observatio	n Report			RedZone	
Date: Pipe Length (ft P.O.#:	03/21/2018): 80.9	Weather: Owner: Surveyor:	NA Selasie Honu	Coding: Pre Clean: PSR:	PACP 6.0 Not Known P-709-011-010	
Customer:		Clean Date:	01/01/1900	Shape:	С	
Street:	DUNLIN CT		Flow Control:	Not Controlled		
City:	Hobart, IN		Year Renewed:			
Location:	Yard		Tape/Media #:			
Purpose:	Maintenance Rela	ated	Dia/Height:	8"		
Use:	Sanitary		Material:	PVC		
Drain Area:	NA		Lining:			
Category:	NA					
Comment:	Reverse setup. heavy gravel and sludge at 69'.					
Location Detai	ls:		Direction of Surve	y: Upstream		
US MH:	M-709-010	DS MH:	M-709-011	Total Length Surveyed (ft)	: 70.3	
D&M Index:	2.00	O&M Quick:	2100	O&M Rating:	2.00	
Structural Index:	0.00	Structural Qu	ick: 0000	Structural Rating:	0.00	
Overall Index:	2.00	Overall Quick	2100	Overall Rating:	2.00	





Code: Description:	AMH Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-709-011

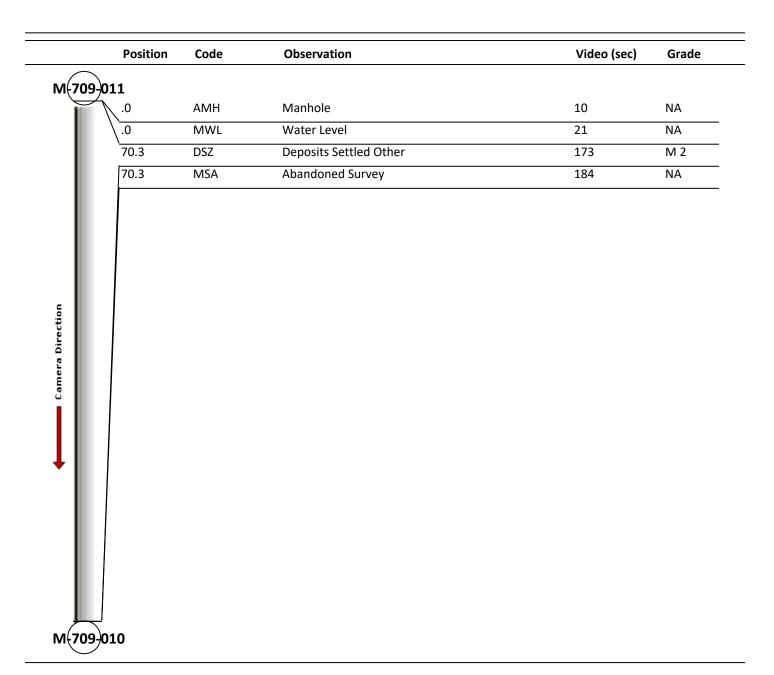

Code: MWL Description: Water Level

Distance (ft): .0 Structural Grade: 0 O&M Grade: 0 Clock Start/From: Clock To: 1st Value: 2nd Value: Value Percent: 5.000 Continuous Index: Within 8" of Joint: NO Remarks:



Code: Description:	DSZ Deposits Settled Other
Distance (ft):	70.3
Structural Grade:	0
O&M Grade:	2
Clock Start/From:	6
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	5.000
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	mixed material

Thursday, November 16, 2023



Code:MSADescription:Abandoned Survey

Distance (ft):	70.3
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	mixed ma

NO mixed material blocking passage
