
Profile/Ph	oto Observatio	n Report				RedZone
Date:	03/20/2018	Weather:			Coding:	PACP 6.0
Pipe Length (ft)	: <b>75.0</b>	Owner:	NA		Pre Clean:	Not Known
P.O.#:		Surveyor:	John Kuglma	er	PSR:	P-802-012-011
Customer:		Clean Date:	01/01/1900		Shape:	0
Street:	N Hobart Rd		Flow Control:		Not Controlled	
City:	Hobart, IN		Year Renewed			
Location:	Main Highway - S	uburban/Rural	Tape/Media #:			
Purpose:	Resurvey		Dia/Height:		10"	
Use:	Sanitary		Material:		PVC	
Drain Area:	NA		Lining:			
Category:	NA					
Comment:						
Location Details	s:		Direction of Su	rvey:	Upstream	
US MH:	M-802-011	DS MH:	M-802-012	Total I	Length Surveyed (ft):	73.0
D&M Index:	2.00	O&M Quick:	2/	00	O&M Rating:	28.00
Structural Index:	0.00	Structural Qu	uick: 00	000	Structural Rating:	0.00
Overall Index:	2.00	Overall Quicl	<: <b>2</b> /	00	Overall Rating:	28.00





Code: Description:	AMH Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-802-012

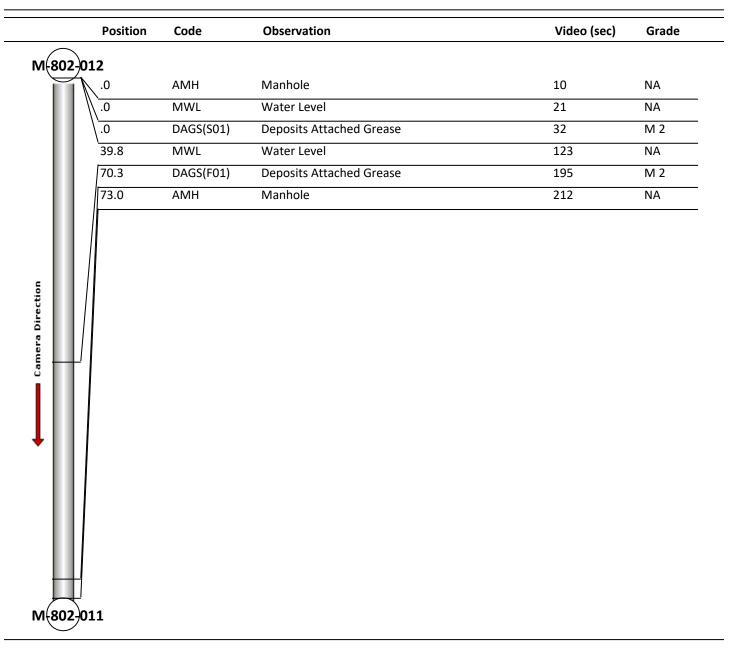

Code: MWL Description: Water Level

Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	10.000
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	



Code:	DAGS
Description:	<b>Deposits Attached Grease</b>

Distance (ft):	.0
Structural Grade:	0
O&M Grade:	2
Clock Start/From:	4
Clock To:	8
1st Value:	
2nd Value:	
Value Percent:	10.000
Continuous Index:	S01
Within 8" of Joint:	NO
Remarks:	



Code: MWL Description: Water Level

Distance (ft):	39.8
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	25.000
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	

Code:

Description:



Distance (ft):	70.3
Structural Grade:	0
O&M Grade:	2
Clock Start/From:	4
Clock To:	8
1st Value:	
2nd Value:	
Value Percent:	10.000
Continuous Index:	F01
Within 8" of Joint:	NO
Remarks:	Clock positions vary

DAGS

**Deposits Attached Grease** 



Code:AMHDescription:Manhole

Distance (ft):	73.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-802-011
