


Date:	03/28/2018	Weather:		Coding:	PACP 6.0
Pipe Length (ft):	207.8	Owner:	NA	Pre Clean:	Not Known
P.O.#:		Surveyor:	Selasie Honu	PSR:	P-803-034-035
Customer:		Clean Date:	01/01/1900	Shape:	С
Street:	E 40TH AVE		Flow Control:	Not Controlled	
City:	Hobart, IN		Year Renewed:		
Location:	Other		Tape/Media #:		
Purpose:	Not Known		Dia/Height:	10"	
Use:	Sanitary		Material:	VCP	
Drain Area:	NA		Lining:		
Category:	NA				
Comment:					
Location Details:			Direction of Surve	ey: Upstream	
US MH: N	Л-803-035	DS MH:	M-803-034	Total Length Surveyed (ft)	: 8.0
D&M Index:	3.00	O&M Quick:	3100	O&M Rating:	3.00
Structural Index:	0.00	Structural Qu	uick: 0000		0.00
Overall Index:	3.00	Overall Quicl	24.00		3.00

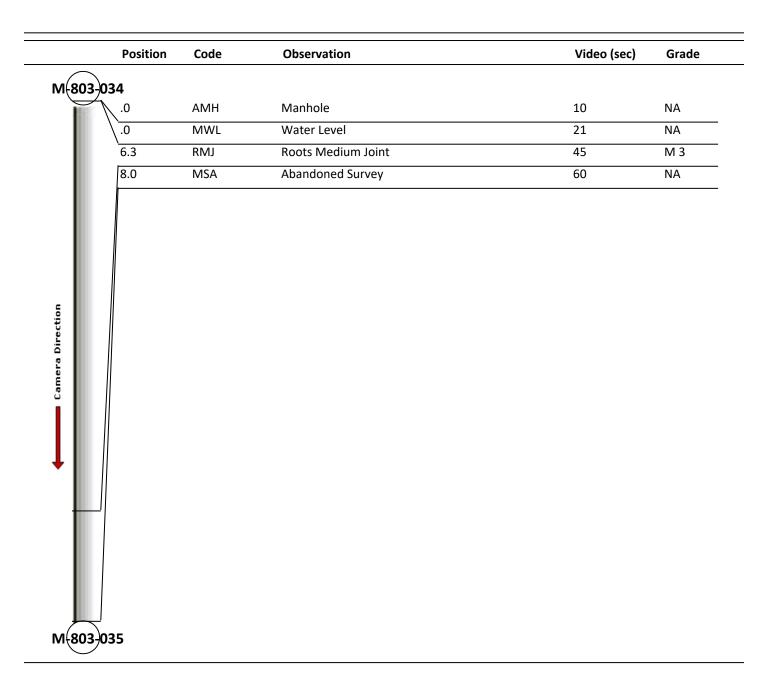



Code: Description:	AMH Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-803-034



Code: MWL Description: Water Level


Remarks:

Distance (ft): .0 Structural Grade: 0 O&M Grade: 0 Clock Start/From: 0 Clock To: 1 1st Value: 2 2nd Value: 5.000 Continuous Index: NO



Code:	RMJ
Description:	Roots Medium Joint

Distance (ft):	6.3
Structural Grade:	0
O&M Grade:	3
Clock Start/From:	8
Clock To:	9
1st Value:	
2nd Value:	
Value Percent:	5.000
Continuous Index:	
Within 8" of Joint:	YES
Remarks:	



Code: Description: MSA Abandoned Survey

Distance (ft):	8.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	camera stopped
