Profile/Photo Observation Report



| Profile/Photo Observation Report | | | | | | | | |
|----------------------------------|---------------------------|--------------------|---------------------|----------------------------|-----------------------------|--|--|--|
| Date: Pipe Length (ft | 05/05/2018): | Weather: Owner: | City of Hobart | Coding: Pre Clean: | PACP 6.0 No Pre-Cleaning | | | |
| P.O.#: | 192 | Surveyor: | M. Pielacha | PSR: | P-805-013-018 | | | |
| Customer: | City of Hobart | Clean Date: | | Shape: | С | | | |
| Street: | 5th Street | | Flow Control: | Not Controlled | | | | |
| City: | Hobart, IN | | Year Renewed: | | | | | |
| Location: | Light Highway | | Tape/Media #: | DEP 192 | | | | |
| Purpose: | Routine Assessment | | Dia/Height: | 18" | | | | |
| Use: | Sanitary | | Material: | VCP | | | | |
| Drain Area: | | | Lining: | | | | | |
| Category: | NA | | | | | | | |
| Comment: | 5-21-2018 | | | | | | | |
| Location Detail | s: | | Direction of Survey | : Downstream | | | | |
| US MH: | M-805-013 | DS MH: | W-805-018 | Total Length Surveyed (ft) | : 13.0 | | | |
| O&M Index: | 3.00 | O&M Quick: | 3200 | O&M Rating: | 6.00 | | | |
| Structural Index: | 0.00 | Structural Quid | ck: 0000 | Structural Rating: | 0.00 | | | |
| Overall Index: | 3.00 | Overall Quick: | 3200 | Overall Rating: | 6.00 | | | |


Thursday, May 4, 2023

| | Position | Code | Observation | Video (sec) | Grade |
|------------------|----------|------|--------------------------------|-------------|-------|
| M(805-)0 | 13 | | | | |
| | 0 | AMH | Manhole | 0 | NA |
| ш | 0. | MWL | Water Level | 12 | NA |
| ш | 6.8 | ID | Infil Dripper | 195 | M 3 |
| ш | 11.1 | DAE | Deposits Attached Encrustation | 224 | M 3 |
| - | 13.0 | MSA | Abandoned Survey | 271 | NA |
| Camera Direction | | | | | |



| Code: Description: | AMH Manhole |
|-----------------------|----------------|
| | |
| Distance (ft): | .0 |
| Structural Grade: | 0 |
| O&M Grade: | 0 |
| Clock Start/From: | |
| Clock To: | |
| 1st Value: | |
| 2nd Value: | |
| Value Percent: | |
| Continuous Index: | |
| Within 8" of Joint: | NO |
| Remarks: | M-805-013 |
| | |

Thursday, May 4, 2023 2

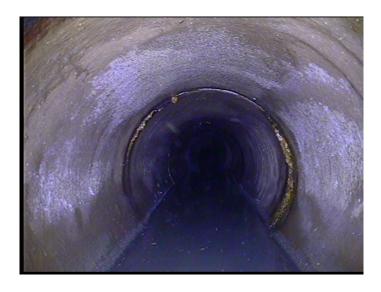

Code: MWL Description: **Water Level**

Distance (ft): .0 Structural Grade: 0 O&M Grade: 0

Clock Start/From:

Clock To: 1st Value: 2nd Value:


Value Percent:

Continuous Index:

Within 8" of Joint: NO

Remarks:

10.000

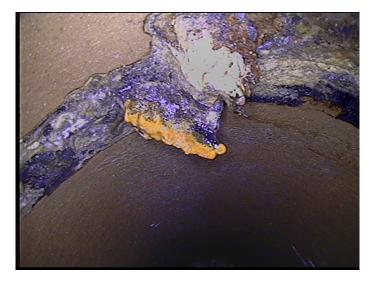

Code: ID

Description: **Infil Dripper**

Distance (ft): 6.8 Structural Grade: 0 O&M Grade: 3 Clock Start/From: 1 Clock To: 1st Value: 2nd Value:


Continuous Index: Within 8" of Joint:

Remarks:

Value Percent:

YES

3 Thursday, May 4, 2023

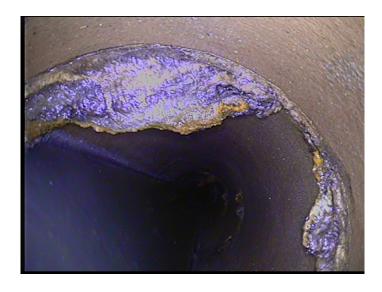

Code: DAE

Description: Deposits Attached Encrustation

Distance (ft): 11.1
Structural Grade: 0
O&M Grade: 3
Clock Start/From: 7
Clock To: 5

1st Value: 2nd Value:

Value Percent: 15.000

Continuous Index:

Within 8" of Joint:

Remarks:

YES



Code: MSA

Description: Abandoned Survey

Distance (ft): 13.0
Structural Grade: 0
O&M Grade: 0

Clock Start/From:

Clock To:
1st Value:
2nd Value:
Value Percent:
Continuous Index:

Within 8" of Joint: NO

Remarks: encrustation

Thursday, May 4, 2023 4
