

					ROBOTIO
Date:	04/12/2018	Weather:		Coding:	PACP 6.0
Pipe Length (ft	:): 191.2	Owner:	NA	Pre Clean:	Not Known
P.O.#:		Surveyor:	Jen Costello	PSR:	P-806-057-058
Customer:		Clean Date:	01/01/1900	Shape:	С
Street:	Capitol		Flow Control:	Not Controlle	ł
City:	Hobart, IN		Year Renewed:		
Location:	Sidewalk		Tape/Media #:		
Purpose:	Maintenance Rela	ited	Dia/Height:	8"	
Use:	Sanitary		Material:	PVC	
Drain Area:	NA		Lining:	Cured in Place	•
Category:	NA				
Comment:					
Location Detai	ls:		Direction of Surv	vey: Downstream	
US MH:	M-806-057	DS MH:	M-806-058	Total Length Surveyed (ft): 188.2
D&M Index:	1.00	O&M Quick:	110	0 O&M Rating:	1.00
Structural Index	0.00	 Structural Q	uick: 000		0.00
Overall Index: 1.00		Overall Quic		0 Overall Rating:	1.00



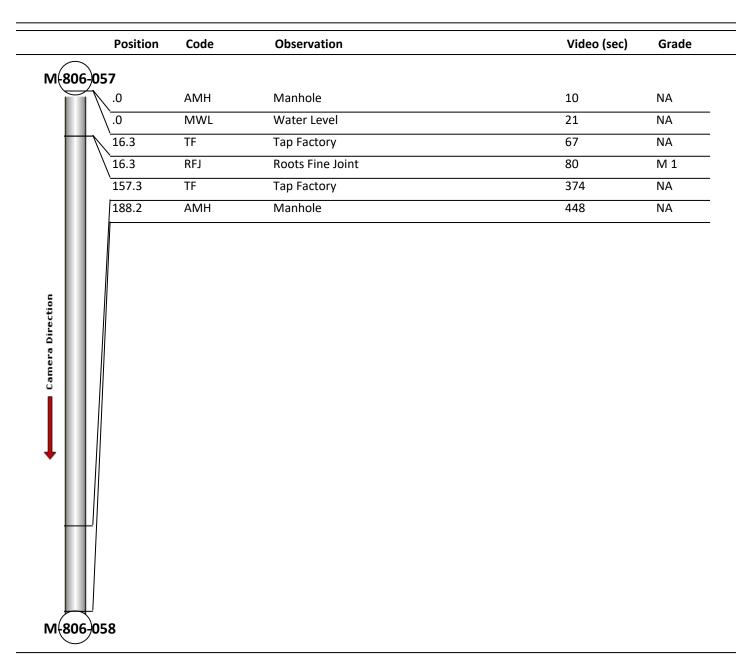


Code:	АМН
Description:	Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-806-057



Code: MWL Description: Water Level

Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	5.000
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	



Code: Description:	TF Tap Factory
Distance (ft):	16.3
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	1
Clock To:	
1st Value:	4.000
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	
Remarks:	




Code:	RFJ
Description:	Roots Fine Joint
Distance (ft):	16.3
Structural Grade:	0
O&M Grade:	1
Clock Start/From:	3
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	YES

Remarks:



Code: Description:	TF Tap Factory
Distance (ft): Structural Grade: O&M Grade: Clock Start/From: Clock To: 1st Value: 2nd Value: Value Percent: Continuous Index: Within 8" of Joint: Remarks:	157.3 0 0 2 4.000



Code:AMHDescription:Manhole

Distance (ft):	188.2
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-806-058
