

Date:	04/14/2018	Weather:			Coding:	PACP 6.0
Pipe Length (f	t):	Owner:	City of Hobart	t	Pre Clean:	Not Known
P.O.#:	254	Surveyor:	B. Helbling		PSR:	P-806-062-035
Customer:	City of Hobart	Clean Date	:		Shape:	С
Street:	East 10th Street		Flow Control:		Not Controlled	
City:	Hobart, IN		Year Renewed:			
Location:	Sidewalk		Tape/Media #:		DEP254	
Purpose:	Routine Assessme	nt	Dia/Height:		15"	
Use:	Sanitary		Material:		PVC	
Drain Area:			Lining:			
Category:	NA					
Comment:	YES501824 Submit	al 2				
Location Detai	ils:		Direction of Sur	rvey:	Upstream	
US MH:	M-806-062	DS MH:	M-806-035	Total Leng	th Surveyed (ft)	: 145.8
0&M Index:	2.00	O&M Quick	: 2D	0 <b>0</b> 08	&M Rating:	56.00
Structural Index	c: <b>0.00</b>	 Structural C	uick: 00	00	ructural Rating:	0.00
overall Index: 2.00		Overall Quid		00 0	verall Rating:	56.00



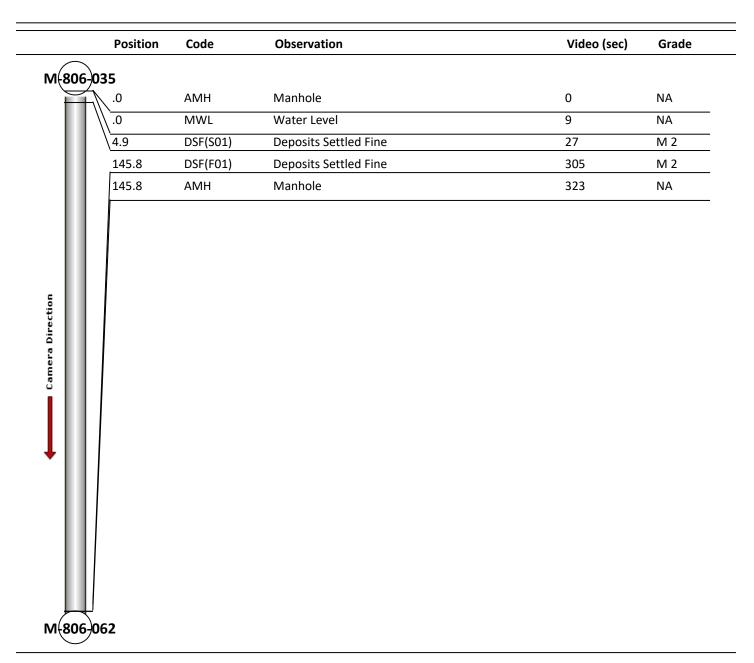

Code: Description:	AMH Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-806-035

Thursday, May 4, 2023

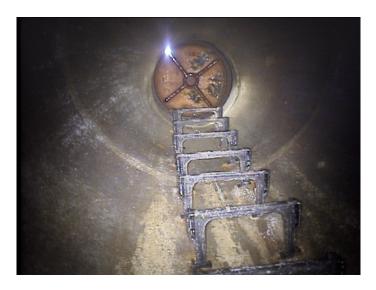

Code:	MWL	
Description:	Water Level	
Distance (ft):	.0	
Structural Grade:	0	
O&M Grade:	0	
	0	
Clock Start/From:		
Clock To:		
1st Value:		
2nd Value:		
Value Percent:	10.000	
Continuous Index:		
Within 8" of Joint:	NO	
Remarks:		



Code: Description:	DSF Deposits Settled Fine
Distance (ft):	4.9
Structural Grade:	0
O&M Grade:	2
Clock Start/From:	5
Clock To:	7
1st Value:	
2nd Value:	
Value Percent:	5.000
Continuous Index:	S01
Within 8" of Joint:	NO
Remarks:	



DSF
<b>Deposits Settled Fine</b>
145.8
145.8
0
2
5
7
5.000
F01
NO



Code: Description:	AMH Manhole
Distance (ft):	145.8
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-806-062
