
| Profile/Ph | oto Observatio | n Report | | | RedZon |
|-----------------|---------------------|-----------------|------------------|---------------------------|------------------|
| Date: | 04/15/2018 | Weather: | | Coding: | PACP 6.0 |
| Pipe Length (ft | :): 188.8 | Owner: | NA | Pre Clean: | Not Known |
| P.O.#: | | Surveyor: | Selasie Honu | PSR: | P-907-004-012 |
| Customer: | | Clean Date: | 01/01/1900 | Shape: | С |
| Street: | S HOBART RD | | Flow Control: | Not Controlle | d |
| City: | Hobart, IN | | Year Renewed: | | |
| Location: | Light Highway | | Tape/Media #: | | |
| Purpose: | Maintenance Rela | ated | Dia/Height: | 12" | |
| Use: | Sanitary | | Material: | PVC | |
| Drain Area: | NA | | Lining: | Cured in Place | 2 |
| Category: | NA | | | | |
| Comment: | battery at 257'. Id | onger than mapp | ed | | |
| Location Detai | ls: | | Direction of Sur | vey: Upstream | |
| US MH: | M-807-012 | DS MH: | M-907-004 | Total Length Surveyed (fi | t): 258.8 |
| 0&M Index: | 0.00 | O&M Quick: | 000 | 00 O&M Rating: | 0.00 |
| tructural Index | 0.00 | Structural Q | uick: 000 | 00 Structural Rating | 0.00 |
| Overall Index: | 0.00 | Overall Quic | k: 000 | 00 Overall Rating: | 0.00 |





| Code: | АМН |
|---------------------|-----------|
| Description: | Manhole |
| | |
| Distance (ft): | .0 |
| Structural Grade: | 0 |
| O&M Grade: | 0 |
| Clock Start/From: | |
| Clock To: | |
| 1st Value: | |
| 2nd Value: | |
| Value Percent: | |
| Continuous Index: | |
| Within 8" of Joint: | NO |
| Remarks: | M-907-004 |

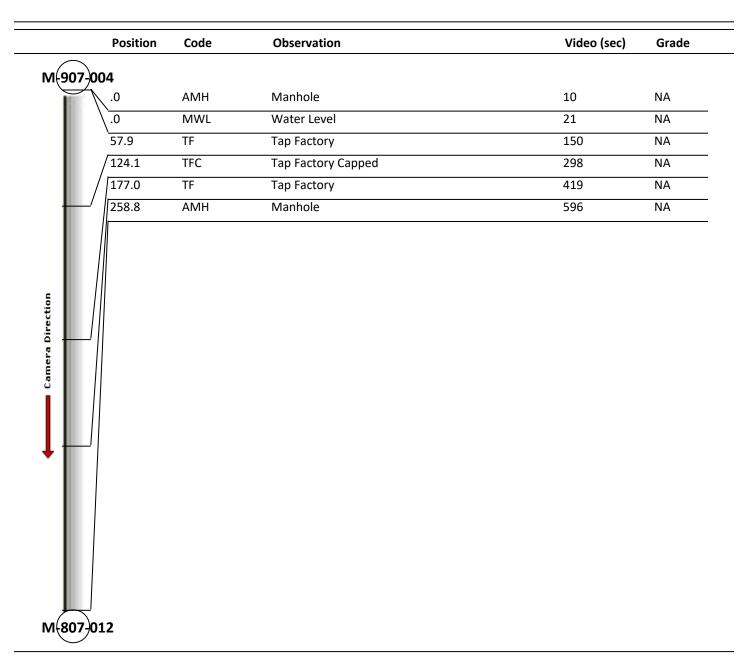

Code: MWL Description: Water Level

| Distance (ft): | .0 |
|---------------------|-------|
| Structural Grade: | 0 |
| O&M Grade: | 0 |
| Clock Start/From: | |
| Clock To: | |
| 1st Value: | |
| 2nd Value: | |
| Value Percent: | 5.000 |
| Continuous Index: | |
| Within 8" of Joint: | NO |
| Remarks: | |
| | |



| Code: Description: | TF Tap Factory |
|-----------------------|-------------------|
| Distance (ft): | 57.9 |
| Structural Grade: | 0 |
| O&M Grade: | 0 |
| Clock Start/From: | 10 |
| Clock To: | |
| 1st Value: | 4.000 |
| 2nd Value: | |
| Value Percent: | |
| Continuous Index: | |
| Within 8" of Joint: | |
| Remarks: | |
| | |




Code:TFCDescription:Tap Factory Capped

| Distance (ft): | 124.1 |
|---------------------|-------|
| Structural Grade: | 0 |
| O&M Grade: | 0 |
| Clock Start/From: | 10 |
| Clock To: | |
| 1st Value: | 4.000 |
| 2nd Value: | |
| Value Percent: | |
| Continuous Index: | |
| Within 8" of Joint: | |
| Remarks: | |



| Code: Description: | TF Tap Factory |
|---|--------------------------------|
| Distance (ft): Structural Grade: O&M Grade: Clock Start/From: Clock To: 1st Value: 2nd Value: Value Percent: Continuous Index: Within 8" of Joint: | 177.0 0 0 10 4.000 |
| Remarks: | |



Code:AMHDescription:Manhole

| Distance (ft): | 258.8 | |
|---------------------|-----------|--|
| Structural Grade: | 0 | |
| O&M Grade: | 0 | |
| Clock Start/From: | | |
| Clock To: | | |
| 1st Value: | | |
| 2nd Value: | | |
| Value Percent: | | |
| Continuous Index: | | |
| Within 8" of Joint: | NO | |
| Remarks: | M-807-012 | |
