
Profile/Ph	oto Observation	Report				RedZon
Date:	10/12/2018	Weather:			Coding:	PACP 6.0
Pipe Length (ft): 391.8	Owner:	NA		Pre Clean:	Not Known
P.O.#:		Surveyor:	Selasie Honu		PSR:	P-808-029-030
Customer:		Clean Date:	01/01/1900		Shape:	С
Street:	Hobart Rd.		Flow Control:		Not Controlled	
City:	Hobart, IN		Year Renewed	:		
Location:	Light Highway		Tape/Media #			
Purpose:	Routine Assessmen	t	Dia/Height:		12"	
Use:	Sanitary		Material:		PVC	
Drain Area:	NA		Lining:			
Category:	NA					
Comment:						
Location Detail	ls:		Direction of Su	rvey:	Downstream	
US MH:	M-808-030	DS MH:	M-808-029	Total	Length Surveyed (ft)	: 334.4
0&M Index:	1.00	O&M Quick:	1:	L00	O&M Rating:	1.00
tructural Index:	0.00	 Structural Qu	iick: 0	000	Structural Rating:	0.00
Overall Index:	1.00	Overall Quick	1:	100	Overall Rating:	1.00





Code: Description:	AMH Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-808-030

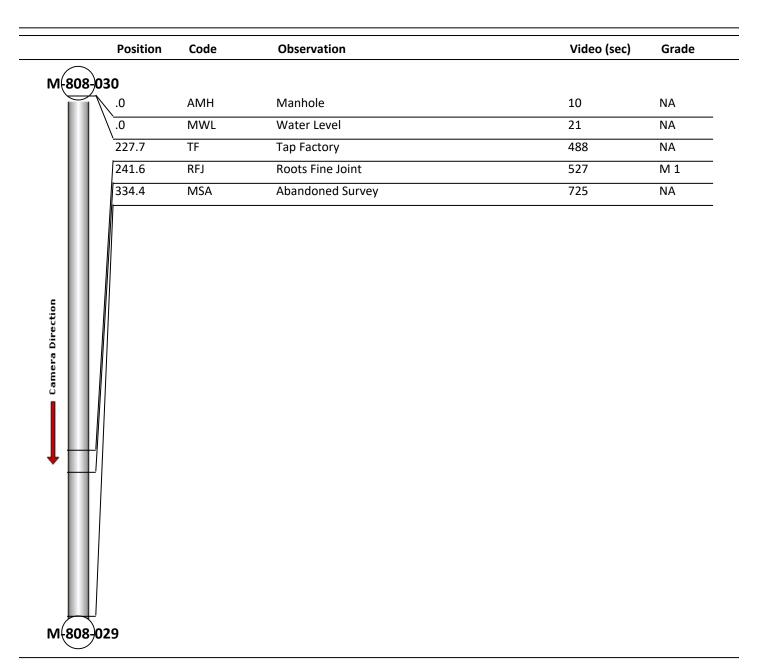


Code: Description:

MWL

Water Level

Distance (ft): .0 Structural Grade: 0 O&M Grade: 0 Clock Start/From: Clock To: 1st Value: 2nd Value: Value Percent: 5.000 Continuous Index: Within 8" of Joint: NO Remarks:




Code: Description:	TF Tap Factory
Distance (ft):	227.7
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	2
Clock To:	
1st Value:	4.000
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	
Remarks:	



Code:RFJDescription:Roots Fine Joint

Distance (ft):	241.6		
Structural Grade:	0		
O&M Grade:	1		
Clock Start/From:	11		
Clock To:			
1st Value:			
2nd Value:			
Value Percent:			
Continuous Index:			
Within 8" of Joint:	YES		
Remarks:			

Code: Description: MSA Abandoned Survey



Distance (ft):	334.4
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	camera stopped
