


| Profile/Ph       | oto Observatior   | n Report         |                    |       |                       | RedZon        |
|------------------|-------------------|------------------|--------------------|-------|-----------------------|---------------|
| Date:            | 04/05/2018        | Weather:         |                    |       | Coding:               | PACP 6.0      |
| Pipe Length (ft) | ): <b>394.2</b>   | Owner:           | NA                 |       | Pre Clean:            | Not Known     |
| P.O.#:           |                   | Surveyor:        | Jen Costello       |       | PSR:                  | P-808-030-031 |
| Customer:        |                   | Clean Date:      | 01/01/1900         |       | Shape:                | с             |
| Street:          | S HOBART RD       |                  | Flow Control:      |       | Not Controlled        |               |
| City:            | Hobart, IN        |                  | Year Renewed:      |       |                       |               |
| Location:        | Light Highway     |                  | Tape/Media #:      |       |                       |               |
| Purpose:         | Maintenance Rela  | ited             | Dia/Height:        |       | 12"                   |               |
| Use:             | Sanitary          |                  | Material:          |       | PVC                   |               |
| Drain Area:      | NA                |                  | Lining:            |       | Cured in Place        |               |
| Category:        | NA                |                  |                    |       |                       |               |
| Comment:         | Flow direction wr | ong. Reverse set | up. Debris at 54'. |       |                       |               |
| Location Detail  | ls:               |                  | Direction of Su    | rvey: | Downstream            |               |
| US MH:           | M-808-031         | DS MH:           | M-808-030          | Total | Length Surveyed (ft): | 56.3          |
| 0&M Index:       | 2.00              | O&M Quick:       | 28                 | 00    | O&M Rating:           | 16.00         |
| tructural Index: | 0.00              | Structural Q     | uick: 00           | 00    | Structural Rating:    | 0.00          |
| Overall Index:   | 2.00              | Overall Quic     | k: 28              | 00    | Overall Rating:       | 16.00         |

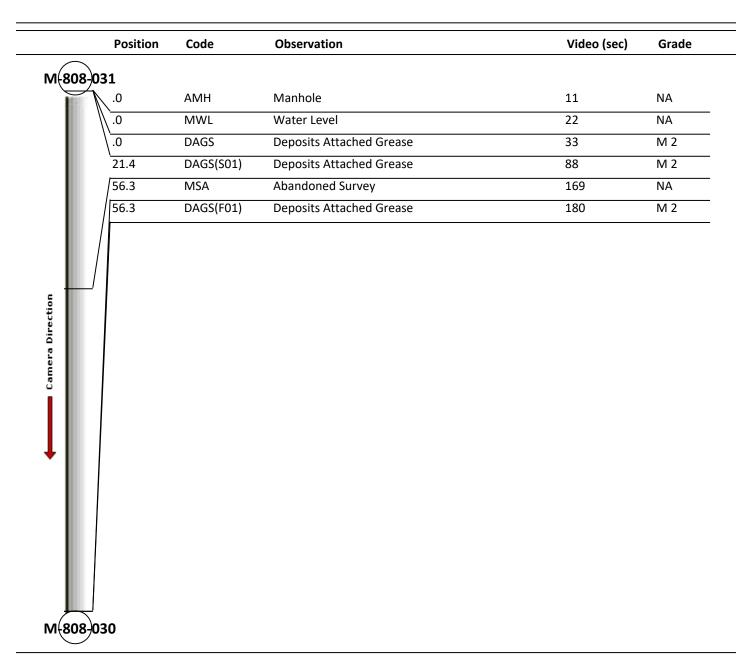




| Code:<br>Description: | AMH<br>Manhole |
|-----------------------|----------------|
|                       |                |
| Distance (ft):        | .0             |
| Structural Grade:     | 0              |
| O&M Grade:            | 0              |
| Clock Start/From:     |                |
| Clock To:             |                |
| 1st Value:            |                |
| 2nd Value:            |                |
| Value Percent:        |                |
| Continuous Index:     |                |
| Within 8" of Joint:   | NO             |
| Remarks:              | M-808-031      |



Code: MWL Description: Water Level

Distance (ft): .0 Structural Grade: 0 O&M Grade: 0 Clock Start/From: Clock To: 1st Value: 2nd Value: Value Percent: 10.000 Continuous Index: Within 8" of Joint: NO Remarks:



| Code:        | DAGS                     |
|--------------|--------------------------|
| Description: | Deposits Attached Grease |
|              |                          |

| Distance (ft):      | .0    |
|---------------------|-------|
| Structural Grade:   | 0     |
| O&M Grade:          | 2     |
| Clock Start/From:   | 8     |
| Clock To:           | 4     |
| 1st Value:          |       |
| 2nd Value:          |       |
| Value Percent:      | 5.000 |
| Continuous Index:   |       |
| Within 8" of Joint: | NO    |
| Remarks:            |       |
|                     |       |



Code:DAGSDescription:Deposits Attached Grease


| Distance (ft):      | 21.4  |
|---------------------|-------|
| Structural Grade:   | 0     |
| O&M Grade:          | 2     |
| Clock Start/From:   | 5     |
| Clock To:           | 4     |
| 1st Value:          |       |
| 2nd Value:          |       |
| Value Percent:      | 5.000 |
| Continuous Index:   | S01   |
| Within 8" of Joint: | NO    |
| Remarks:            |       |



| Code:        |  |
|--------------|--|
| Description: |  |

| MSA             |   |
|-----------------|---|
| Abandoned Surve | y |

| Distance (ft):      | 56.3 |
|---------------------|------|
| Structural Grade:   | 0    |
| O&M Grade:          | 0    |
| Clock Start/From:   |      |
| Clock To:           |      |
| 1st Value:          |      |
| 2nd Value:          |      |
| Value Percent:      |      |
| Continuous Index:   |      |
| Within 8" of Joint: | NO   |
| Remarks:            | DAGS |



Code:DAGSDescription:Deposits Attached Grease

| Distance (ft):      | 56.3  |
|---------------------|-------|
| Structural Grade:   | 0     |
| O&M Grade:          | 2     |
| Clock Start/From:   | 5     |
| Clock To:           | 4     |
| 1st Value:          |       |
| 2nd Value:          |       |
| Value Percent:      | 5.000 |
| Continuous Index:   | F01   |
| Within 8" of Joint: | NO    |
| Remarks:            |       |
