
| Profile/Ph | oto Observatio | n Report | | | | RedZone |
|------------------|------------------|--------------|--------------|---------|--------------------------|---------------|
| Date: | 03/22/2018 | Weather: | | | Coding: | PACP 6.0 |
| Pipe Length (ft |): 128.4 | Owner: | NA | | Pre Clean: | Not Known |
| P.O.#: | | Surveyor: | Selasie Ho | nu | PSR: | P-809-029-030 |
| Customer: | | Clean Date | : 01/01/190 | 0 | Shape: | С |
| Street: | MURRELET ST | | Flow Contro | l: | Not Controlled | |
| City: | Hobart, IN | | Year Renew | ed: | | |
| Location: | Yard | | Tape/Media | #: | | |
| Purpose: | Maintenance Rela | ated | Dia/Height: | | 8" | |
| Use: | Sanitary | | Material: | | PVC | |
| Drain Area: | NA | | Lining: | | | |
| Category: | NA | | | | | |
| Comment: | | | | | | |
| Location Detail | s: | | Direction of | Survey: | Downstream | |
| US MH: | M-809-030 | DS MH: | M-809-029 | То | tal Length Surveyed (ft) | 126.5 |
| 0&M Index: | 0.00 | O&M Quick | : | 0000 | O&M Rating: | 0.00 |
| tructural Index: | 0.00 | Structural C | | 0000 | Structural Rating: | 0.00 |
| Overall Index: | 0.00 | Overall Quid | ck: | 0000 | Overall Rating: | 0.00 |






| Code: Description: | AMH Manhole |
|-----------------------|----------------|
| Distance (ft): | .0 |
| Structural Grade: | 0 |
| O&M Grade: | 0 |
| Clock Start/From: | |
| Clock To: | |
| 1st Value: | |
| 2nd Value: | |
| Value Percent: | |
| Continuous Index: | |
| Within 8" of Joint: | NO |
| Remarks: | M-809-030 |

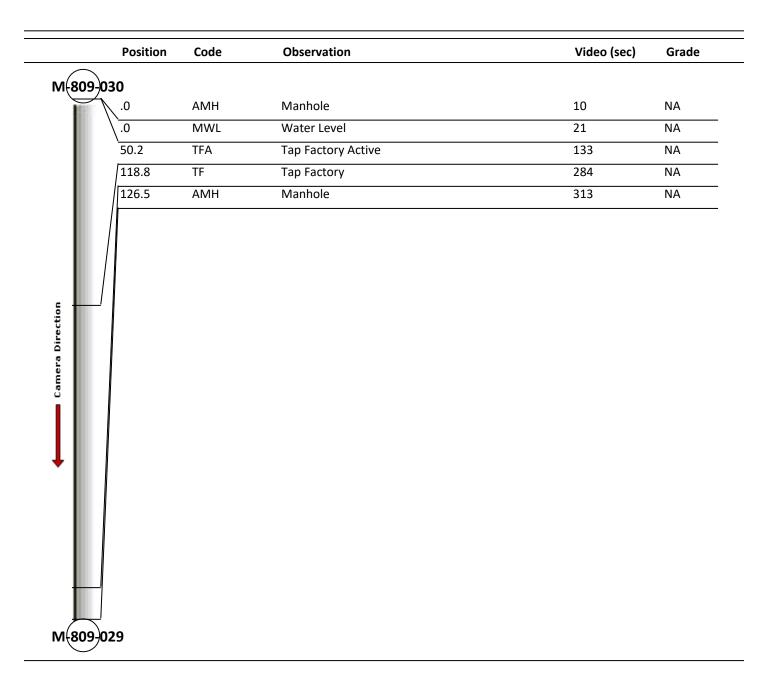


Code: MWL Description: Water Level

| Distance (ft): | .0 |
|---------------------|-------|
| Structural Grade: | 0 |
| O&M Grade: | 0 |
| Clock Start/From: | |
| Clock To: | |
| 1st Value: | |
| 2nd Value: | |
| Value Percent: | 5.000 |
| Continuous Index: | |
| Within 8" of Joint: | NO |
| Remarks: | |
| | |



| Code: Description: | TFA Tap Factory Active |
|-----------------------|---------------------------|
| Distance (ft): | 50.2 |
| Structural Grade: | 0 |
| O&M Grade: | 0 |
| Clock Start/From: | 10 |
| Clock To: | |
| 1st Value: | 4.000 |
| 2nd Value: | |
| Value Percent: | |
| Continuous Index: | |
| Within 8" of Joint: | |
| Remarks: | |



| Code: | TF |
|--------------|-------------|
| Description: | Tap Factory |

| Distance (ft): | 118.8 |
|---------------------|-------|
| Structural Grade: | 0 |
| O&M Grade: | 0 |
| Clock Start/From: | 10 |
| Clock To: | |
| 1st Value: | 4.000 |
| 2nd Value: | |
| Value Percent: | |
| Continuous Index: | |
| Within 8" of Joint: | |
| Remarks: | |



| Code: | AMH |
|--------------|---------|
| Description: | Manhole |

| 126.5 |
|-----------|
| 0 |
| 0 |
| |
| |
| |
| |
| |
| |
| NO |
| M-809-029 |
| |
