

Date:	03/28/2018	Weather:		Coding:	PACP 6.0
Pipe Length (ft)	: 271.5	Owner:	NA	Pre Clean:	Not Known
P.O.#:		Surveyor:	Selasie Honu	PSR:	P-809-049-050
Customer:		Clean Date:	01/01/1900	Shape:	С
Street:	Tanager		Flow Control:	Not Controlled	ł
City:	Hobart, IN		Year Renewed:		
Location:	Sidewalk		Tape/Media #:		
Purpose:	Maintenance Relate	d	Dia/Height:	8"	
Use:	Sanitary		Material:	PVC	
Drain Area:	NA		Lining:		
Category:	NA				
Comment:	Reverse setup.				
Location Details	5:		Direction of Surv	ey: Upstream	
US MH:	M-809-049	DS MH:	M-809-050	Total Length Surveyed (ft): 122.0
0&M Index:	2.00	O&M Quick:	220	0 O&M Rating:	4.00
tructural Index:	0.00	 Structural Qu	uick: 000		0.00
)verall Index:	2.00	Overall Quick			4.00



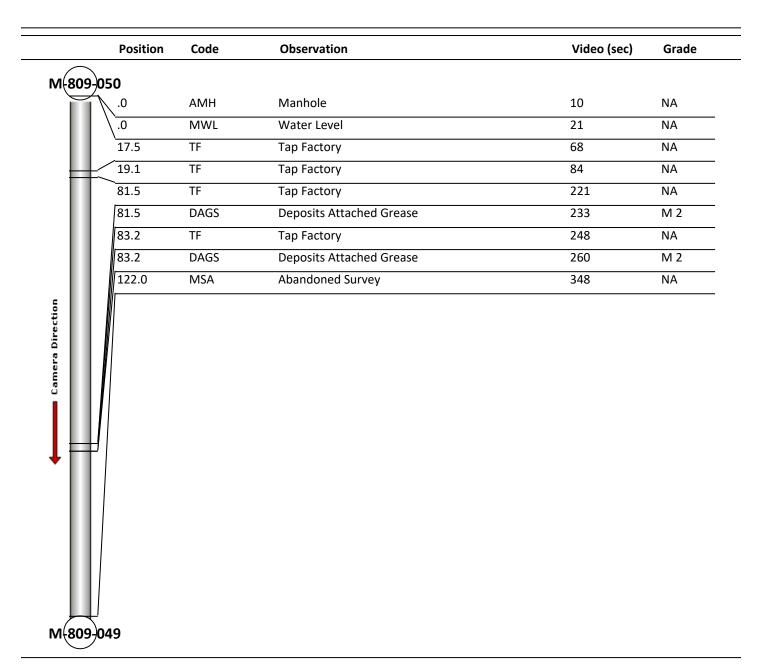


Code: Description:	AMH Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-809-050




Code: MWL Description: Water Level


Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	5.000
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	



Code: Description:	TF Tap Factory
Distance (ft):	17.5
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	2
Clock To:	
1st Value:	4.000
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	
Remarks:	



Code:	TF
Description:	Tap Factory
Distance (ft):	19.1
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	11
Clock To:	
1st Value:	4.000
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	
Remarks:	




Code: Description:	TF Tap Factory
Distance (ft): Structural Grade: O&M Grade: Clock Start/From: Clock To: 1st Value:	81.5 0 0 1 4.000
2nd Value: Value Percent: Continuous Index: Within 8" of Joint: Remarks:	




Code:DAGSDescription:Deposits Attached Grease

Distance (ft):	81.5
Structural Grade:	0
O&M Grade:	2
Clock Start/From:	8
Clock To:	4
1st Value:	
2nd Value:	
Value Percent:	5.000
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	



Code: Description:	TF Tap Factory
Distance (ft): Structural Grade: O&M Grade: Clock Start/From: Clock To: 1st Value: 2nd Value:	83.2 0 0 11 4.000
Value Percent: Continuous Index: Within 8" of Joint: Remarks:	



Code:DAGSDescription:Deposits Attached Grease

Distance (ft):	83.2
Structural Grade:	0
O&M Grade:	2
Clock Start/From:	8
Clock To:	4
1st Value:	
2nd Value:	
Value Percent:	5.000
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	

Code:	
Description:	

MSA Abandoned Survey

Distance (ft):	122.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	debris
