
Profile/Ph	noto Observation	n Report				RedZo
Date:	03/23/2018	Weather:			Coding:	PACP 6.0
Pipe Length (ft	t): 400.6	Owner:	NA		Pre Clean:	Not Known
P.O.#:		Surveyor:	Jen Coste	ello	PSR:	P-809-062-019
Customer:		Clean Date	e: 01/01/19	000	Shape:	С
Street:	Oak		Flow Contr	ol:	Not Controlled	
City:	Hobart, IN		Year Renev	wed:		
Location:	Sidewalk		Tape/Med	ia #:		
Purpose:	Maintenance Rela	ated	Dia/Height	:	8"	
Use:	Sanitary		Material:		PVC	
Drain Area:	NA		Lining:			
Category:	NA					
Comment:	debris rollover at	43'.				
Location Detai	ils:		Direction o	of Survey:	Downstream	
US MH:	M-809-062	DS MH:	M-809-019	Тс	otal Length Surveyed (ft)	44.4
D&M Index:	2.00	O&M Quick		2900	O&M Rating:	18.00
Structural Index	. 0.00	Structural C		0000	Structural Rating:	0.00
Overall Index:	2.00	Overall Qui		2900	Overall Rating:	18.00





Code: Description:	AMH Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-809-062

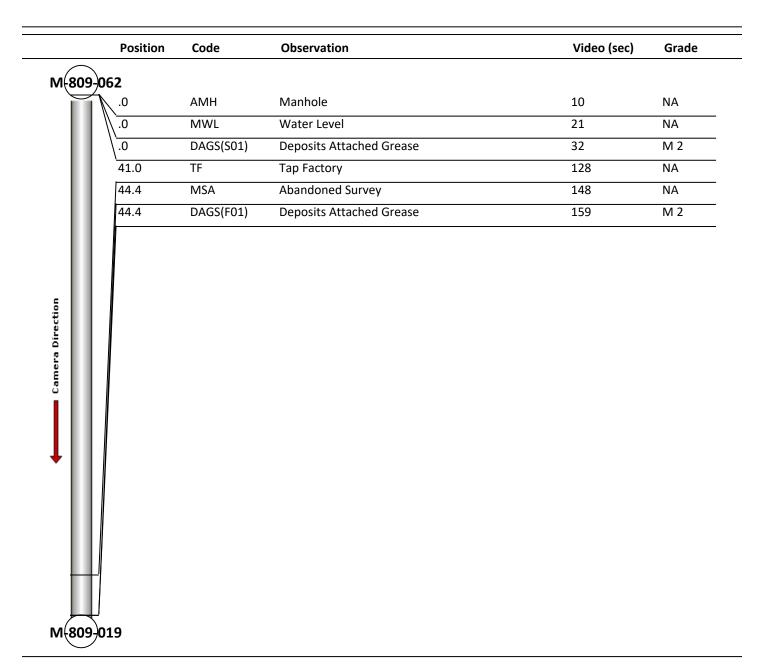

Code: MWL Description: Water Level

Distance (ft): .0 Structural Grade: 0 O&M Grade: 0 Clock Start/From: Clock To: 1st Value: 2nd Value: Value Percent: 10.000 Continuous Index: Within 8" of Joint: NO Remarks:

Code:	DAGS
Description:	Deposits Attached Grease

Distance (ft):	.0
Structural Grade:	0
O&M Grade:	2
Clock Start/From:	8
Clock To:	4
1st Value:	•
2nd Value:	
Value Percent:	5.000
Continuous Index:	S1000
Within 8" of Joint:	NO
Remarks:	NU
NEILIAINS.	




Code:	TF
Description:	Tap Factory

Distance (ft):	41.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	10
Clock To:	
1st Value:	4.000
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	
Remarks:	



Code:	MSA
Description:	Abandoned Survey

Distance (ft):	44.4
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	OVERTURNED



Code:DAGSDescription:Deposits Attached Grease

Distance (ft):	44.4
Structural Grade:	0
O&M Grade:	2
Clock Start/From:	8
Clock To:	4
1st Value:	
2nd Value:	
Value Percent:	5.000
Continuous Index:	F01
Within 8" of Joint:	NO
Remarks:	
