
Date:	05/05/2018	Weather:			Coding:	PACP 4.2
Pipe Length (ft):	227.9	Owner:	City of Ho	bart	Pre Clean:	No Pre-Cleaning
P.O.#:	2004	Surveyor:	SAN		PSR:	P-903-034-033
Customer:	Red Zone	Clean Date:			Shape:	С
Street:	703 N Hobart Rd		Flow Contro	ol:	Not Controlled	l
City:	Hobart In		Year Renew	ved:		
Location:	Main Highway - Urb	an	Tape/Media	a #:	Deliverable 1	
Purpose:	Routine Assessment		Dia/Height:		12"	
Use:	Sanitary		Material:		VCP	
Drain Area:	Northeast		Lining:			
Category:	NA					
Comment:	450-1					
Location Details:	Edge of street		Direction of	f Survey:	Upstream	
US MH:	M-903-034	DS MH:	M-903-033	-	Total Length Surveyed (ft): 227.9
0&M Index:	0.00	O&M Quick:		0000	O&M Rating:	0.00
tructural Index:	0.00	 Structural Qu		0000	 Structural Rating:	0.00
Overall Index:	0.00	Overall Quic		0000	Overall Rating:	0.00





Code: Description:	AMH Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-903-033

Thursday, May 4, 2023

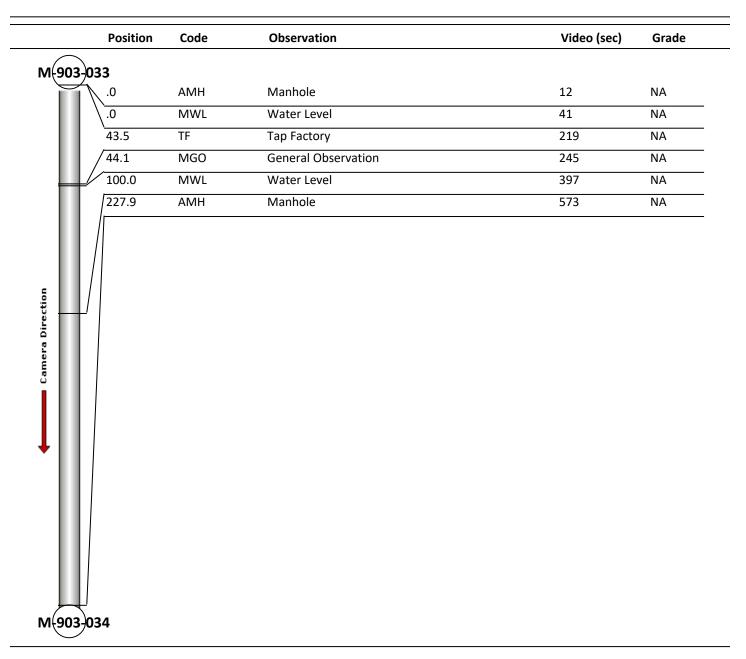

Code:	MWL
Description:	Water Level
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	15.000
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	



TF Tap Factory
43.5
0
0
2
4.000
NO



Code:	MGO
Description:	General Observation
Distance (ft):	44.1
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	resume after video issue



Code: Description:	MWL Water Level
Distance (ft):	100.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	10.000
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	



Code: Description:	AMH Manhole
Distance (ft):	227.9
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-903-034
