

Date:	10/20/2021	Weather:		Coding:	PACP 6.0
Pipe Length (ft):		Owner: Hobart, IN		Pre Clean:	Not Known
P.O.#:	905_1	Surveyor:	M. Pielacha	PSR:	P-905-009-008
Customer:	Hobart, IN	Clean Date:		Shape:	С
Street:	Sullivan Street		Flow Control:	Not Controlled	
City:	Hobart, IN		Year Renewed:		
Location:	Light Highway		Tape/Media #:	905	
Purpose:	Reversal		Dia/Height:	10"	
Use:	Sanitary		Material:	PVC	
Drain Area:			Lining:		
Category:	NA				
Comment:					
Location Deta	ils:		Direction of Survey:	Upstream	
US MH:	M-905-8	DS MH: N	M-905-9	Total Length Surveyed (ft)	.1
0&M Index:	3.00	O&M Quick:	3100	O&M Rating:	3.00
Structural Index	«: 0.00	Structural Quid	ck: 0000	Structural Rating:	0.00
Overall Index: 3.00		Overall Quick:	3100	Overall Rating:	3.00



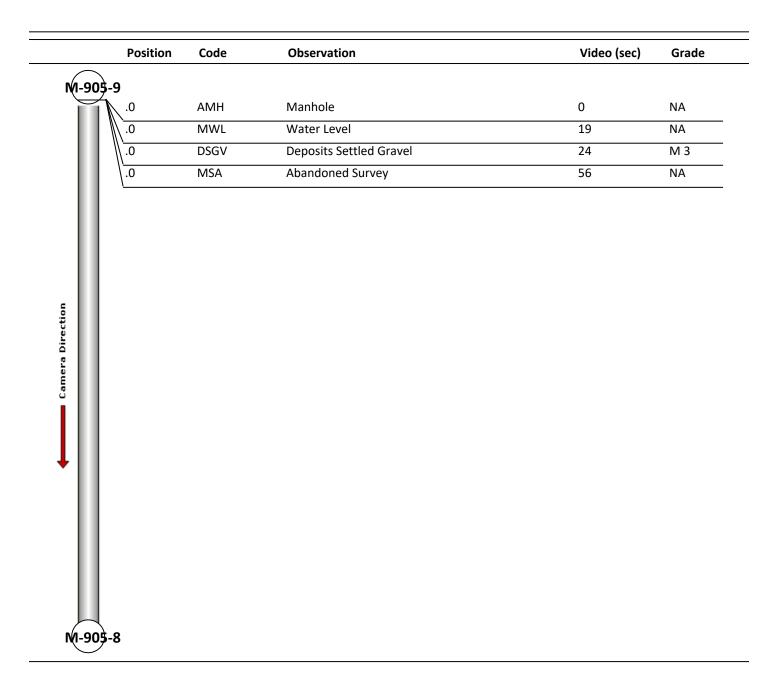


Code:	АМН
Description:	Manhole
Distance (ft):	0
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-905-9


Wednesday, May 3, 2023

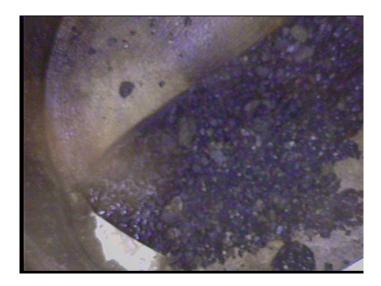

Code:	MWL
Description:	Water Level
	_
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	0.000
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	

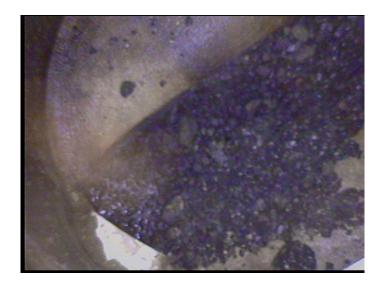

Code: Description:	DSGV Deposits Settled Gravel
Distance (ft): Structural Grade: O&M Grade: Clock Start/From: Clock To: 1st Value: 2nd Value: Value Percent:	.0 0 3 4 8 20.000
Continuous Index: Within 8" of Joint: Remarks:	NO

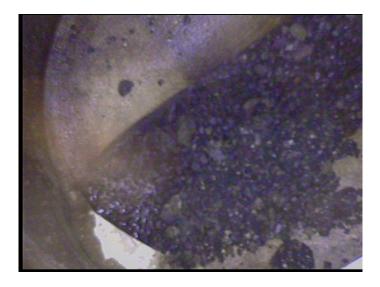

Code:	MSA
Description:	Abandoned Survey
Distance (ft): Structural Grade: O&M Grade: Clock Start/From: Clock To: 1st Value: 2nd Value: Value Percent: Continuous Index:	.0 0 0
Within 8" of Joint:	NO
Remarks:	Debris in pipe entrance
