
Profile/Ph	noto Observatio	on Report			RedZo
Date:	04/11/2018	Weather:		Coding:	PACP 6.0
Pipe Length (ft	t): 358.7	Owner:	NA	Pre Clean:	Not Known
P.O.#:		Surveyor:	Jen Costello	PSR:	P-907-006-007
Customer:		Clean Date:	01/01/1900	Shape:	С
Street:	Capitol		Flow Control:	Not Controlled	l
City:	Hobart, IN		Year Renewed:		
Location:	Ditch		Tape/Media #:		
Purpose:	Maintenance Re	lated	Dia/Height:	12"	
Use:	Sanitary		Material:	PVC	
Drain Area:	NA		Lining:	Cured in Place	
Category:	NA				
Comment:	battery at 350'-f	low incorrect			
Location Detai	ils:		Direction of Surv	vey: Upstream	
US MH:	M-907-007	DS MH:	M-907-006	Total Length Surveyed (ft): 351.3
D&M Index:	2.00	O&M Quick:	2M(00 O&M Rating:	140.00
Structural Index	0.00	Structural Q	uick: 000	• Structural Rating:	0.00
Overall Index:	2.00	Overall Quic			140.00





Code: Description:	AMH Manhole
Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	M-907-006

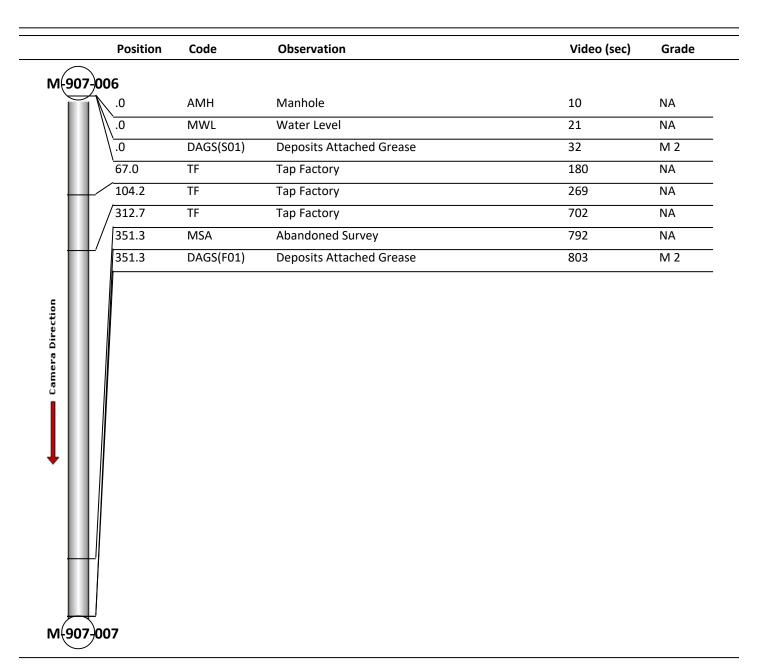

Code: MWL Description: Water Level

Distance (ft):	.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	5.000
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	



Code:	DAGS
Description:	Deposits Attached Grease

Distance (ft):	.0
Structural Grade:	0
O&M Grade:	2
Clock Start/From:	8
Clock To:	4
1st Value:	
2nd Value:	
Value Percent:	5.000
Continuous Index:	S01
Within 8" of Joint:	NO
Remarks:	




Code: Description:	TF Tap Factory
Distance (ft):	67.0
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	2
a	

Clock Start/From: 2 Clock To: 1st Value: 4.000 2nd Value: Value Percent: Continuous Index: Within 8" of Joint: Remarks:




Code: Description:	TF Tap Factory
Distance (ft): Structural Grade: O&M Grade: Clock Start/From: Clock To: 1st Value: 2nd Value: Value Percent:	104.2 0 0 2 4.000
Continuous Index: Within 8" of Joint: Remarks:	



Code:	TF
Description:	Tap Factory

Distance (ft):	312.7
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	10
Clock To:	
1st Value:	4.000
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	
Remarks:	



Code:	MSA
Description:	Abandoned Survey

Distance (ft):	351.3
Structural Grade:	0
O&M Grade:	0
Clock Start/From:	
Clock To:	
1st Value:	
2nd Value:	
Value Percent:	
Continuous Index:	
Within 8" of Joint:	NO
Remarks:	dags



Code:DAGSDescription:Deposits Attached Grease

Distance (ft):	351.3
Structural Grade:	0
O&M Grade:	2
Clock Start/From:	8
Clock To:	4
1st Value:	
2nd Value:	
Value Percent:	5.000
Continuous Index:	F01
Within 8" of Joint:	NO
Remarks:	
